

LA-UR-22-31053

Approved for public release; distribution is unlimited.

Title: FY2022 End of Year Disposition Project Update TA-16-0306, TA-16-0460, TA-22/37 Magazines, TA-41-0004, PHERMEX & TA-22 Storage Sheds

Author(s): Quintana, Vicente M.

Intended for: Report

Issued: 2022-10-19



Los Alamos National Laboratory, an affirmative action/equal opportunity employer, is operated by Triad National Security, LLC for the National Nuclear Security Administration of U.S. Department of Energy under contract 89233218CNA000001. By approving this article, the publisher recognizes that the U.S. Government retains nonexclusive, royalty-free license to publish or reproduce the published form of this contribution, or to allow others to do so, for U.S. Government purposes. Los Alamos National Laboratory requests that the publisher identify this article as work performed under the auspices of the U.S. Department of Energy. Los Alamos National Laboratory strongly supports academic freedom and a researcher's right to publish; as an institution, however, the Laboratory does not endorse the viewpoint of a publication or guarantee its technical correctness.



FY2022 End of Year Disposition Project Update

**TA-16-0306, TA-16-0460, TA-22/37 Magazines, TA-41-0004,
PHERMEX & TA-22 Storage Sheds**

Vicente Quintana

Projects Completed in FY22

Project	Status	Complete Date	ERI	GSF
DIRECT				
TA16-0306 Disposition	Complete	March 29,2022	91	19,639
TA16-0460 Disposition	Complete	February 28, 2022	74	13,825
TA22/37 Disposition of 19 Magazines	Complete	September 21, 2022	62	4,405
INDIRECT				
TA22 Storage Sheds	Complete	July 21, 2022	33	1,440



Carryover Projects to FY23 in Execution

Project	Status
DIRECT	
TA-41-0004 Disposition	Execution – Demolition of TA41-0004 to begin in October - Project complete expected in February 2023
PHERMEX De-Inventory	~500,000 lbs. of debris were loaded into 33 roll off bins. Field work is complete; waste bin shipments continue. Project complete expected in the 1 st quarter of FY23. Additional de-inventory projects as shown in G2 are required to complete the debris removal prior to characterization and demolition.
INDIRECT	
TA-52-0001	Working through award process which is expected in November 2022 – Project complete expected in 4 th quarter of FY23



TA-22 Storage Sheds Demolition



TA- 41-0004 & TA-41-0007



TA-41-0004 – Removal of piping



- The crew shown working on removing over head piping.
- In the foreground a Continuous Air Monitor is in place.



TA- 41-0004 – Air Duct removal



TA- 41-0006 – Portion of the covered walkway prepped for demolition



TA- 41-0007 – Demolition in progress



TA- 41-0007 – Demolition in progress




TA- 41-0004 – Preparing waste for shipment



TA- 41-0004 – Preparing waste for shipment



TA-16-0306 – Before Demolition

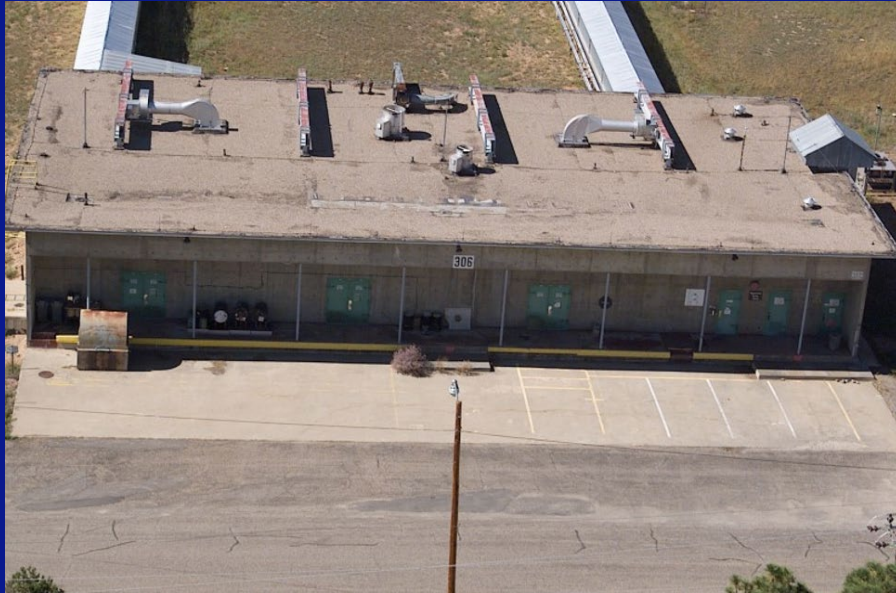

TA-16-0306 - Asbestos Abatement Complete in Basement



TA-16-0306 - Demolition



TA-16-0306 – Demolition in the basement



TA-16-0306 – Demolition of the basement walls



TA-16-0306 – Site stabilized



PHERMEX – Before / After Site De-Inventory Project



PHERMEX – Preparing bins for shipment



PHERMEX – Preparing bins for shipment



TA-37 Before demolition



TA-37-0006 Before and After



TA-37-0008 Before and After



TA-37-0009 Before and After



TA-37-0019 Before and After



TA-37-0020 Before and After



TA-22 Before and after magazine demolition – TA-22-0011,-0012



TA-22 Before and after magazine demolition– TA-22-0015



TA-22 Before and after magazine demolition– TA-22-0016



TA-22 Before and after magazine demolition– TA-22-0017



TA-22 Before and after magazine demolition– TA-22-0019



TA-22 Before and after magazine demolition– TA-22-0021



TA-22 Before and after magazine demolition– TA-22-0023



TA-22 Before and after magazine demolition– Site Stabilization Process

