

330
10-27-78
minis NTLS

DOE/NASA CONTRACTOR REPORT

10. 656

MASTER

DOE/NASA CR-150640

**SOLAR HEATING AND COOLING SYSTEMS DESIGN AND
DEVELOPMENT (Quarterly Report)**


Prepared by

Honeywell
Energy Resources Center
2600 Ridgway Parkway
Minneapolis, Minnesota 55413

Under Contract NAS8-32093 with

National Aeronautics and Space Administration
George C. Marshall Space Flight Center, Alabama

For the U. S. Department of Energy



U.S. Department of Energy



Solar Energy

DISTRIBUTION OF THIS DOCUMENT IS UNLIMITED

DISCLAIMER


This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency Thereof, nor any of their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or usefulness of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

DISCLAIMER

Portions of this document may be illegible in electronic image products. Images are produced from the best available original document.

NOTICE

This report was prepared to document work sponsored by the United States Government. Neither the United States nor its agents the United States Department of Energy, the United States National Aeronautics and Space Administration, nor any federal employees, nor any of their contractors, subcontractors or their employees, make any warranty, express or implied, or assume any legal liability or responsibility for the accuracy, completeness, or usefulness of any information, apparatus, product or process disclosed, or represent that its use would not infringe privately owned rights.

1. REPORT NO. DOE/NASA CR-150640		2. GOVERNMENT ACCESSION NO.		3. RECIPIENT'S CATALOG NO.	
4. TITLE AND SUBTITLE Solar Heating and Cooling Systems Design and Development - (Quarterly Report)				5. REPORT DATE March 10, 1978	
				6. PERFORMING ORGANIZATION CODE	
7. AUTHOR(S)				8. PERFORMING ORGANIZATION REPORT # F3437-QR-108	
9. PERFORMING ORGANIZATION NAME AND ADDRESS Honeywell - Energy Resources Center 2600 Ridgway Parkway Minneapolis, Minnesota 55413				10. WORK UNIT NO.	
				11. CONTRACT OR GRANT NO. NAS8-32093	
12. SPONSORING AGENCY NAME AND ADDRESS National Aeronautics and Space Administration Washington, D. C. 20546				13. TYPE OF REPORT & PERIOD COVERED Contractor Report 1 Oct 77 - 31 Dec 77	
				14. SPONSORING AGENCY CODE	
15. SUPPLEMENTARY NOTES This work was done under the technical management of Mr. A. Krupnick, George C. Marshall Space Flight Center, Alabama.					
16. ABSTRACT Honeywell was awarded Contract NAS8-32093 by the George C. Marshall Space Flight Center effective 9 July 1976. The program calls for the development and delivery of eight (was 12) prototype solar heating and cooling systems for installation and operational test. Two (was 6) heating and six heating and cooling units will be delivered for single-family residences (SFR), multiple-family residences (MFR) and commercial applications. Lennox Industries, Marshalltown, Iowa, and Barber Nichols Engineering Company, Arvada, Colorado, are supporting Honeywell in subcontractor roles. This document describes the progress of the program during the sixth program quarter, 1 October 1977 to 31 December 1977. It is submitted to MSFC for information per DR 500 Item 10 and has been edited for public release.					
17. KEY WORDS			18. DISTRIBUTION STATEMENT Unclassified-Unlimited  WILLIAM A. BROOKSBANK, JR. Manager, Solar Heating & Cooling Proj Ofc		
19. SECURITY CLASSIF. (of this report) Unclassified		20. SECURITY CLASSIF. (of this page) Unclassified		21. NO. OF PAGES 8	
				22. PRICE NTIS	

THIS PAGE
WAS INTENTIONALLY
LEFT BLANK

TABLE OF CONTENTS

	Page
Quarterly Summary	1
Site Activity	2
William O'Brien- OTS-40	2
New Castle, PA - OTS-39	2
Kansas University - OTS-43	4
Sacramento - OTS-41	5

NOTICE

This report was prepared as an account of work sponsored by the United States Government. Neither the United States nor the United States Department of Energy, nor any of their employees, nor any of their contractors, subcontractors, or their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness or usefulness of any information, apparatus, product or process disclosed, or represents that its use would not infringe privately owned rights.

QUARTERLY SUMMARY

The William O'Brien single-family heating system has been installed and is operational. The system is waiting for SDAS completion and checkout before the Installation Acceptance Review. The New Castle single-family heating residence is under construction with collector installation scheduled for mid-January 1978. All equipment except a few SDAS components have been shipped.

The Kansas University (KU) system is in the final design stages. A preliminary design review is scheduled for 28 February 1978. No significant design problems have been encountered.

The 25-ton cooling subsystem for KU is in the debugging stage. Pressure drops that were greater than anticipated were encountered. These problems are expected to be resolved, and the subsystem is expected to be operational by January 20, 1978.

The 3-ton redesign is in preliminary design stages. The rotary compressor has been received and is being prepared for testing. The 3-ton simulation work is being finalized and the design parameters for the Rankine system have been determined from simulation output.

SITE ACTIVITY

WILLIAM O'BRIEN SINGLE FAMILY HEATING (OTS #40)

The solar heating equipment installation was completed early in December and was checked out. The system was put into operation December 12, 1977 although some parts of the SDAS equipment were not delivered. The operating of Energy Transport Unit #1 (ETM) was verified. The system will remain operational, and SDAS data will be taken starting early in 1978.

NEW CASTLE, PA SITE--SINGLE-FAMILY HEATING (OTS #39)

The general contractor has begun construction of the house. All government furnished equipment for the solar heating system has either arrived at the site or is in transit. Inclement weather during the month of December held up construction and caused a delay in completion of the solar heating system. The solar collectors will be installed as soon as the roof is completed. The rest of the system will be installed as rapidly as possible to expedite system operation so the SDAS subsystem can gather operational data for this heating season.

The Energy Transport Module (ETM) for OTS #39 has undergone thorough inspections. Tests were made by Honeywell Quality and DCAS personnel.

The control subsystem for the single-family residence at the New Castle, Pennsylvania, site has been completed and installed in the Energy Transport Module (Figure 1). All electrical wiring internal to the ETM was installed, and a functional checkout of all operating modes was completed prior to shipment of the ETM to the site. The control panel provides manual control for adjustment of collector plate temperature (direct heating mode), and toggle switches control each active component in the system (pumps, control valves and purge unit).

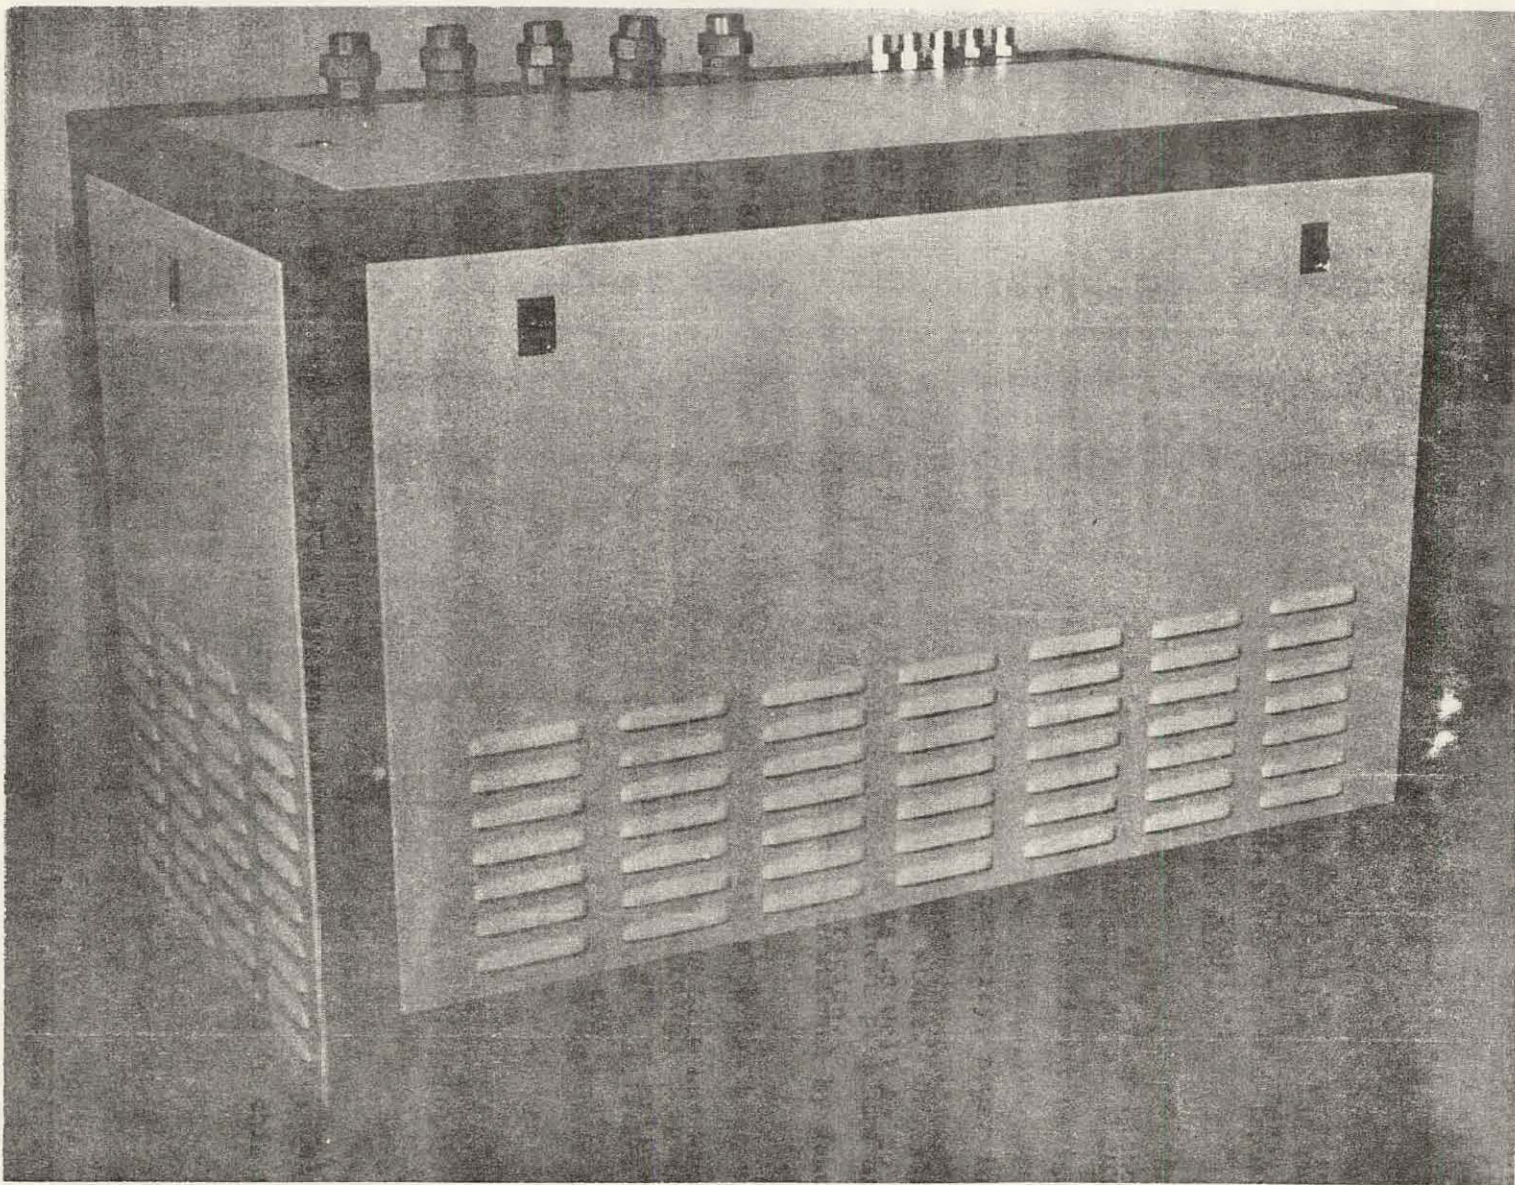


Figure 1. Energy Transport Module

This heating system is controlled by a two-stage heating thermostat. First-stage heating utilizes solar energy if available; second-stage heating will supply auxiliary energy. The system control logic is as follows:

- Collect solar energy when available. Store energy under no-load conditions.
- Provide energy directly to load on demand. Use direct solar energy before stored energy.
- Use storage energy when direct solar energy is not available.
- Use direct or stored solar energy before auxiliary energy.

KANSAS UNIVERSITY--MULTIFAMILY HEATING AND COOLING (OTS #43)

The Legal departments for both KU and Honeywell have reached agreement. Final drafts will be drawn up for approval on the contract for installation. Site work is expected to begin late in March 1978.

A preliminary plumbing layout for the solar H/C system at the Kansas University site has been completed. After corresponding piping sizes and fluid flow rates were selected, the pump requirements were determined. Internally located pump units are close-coupled, base-mounted, end-suction centrifugal pumps. Motors are open, drip-proof, 60 Hz/3-phase/230-volt/1750-rpm. The three-phase motor has been selected, even for the fractional horsepower size, due to lower power consumption. Cost and durability are the same as equivalent one-phase units.

Sump pumps are close-coupled general-service submersible units located in the sump below the cooling tower. Motors are 60-Hz/3-phase/230-volt/1150- or 1750-rpm.

The collector support structure design for two-high arrays has been completed. Modifications to reduce collector installation time were investigated during erection of the 45° structure at our Harding Solar Lab. Figure 2 shows the erected Harding structure.

Bid packages for the 30° support structure for the KU site were sent to steel supply houses and fabricators in the Kansas City and Minneapolis areas. A majority of the bids, along with an alternate design have been received.

The development testing on the number one 25-ton system at Barber-Nichols in Denver is complete.

Testing included necessary measurements to determine capacity, power input and coefficient of performance at design and off-design conditions. Other measurements were taken to confirm safe operation of components as well as to confirm proper equipment selection and sizing for efficient operation.

The 8,000-gallon storage tank for the Kansas University site has been specified. Bid packages were sent to tank manufacturers in the Kansas City and Minneapolis areas. Response has been received for both a lined steel and an unlined stainless steel design. Preliminary tank drawings have been sent to the KU site owner for tank foundation preparations.

SACRAMENTO--SFR H/C (OTS #41)

A simulation of the new 3-ton RC/AC system operating in Sacramento, California, has been run. Preliminary RC/AC performance data was utilized in this run to predict seasonal performance data.



Figure 2. Harding A-Frame Structure Showing Horizontal Support Member
