

S  
**ENGINEERING CHANGE NOTICE**

Page 1 of 2

1-ECN: 648541

Proj.  
ECN

2. ECN Category (mark one)	3. Originator's Name, Organization, MSIN, and Telephone No.		
Supplemental <input type="radio"/>	B. R. Johns, ISE, S7-24, 373-3429		
Direct Revision <input checked="" type="radio"/>	4. USQ Required? <input checked="" type="radio"/> Yes <input type="radio"/> No		
Change ECN <input type="radio"/>	5. Date 12/10/99		
Temporary <input type="radio"/>	6. Project Title/No./Work Order No.		
Standby <input type="radio"/>	Interim Stabilization, Leak		
Supersedure <input type="radio"/>	Detector Dedication, 103361		
Cancel/Void <input type="radio"/>	7. Bldg./Sys./Fac. No. 241-G/200-GEN		
12a. Modification Work	8. Approval Designator SQ		
<input type="radio"/> Yes (fill out Blk. 12b)	12b. Work Package No. N/A	12c. Modification Work Completed N/A	12d. Restored to Original Condition (Temp. or Standby ECNs only) N/A
<input checked="" type="radio"/> No (NA Blks. 12b, 12c, 12d)		Design Authority/Cog. Engineer Signature & Date	Design Authority/Cog. Engineer Signature & Date

13a. Description of Change

13b. Design Baseline Document?  Yes  No


This ECN is a direct revision of document HNF-4275, Commercial Grade Item Dedication for Leak Detection Relays. The revision changes steps 6.1.5 through 6.1.27 and adds steps 6.1.28 through 6.1.42. Step 6.2.1, is changed and steps 6.2.19, 6.2.23, 6.2.27, 6.2.31, 6.2.35, 6.2.39, and 6.2.43 were added to section 6.2. The references in section 12 were updated. The data sheets and sketches were changed to reflect the changes in the steps in sections 6.1 and 6.2.





14a. Justification (mark one)	14b. Justification Details
Criteria Change <input type="radio"/>	This direct revision of HNF-4275 reflects the changes in the site wide
Design Improvement <input type="radio"/>	procedure 7-LDD-483 for leak detector relay dedication bench testing.
Environmental <input type="radio"/>	Design verification by Inform review per HNF-IP-0842, volume IV, section
Facility Deactivation <input type="radio"/>	4.24. USQ tracking #TF-99-0973, revision 0.
As-Found <input type="radio"/>	This direct revision will not change collective dose since it has no
Facilitate Const. <input type="radio"/>	impact on radiological sources, contamination control or shielding.
Const. Error/Omission <input type="radio"/>	A NEPA review is not required since this is an administrative change per
Design Error/Omission <input checked="" type="radio"/>	HNF-PRO-452, section 2.1, paragraph 10.

15. Distribution (include name, MSIN, and no. of copies)

F. A. ZAK	S7-34
B. R. Johns	S7-24
M. R. Koch	S7-24
G. J. Coleman	S7-24
T. J. Volkman	S7-34
W. F. Zuroff	S7-24

RELEASE STAMP



ENGINEERING CHANGE NOTICE				Page 2 of 2	1. ECN (use no. from pg. 1) 648541	
16. Design Verification Required	17. Cost Impact			18. Schedule Impact (days)		
	ENGINEERING		CONSTRUCTION			
<input checked="" type="radio"/> Yes	Additional <input type="radio"/>	\$ <u>N/A</u>	Additional <input type="radio"/>	\$ <u>N/A</u>	Improvement <input type="radio"/>	<u>N/A</u>
<input type="radio"/> No	Savings <input type="radio"/>	\$ <u>N/A</u>	Savings <input type="radio"/>	\$ <u>N/A</u>	Delay <input type="radio"/>	<u>N/A</u>
19. Change Impact Review: Indicate the related documents (other than the engineering documents identified on Side 1) that will be affected by the change described in Block 13. Enter the affected document number in Block 20.						
SDD/DD	<input type="checkbox"/>	Seismic/Stress Analysis	<input type="checkbox"/>	Tank Calibration Manual <input type="checkbox"/>		
Functional Design Criteria	<input type="checkbox"/>	Stress/Design Report	<input type="checkbox"/>	Health Physics Procedure <input type="checkbox"/>		
Operating Specification	<input type="checkbox"/>	Interface Control Drawing	<input type="checkbox"/>	Spares Multiple Unit Listing <input type="checkbox"/>		
Criticality Specification	<input type="checkbox"/>	Calibration Procedure	<input type="checkbox"/>	Test Procedures/Specification <input type="checkbox"/>		
Conceptual Design Report	<input type="checkbox"/>	Installation Procedure	<input type="checkbox"/>	Component Index <input type="checkbox"/>		
Equipment Spec.	<input type="checkbox"/>	Maintenance Procedure	<input type="checkbox"/>	ASME Coded Item <input type="checkbox"/>		
Const. Spec.	<input type="checkbox"/>	Engineering Procedure	<input type="checkbox"/>	Human Factor Consideration <input type="checkbox"/>		
Procurement Spec.	<input type="checkbox"/>	Operating Instruction	<input type="checkbox"/>	Computer Software <input type="checkbox"/>		
Vendor Information	<input type="checkbox"/>	Operating Procedure	<input type="checkbox"/>	Electric Circuit Schedule <input type="checkbox"/>		
OM Manual	<input type="checkbox"/>	Operational Safety Requirement	<input type="checkbox"/>	ICRS Procedure <input type="checkbox"/>		
FSAR/SAR	<input type="checkbox"/>	IEFD Drawing	<input type="checkbox"/>	Process Control Manual/Plan <input type="checkbox"/>		
Safety Equipment List	<input type="checkbox"/>	Cell Arrangement Drawing	<input type="checkbox"/>	Process Flow Chart <input type="checkbox"/>		
Radiation Work Permit	<input type="checkbox"/>	Essential Material Specification	<input type="checkbox"/>	Purchase Requisition <input type="checkbox"/>		
Environmental Impact Statement	<input type="checkbox"/>	Fac. Proc. Samp. Schedule	<input type="checkbox"/>	Tickler File <input type="checkbox"/>		
Environmental Report	<input type="checkbox"/>	Inspection Plan	<input type="checkbox"/>	<u>NONE</u> <input checked="" type="checkbox"/>		
Environmental Permit	<input type="checkbox"/>	Inventory Adjustment Request	<input type="checkbox"/>			
20. Other Affected Documents: (NOTE: Documents listed below will not be revised by this ECN.) Signatures below indicate that the signing organization has been notified of other affected documents listed below.						
Document Number/Revision	Document Number/Revision		Document Number/Revision			
N/A	N/A		N/A			
21. Approvals						
Signature	Date		Signature	Date		
Design Authority <u>WF ZUROFF</u> 	<u>12/17/99</u>		Design Agent <u>BR JOHNS</u> 	<u>12/10/99</u>		
Cog. Eng. <u>G. J. COLEMAN</u> 	<u>12/16/99</u>		PE	<u> </u>		
Cog. Mgr. <u>MR KOCH</u> 	<u>12/21/99</u>		QA	<u> </u>		
QA <u>TJ VOLKMAN</u> 	<u>12/20/99</u>		Safety	<u> </u>		
Safety <u>CD JACKSON</u> 	<u>12/20/99</u>		Design	<u> </u>		
Environ. <u>N/A</u>	<u> </u>		Environ.	<u> </u>		
Other <u>Informal Review: D. Diefel</u>	<u>12/20/99</u>		Other	<u> </u>		
DEPARTMENT OF ENERGY						
Signature or a Control Number that tracks the Approval Signature						
ADDITIONAL						

# COMMERCIAL GRADE ITEM DEDICATION FOR LEAK DETECTION RELAYS

M. R. Koch

LOCKHEED MARTIN HANFORD CORPORATION

Richland, WA 99352

U.S. Department of Energy Contract DE-AC06-96RL13200

EDT/ECN: 648541

UC:

Org Code: 74D00

Charge Code: 103361

B&R Code: EW3120071

Total Pages: 17

**Key Words:** PICS, SALT WELL, SKID, INTERIM STABILIZATION, LEAK DETECTION

**Abstract:** This Test Plan provides a test method to dedicate the leak detection relays used on the new Pumping and Instrumentation Control (PIC) skids. The new skids are fabricated on-site. The leak detection system is a safety class system per the Authorization Basis.


---

TRADEMARK DISCLAIMER. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors.

Printed in the United States of America. To obtain copies of this document, contact: Document Control Services, P.O. Box 950, Mailstop H6-08, Richland WA 99352, Phone (509) 372-2420; Fax (509) 376-4989.

*genis braden*  
Release Approval

12/21/99  
Date



Release Stamp

Approved For Public Release



## TABLE OF CONTENTS

1. INTRODUCTION.....	2
2. OBJECTIVE.....	2
3. SCOPE .....	2
4. DESCRIPTION OF TEST .....	2
4.1. TEST ITEM.....	2
4.2. TEST ENVIRONMENT .....	2
4.3. EQUIPMENT AND FACILITIES .....	3
4.4. DATA .....	3
4.5. CRITERIA AND CONSTRAINTS.....	3
5. EXPECTED RESULTS .....	3
6. TEST PROCEDURE .....	3
6.1. BENCH TEST .....	3
6.2. FUNCTIONAL TEST.....	6
9. SAFETY.....	9
8. QUALITY ASSURANCE.....	9
9. ORGANIZATION AND FUNCTION RESPONSIBILITIES .....	9
10. SCHEDULE.....	9
11. REPORTS.....	9
12. REFERENCES .....	9
13. DATA SHEETS.....	9
APPENDIX.....	10

COMMERCIAL GRADE ITEM UPGRADE DEDICATION FOR LEAK DETECTION  
RELAYS

## 1. INTRODUCTION

This commercial grade item upgrade dedication test is for the leak detection relays installed on the Pumping Instrumentation and Control (PIC) skids. The PIC skids are used by Interim Stabilization for pumping liquids out of the underground waste tanks. There are two sets of leak detection relay assemblies on each PIC skid. The primary leak detection relay assembly is to monitor the pump pit of the tank being pumped. The second leak detection relay assembly monitors other areas along the transfer line during pumping such as Clean Out Boxes (COB). The leak detection relay assembly is considered Safety Class per the Authorization Basis (LMHC 1999a), chapter 3, tables 3.4.2.7-4 and 3.4.2.8-4.

## 2. OBJECTIVE

The testing outlined in this test procedure will dedicate the two relays used in each leak detector assembly on the PIC skids. These relays are intrinsically safe type relays.

## 3. SCOPE

This test covers the 5300-S-V-OC (or 5300-S-F1-OC) and the 2313A relays used in leak detection assemblies. Upon successful completion and passing of the testing outlined in this procedure, the relays are considered dedicated and can be green tagged and installed in the leak detection units.

## 4. DESCRIPTION OF TEST

### 4.1. TEST ITEM

The items to be tested are the relays in the leak detection assembly. These leak detection assemblies contain B/W Controls relay part number 5300-S-V-OC, a variable sensitivity (or 5300-S-F1-OC, a fixed sensitivity relay) and MTL relay part number 2313A.

### 4.2. TEST ENVIRONMENT

The bench test will be performed in the shop and the functional test will be performed during the Acceptance Test Procedure (ATP) or Operational Test Procedure (OTP) of the leak detection assembly.

#### 4.3. EQUIPMENT AND FACILITIES

Test equipment required is listed below. Calibration is required for the digital voltmeter.

- Digital voltmeter for voltage checks
- Test box to check the B/W Controls relay (Coordinate use with Interim Stabilization maintenance.)
- Bucket of water to test leak detector probe.
- Leak detector probe (Coordinate with Interim Stabilization for probe to use for testing).
- DC power supply for 3.5vdc to 4.0vdc for testing relay.
- A nominal 120vac power source to connect to the leak detection assembly.

#### 4.4. DATA

The test procedure section and data tables identify the parameters to be checked and the acceptable values. The data is primarily voltages and relay contact opening and closing.

#### 4.5. CRITERIA AND CONSTRAINTS

The criteria for acceptance of the relays is based upon proper functioning of the relays during the testing. The relays must function 100% correct to be acceptable. There are no other controlling documents the relays must comply with to be acceptable.

### 5. EXPECTED RESULTS

The relays must function 100% correct which includes all contacts operations and voltage measurements to meet the acceptance criteria as listed on the data sheets.

### 6. TEST PROCEDURE

#### 6.1. BENCH TEST

- 6.1.1. Bench test the Intrinsically Safe 5300-S-V-OC (or 5300-S-F1-OC) (5300) relay as per the following steps:
- 6.1.2. Use a calibrated digital voltmeter. Record calibration data on data sheet.

- 6.1.3. Identify the relays to be tested with a label. Label one as "SALW-LDE-6001\*" and the other as "SALW-LDE-6002\*". Document the number in the component ID column of the data sheets, one on each data sheet. Replace the \* with the skid identification letter.
- 6.1.4. Quality Assurance Inspector to verify the correct part number of 5300-S-V-OC (or 5300-S-F1-OC) of the relay that is being tested. Record on the data sheet.
- 6.1.5. Verify resistance between terminal 12 on the 5300 relay and chassis ground with a VOM is greater than 10M ohms. Record reading on the data sheet.
- 6.1.6. If the 5300 relay does not meet the 10M ohms resistance in step 6.1.5, then reject the relay and get a new relay and restart the testing from step 6.1.3.
- 6.1.7. Connect the 5300 relay to the test box as shown in the attached sketch. Ensure there is no power to the test box when the wires are being connected.
- 6.1.8. Ensure the sensitivity setting on the 5300 relay is turned fully counter clockwise.
- 6.1.9. Ensure switch SW-2 is OPEN
- 6.1.10. Energize the test box and energize the 5300 relay by closing switch SW-1 on the test box. Ensure the "Power ON" light is ON.
- 6.1.11. Verify the output voltage at terminals 14 and 15 on the 5300 is between 9 and 11 vdc. Record voltage on data sheet.
- 6.1.12. Ensure switches SW-3 and SW-4 are OPEN.
- 6.1.13. Place or ensure switches SW-5 and SW-6 are in the "A" positions.
- 6.1.14. Verify the "relay OFF" light is ON.
- 6.1.15. Verify the "relay ON" light is OFF
- 6.1.16. Place or ensure switches SW-5 and SW-6 are in the "B" positions.
- 6.1.17. Verify the "relay OFF" light is ON
- 6.1.18. Verify the "relay ON" light is OFF
- 6.1.19. Close switch SW-2.
- 6.1.20. Verify the voltage between terminals 14 and 15 on the 5300 relay is less than 1vdc. Record on data sheet.

- 6.1.21. Ensure switch SW-2 is closed and switches SW-5 and SW-6 are still in the "B" position.
- 6.1.22. Verify the "relay OFF" light is OFF.
- 6.1.23. Verify the "relay ON" light is ON.
- 6.1.24. Place or ensure switches SW-5 and SW-6 are in the "A" positions.
- 6.1.25. Verify the "relay OFF" light is OFF.
- 6.1.26. Verify the "relay ON" light is ON.
- 6.1.27. Open switch SW-2 and Push the Reset button.
- 6.1.28. Ensure switches SW-5 and SW-6 in the "A" positions.
- 6.1.29. Verify the "relay OFF" light is ON.
- 6.1.30. Verify the "relay ON" light is OFF.
- 6.1.31. Place switches SW-5 and SW-6 in the "B" positions.
- 6.1.32. Verify the "relay OFF" light is ON.
- 6.1.33. Verify the "relay ON" light is OFF.
- 6.1.34. Perform steps 6.1.21 through 6.1.33 a total of 10 times. Pause before performing each switch SW-2 operation. Record results on the data sheet.
- 6.1.35. The 5300 relay passes the bench contact test if the results of all 10 tests are satisfactory. Any failure during any of the 10 tests is considered a failure of the relay.
- 6.1.36. Open switch SW-1.
- 6.1.37. Ensure the "Power On" light is OFF.
- 6.1.38. Close switches SW-3 and SW-4.
- 6.1.39. Close switch SW-1.
- 6.1.40. Repeat steps 6.1.13 through 6.1.35 and record data on data sheets.
- 6.1.41. Open switch SW-1.
- 6.1.42. Disconnect the 5300 relay from the test box.
- 6.1.43. Quality Assurance Inspector is to sign the data sheet and green tag the 5300 relay as acceptable for installation.
- 6.1.44. Repeat steps 6.1.3 through 6.1.43 for each relay.

## 6.2. FUNCTIONAL TEST

- 6.2.1. Perform the functional test after the leak detector relays (5300-S-V-OC (or 5300-S-F1-OC) and 2313A) are installed and the skid is assembled to the point where 120vac control power can be applied to the leak detector assembly. Test each of the two leak detector sets separately. ~~Identify relay being tested as either SALW-LDE-6001\* or SALW-LDE-6002\*~~ Record on data sheet.
- 6.2.2. Record the calibration of the digital multimeter on data sheet.
- 6.2.3. Quality Assurance Inspector to verify part number of MTL relay as "2313A" and record on data table.
- 6.2.4. Apply 120vac power to the leak detector assembly either from the skid distribution panel or from a 120vac power source to the line side of the leak detector fuse block.
- 6.2.5. Disconnect the wires from terminals 1 and 4 of the MTL 2313A relay.
- 6.2.6. Apply 3.5 to 4.0 vdc power to the MTL 2313A terminals where positive dc goes to terminal 1 and negative dc goes to terminal 4.
- 6.2.7. Adjust the MTL 2313A relay to activate (where the red light on the relay is OFF) at 3.5 to 4.0 vdc. Record on the data table.
- 6.2.8. Disconnect the dc power supply from the MTL 2313A relay.
- 6.2.9. Reconnect the wires disconnected in step 6.2.5 to the MTL 2313A relay.
- 6.2.10. Place the selector switch on the front of the panel from the leak detector relays to be tested in the "PROBE TEST" position.
- 6.2.11. Adjust the 5300 sensitivity (if an adjustable sensitivity relay is used) until the MTL relay activates (that is the red light OFF). Then add 0.25 to the 5300 sensitivity setting to ensure a margin for activation. Record on data sheet.
- 6.2.12. Release the selector switch on the front of the panel ~~to return to the "OPERATE" position.~~
- 6.2.13. Verify the voltage across terminals 14 and 15 on the 5300 relay and terminals 1 and 4 on the MTL 2313A relay is 9 to 11 vdc.
- 6.2.14. Remove the 120vac power from the leak detector assembly.
- 6.2.15. Connect a leak detector probe to the leak detector terminal block as shown in the attached sketch 2.

- 6.2.16. Return 120vac power to the leak detector assembly.
- 6.2.17. Place the selector switch on the front of the panel to the “OPERATE” position for the leak detector assembly to be tested.
- 6.2.18. Verify the contacts between terminals 4 and 5 are CLOSED on the 5300 relay.
- 6.2.19. Verify contacts 3 and 6 are OPEN on the 5300 relay by observing the red light is OFF. (normally located on the front door of the Instrument Enclosure)
- 6.2.20. Verify the contacts between terminals 9 and 10 are OPENED, the contacts between terminals 13 and 14 are CLOSED and the red light is ON at the MTL 2313A relay.
- 6.2.21. Place the selector switch to the “TEST PROBE” position.
- 6.2.22. Verify the contacts between terminals 4 and 5 are OPENED on the 5300 relay.
- 6.2.23. Verify contacts 3 and 6 are CLOSED on the 5300 relay by observing the red light is ON. (normally located on the front door of the Instrument Enclosure)
- 6.2.24. Verify the contacts between terminals 9 and 10 are CLOSED, the contacts between terminals 13 and 14 are OPENED and the red light is OFF at the MTL 2313A relay.
- 6.2.25. Return the selector switch to the “OPERATE” position.
- 6.2.26. Verify the contacts between terminals 4 and 5 are CLOSED on the 5300 relay.
- 6.2.27. Verify contacts 3 and 6 are OPEN on the 5300 relay by observing the red light is OFF. (normally located on the front door of the Instrument Enclosure)
- 6.2.28. Verify the contacts between terminals 9 and 10 are OPENED, the contacts between terminals 13 and 14 are CLOSED and the red light is ON at the MTL 2313A relay.
- 6.2.29. Place the selector switch to the “FAIL” position.
- 6.2.30. Verify the contacts between terminals 4 and 5 are CLOSED on the 5300 relay.
- 6.2.31. Verify contacts 3 and 6 are CLOSED on the 5300 relay by observing the red light is ON. (normally located on the front door of the Instrument Enclosure)
- 6.2.32. Verify the contacts between terminals 9 and 10 are CLOSED, the contacts between terminals 13 and 14 are OPENED and the red light is OFF at the MTL 2313A relay.
- 6.2.33. Return the selector switch to the “OPERATE” position.

HNF-4275  
REVISION 3

- 6.2.34. Verify the contacts between terminals 4 and 5 are CLOSED on the 5300 relay.
- 6.2.35. Verify contacts 3 and 6 are OPEN on the 5300 relay by observing the red light is OFF (normally located on the front door of the Instrument Enclosure)
- 6.2.36. Verify the contacts between terminals 9 and 10 are OPENED, the contacts between terminals 13 and 14 are CLOSED and the red light is ON at the MTL 2313A relay.
- 6.2.37. Place the leak detector probe into a bucket of water.
- 6.2.38. Verify the contacts between terminals 4 and 5 are OPENED on the 5300 relay.
- 6.2.39. Verify contacts 3 and 6 are CLOSED on the 5300 relay by observing the red light is ON (normally located on the front door of the Instrument Enclosure)
- 6.2.40. Verify the contacts between terminals 9 and 10 are CLOSED, the contacts between terminals 13 and 14 are OPENED and the red light is OFF at the MTL 2313A relay.
- 6.2.41. Remove the leak detector from the bucket of water.
- 6.2.42. Verify the contacts between terminals 4 and 5 are CLOSED on the 5300 relay.
- 6.2.43. Verify contacts 3 and 6 are OPEN on the 5300 relay by observing the red light is OFF (normally located on the front door of the Instrument Enclosure)
- 6.2.44. Verify the contacts between terminals 9 and 10 are OPENED, the contacts between terminals 13 and 14 are CLOSED and the red light is ON at the MTL 2313A relay.
- 6.2.45. Remove the power from the leak detector assembly being tested.
- 6.2.46. Disconnect the leak detector probe from the relay set being tested.
- 6.2.47. Quality Assurance Inspector to sign the data table upon successful completion of the functional tests.
- 6.2.48. Repeat steps 6.2.31 through 6.2.47 for the other leak detector relay set.

## 9. SAFETY

This test procedure creates no unique safety hazard. Standard electrical practices are to be used for performing voltage checks on low voltage equipment. Voltages encountered in this test are 5 volts dc and 120 volts ac.

## 8. QUALITY ASSURANCE

Quality Assurance Inspector shall witness the performance of this test procedure. Quality Assurance Inspector shall be responsible to sign the completed data sheets along with engineering and green tag those relays that successfully complete the testing.

## 9. ORGANIZATION AND FUNCTION RESPONSIBILITIES

Lockheed Martin Hanford Corporation shall provide the engineering support to ensure the proper test procedure is prepared and the Commercial Grade Item (CGI) dedication forms are completed prior to use of the leak detection relays.

Site Fabrication Services shall perform this test procedure for leak detection relays used in the fabrication of new PIC skids.

## 10. SCHEDULE

The bench test shall be performed prior to the relays being installed in the PIC skids. The functional test shall be performed during the ATP of the PIC skids that are fabricated.

## 11. REPORTS

The CGI forms and attached data sheets shall be the official test record. A formal test report will not be issued.

## 12. REFERENCES

LMHC 1999a, HNF-SD-WM-SAR-067, REVISION 1, *TANK WASTE REMEDIATION SYSTEM FINAL SAFETY ANALYSIS REPORT*, October 1999.

LMHC 1999b, HNF-IP-0842, VOLUME IV, SECTION 3.11, REVISION 3b, *COMMERCIAL GRADE ITEM UPGRADE*, October 1999.

## 13. DATA SHEETS

Typical data sheets are in the appendix. A completed copy of each data sheet shall be part of the completed CGI form.

HNF-4275  
REVISION 3

## **APPENDIX**

### **TEST DATA SHEETS**

1. BENCH TEST DATA SHEET
2. FUNCTIONAL TEST DATA SHEET

6.1.2 Voltmeter Standards # \_\_\_\_\_  
Voltmeter Calibration Due Date: \_\_\_\_\_

5300-S-V-OC (or 5300-S-F1-OC) RELAY TEST DATA TABLE (switches 3 and 4 OPEN)

STEP	RECORDED DATA	EXPECTED DATA	ACCEPT/UNACCEPT
6.1.3		SALW-LDE-6001* OR SALW-LDE-6002*	
6.1.4		5300-S-V-OC (or 5300-S-F1-OC)	
6.1.5		10M ohms	
6.1.11		9 to 11 vdc	
6.1.12		SW-3 and SW-4 OPEN	
6.1.20		Less than 1vac	

STEP	EXPECTED DATA	TEST SERIES [ACCEPT (A)/UNACCEPT (U)]									
		1	2	3	4	5	6	7	8	9	10
6.1.21	SW-2 Close/SW-5 SW-6 in "B"										
6.1.22	"RELAY OFF" light OFF										
6.1.23	"RELAY ON" light ON										
6.1.24	SW-5 SW-6 in "A"										
6.1.25	"RELAY OFF" light OFF										
6.1.26	"RELAY ON" light ON										
6.1.27	SW-2 Open										
6.1.28	SW-5 SW-6 in "A"										
6.1.29	"RELAY OFF" light ON										
6.1.30	"RELAY ON" light OFF										
6.1.31	SW-5 SW-6 in "B"										
6.1.32	"RELAY OFF" light ON										
6.1.33	"RELAY ON" light OFF										

Relay (PASS/FAIL) \_\_\_\_\_ (ALL TESTS MUST BE ACCEPTABLE)

Quality Assurance Inspector Signature \_\_\_\_\_

Date \_\_\_\_\_

Engineer Signature \_\_\_\_\_

Date \_\_\_\_\_

5300-S-V-OC (or 5300-S-F1-OC) RELAY TEST DATA TABLE (switches 3 and 4 CLOSED)

STEP	RECORDED DATA	EXPECTED DATA	ACCEPT/UNACCEPT
6.1.3		SALW-LDE-6001* OR SALW-LDE-6002*	
6.1.38		SW-3 and SW-4 CLOSED	

STEP	EXPECTED DATA	TEST SERIES [ACCEPT (A)/UNACCEPT (U)]									
		1	2	3	4	5	6	7	8	9	10
6.1.21	SW-2 Close/SW-5 SW-6 in "B"										
6.1.22	"RELAY OFF" light OFF										
6.1.23	"RELAY ON" light ON										
6.1.24	SW-5 SW-6 in "A"										
6.1.25	"RELAY OFF" light OFF										
6.1.26	"RELAY ON" light ON										
6.1.27	SW-2 Open										
6.1.28	SW-5 SW-6 in "A"										
6.1.29	"RELAY OFF" light ON										
6.1.30	"RELAY ON" light OFF										
6.1.31	SW-5 SW-6 in "B"										
6.1.32	"RELAY OFF" light ON										
6.1.33	"RELAY ON" light OFF										

Relay (PASS/FAIL) \_\_\_\_\_ (ALL TESTS MUST BE ACCEPTABLE)

Quality Assurance Inspector Signature \_\_\_\_\_ Date \_\_\_\_\_

Engineer Signature \_\_\_\_\_ Date \_\_\_\_\_

## 5300-S-V-OC (or 5300-S-F1-OC) AND MTL 2313A FUNCTIONAL TESTS

6.2.1 RELAY NUMBER: SALW-LDE-

6.2.2 Voltmeter Standards # \_\_\_\_\_

Voltmeter Calibration Due Date: \_\_\_\_\_

6.2.3 MTL 2313A part number verified correct: (YES/NO) \_\_\_\_\_

Step 6.2.7: MTL 2313A relay adjusted to actuate between 3.5 and 4.0 vdc. (YES/NO) \_\_\_\_\_

Step 6.2.11: B/W relay sensitivity adjusted (+0.25) to actuate the MTL 2313A relay. (YES/NO) \_\_\_\_\_

Step 6.2.11: B/W relay sensitivity adjusted (+0.25) to actuate the MTL 2313A relay. (YES/NO) \_\_\_\_\_ (N/A for fixed sensitivity relay)


CONTROL SWITCH 5300-S-V-OC (or 5300-S-F1-OC)

STEP	POSITION	TERMINALS 4 & 5				TERMINALS 3 & 6				TERMINALS 9 & 10				TERMINALS 13 & 14			
		STEP	ACTUAL	EXPECT	STEP	ACTUAL	EXPECT	STEP	ACTUAL	EXPECT	STEP	ACTUAL	EXPECT	STEP	ACTUAL	EXPECT	LIGHT
6.2.17	OPERATE	6.2.18	CLOSE	6.2.19	OPEN	6.2.20	OPEN	6.2.21	CLOSE	CLOSE	6.2.24	OPEN	CLOSE	6.2.25	OPEN	OPEN	ON
6.2.21	TEST PROBE	6.2.22	OPEN	6.2.23	CLOSE	6.2.24	CLOSE	6.2.25	OPEN	OPEN	6.2.28	OPEN	CLOSE	6.2.29	OPEN	OPEN	OFF
6.2.25	OPERATE	6.2.26	CLOSE	6.2.27	OPEN	6.2.28	OPEN	6.2.29	CLOSE	CLOSE	6.2.32	CLOSE	OPEN	6.2.33	OPEN	OPEN	ON
6.2.29	FAIL	6.2.30	CLOSE	6.2.31	CLOSE	6.2.32	CLOSE	6.2.33	OPEN	OPEN	6.2.36	OPEN	CLOSE	6.2.37	OPEN	OPEN	OFF
6.2.33	OPERATE	6.2.34	CLOSE	6.2.35	OPEN	6.2.36	OPEN	6.2.37	CLOSE	CLOSE	6.2.40	CLOSE	OPEN	6.2.41	OPEN	OPEN	ON
6.2.37	OPERATE/IN WATER	6.2.38	OPEN	6.2.39	CLOSE	6.2.40	CLOSE	6.2.41	OPEN	OPEN	6.2.44	OPEN	CLOSE	6.2.41	OPEN	OPEN	OFF
6.2.41	OPERATE/OUT OF WATER	6.2.42	CLOSE	6.2.43	OPEN	6.2.44	OPEN	6.2.41	OPEN	OPEN	6.2.45	OPEN	CLOSE	6.2.41	OPEN	OPEN	ON

Functional test (PASS/FAIL) \_\_\_\_\_ (ALL EXPECTED DATA MUST BE ACHIEVED)


Quality Assurance Inspector Signature \_\_\_\_\_ Date \_\_\_\_\_

Engineer Signature \_\_\_\_\_ Date \_\_\_\_\_

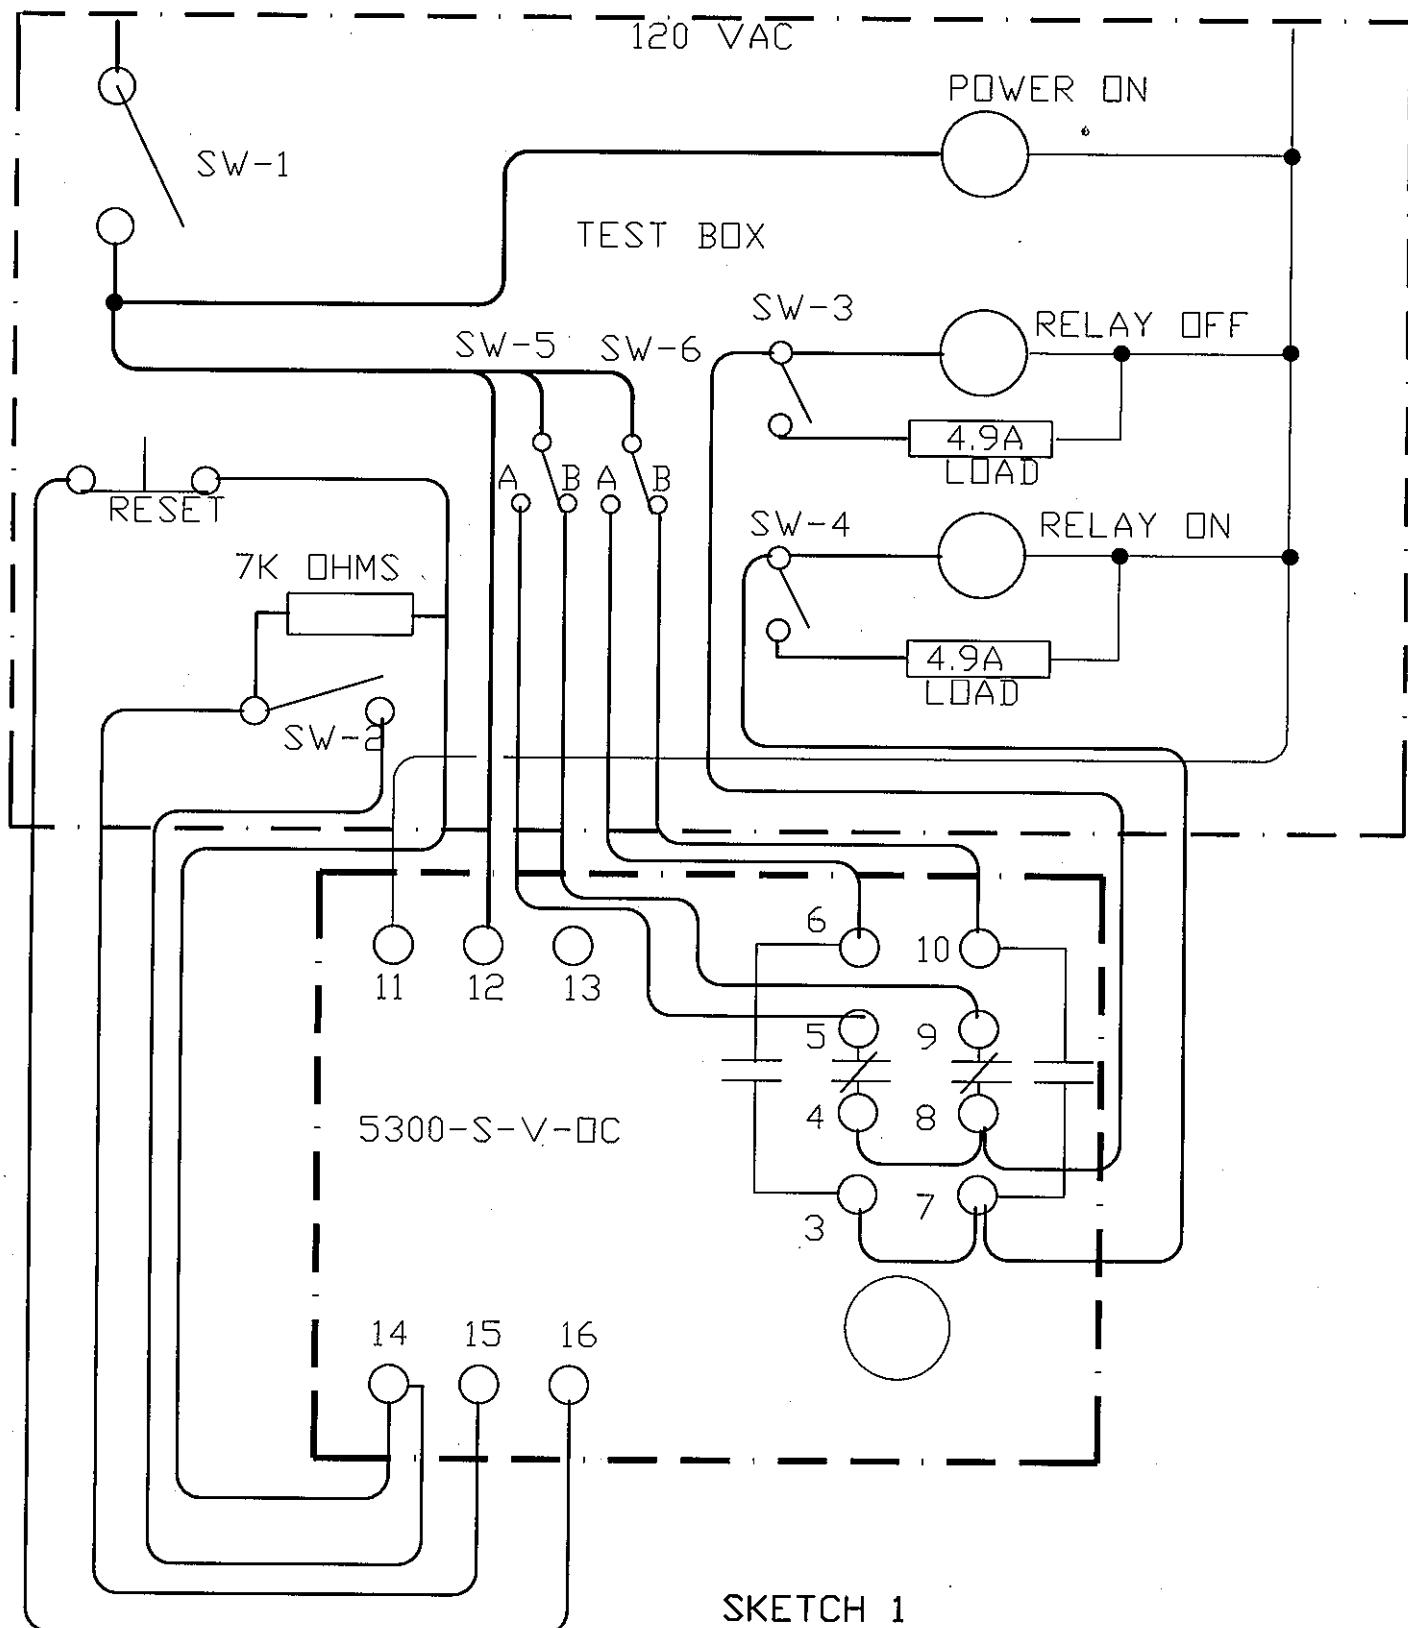

SKETCH 1  
RELAY CONTACT TEST SETUP

HNF-4275, REVISION 3

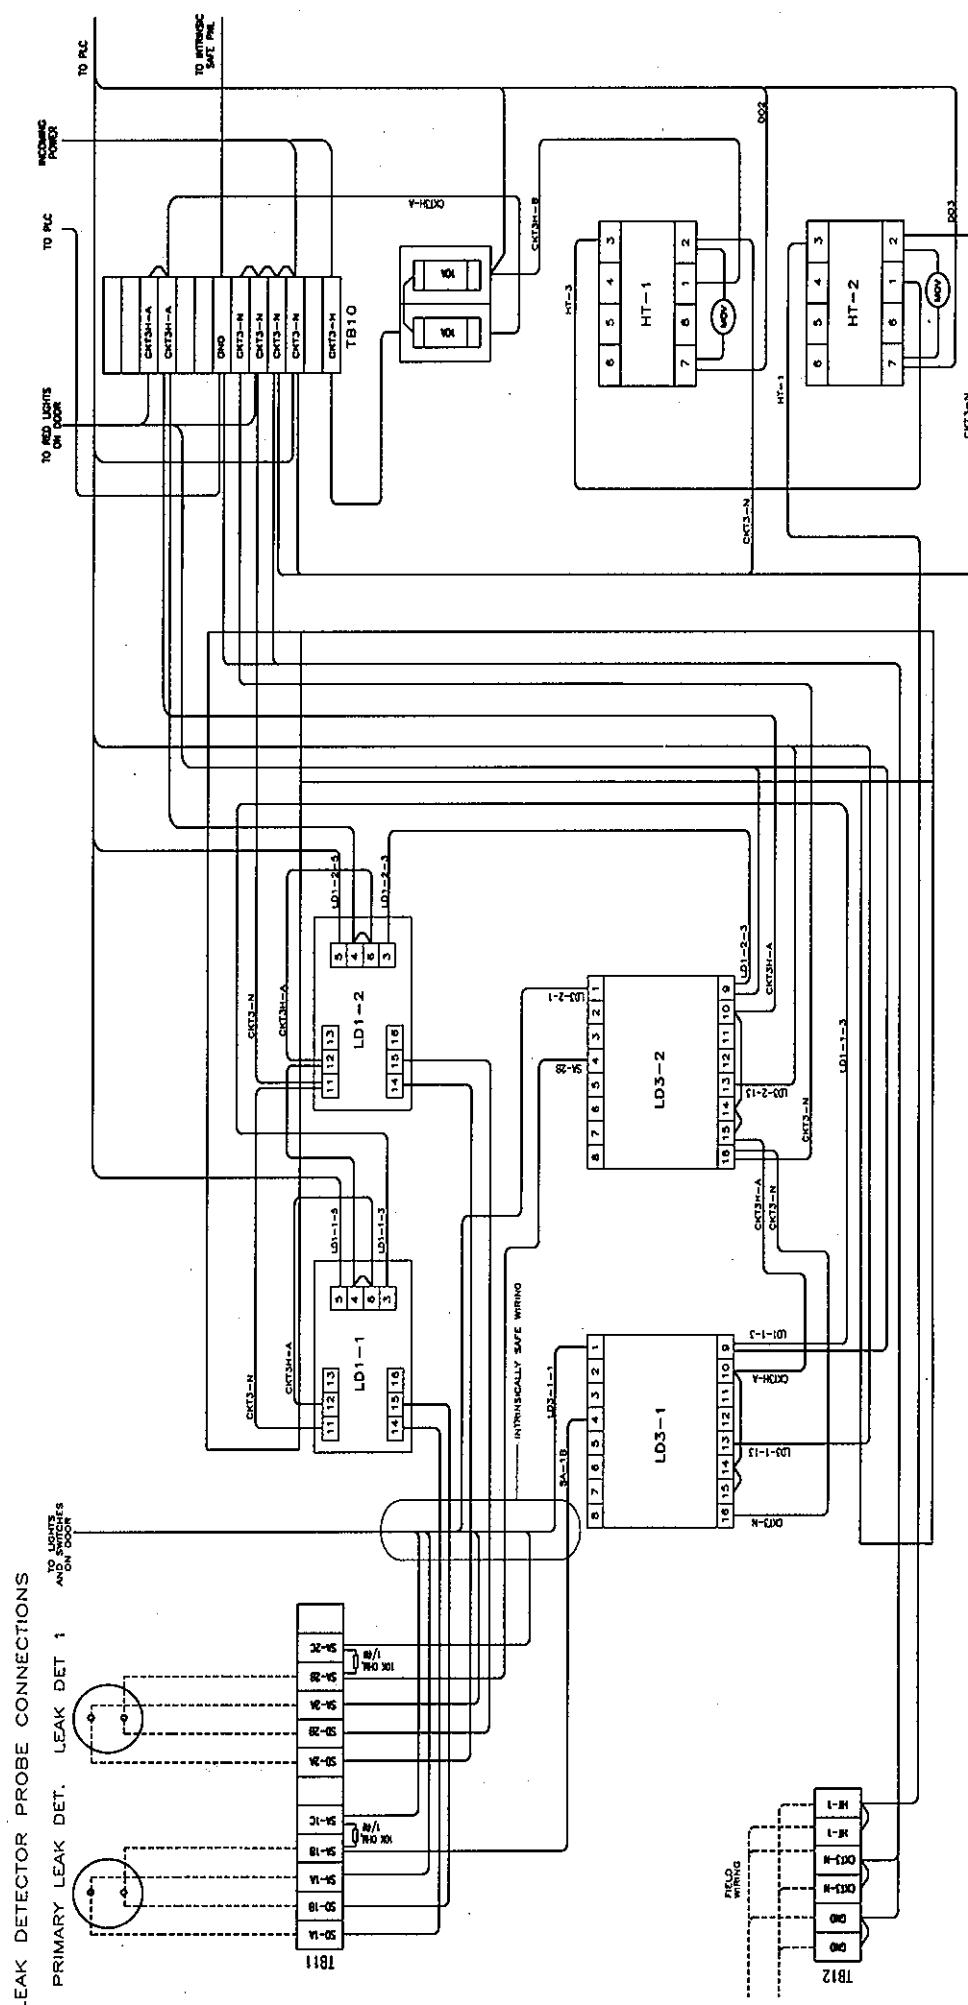

LEAK DETECTOR CONTROL DIAGRAM  
SKETCH 2  
PAGE 15 OF 15
