

Waste Isolation Pilot Plant

Geotechnical Analysis Report For July 2006 – June 2007

U.S. Department of Energy

March 2008



This document has been submitted as required to:

Office of Scientific and Technical Information
P.O. Box 62
Oak Ridge, TN 37831
(865) 576-8401

Additional information about this document may be obtained by contacting the WIPP Information Center at 1-800-336-9477. Copies may be obtained by contacting the National Technical Information Service, U.S. Department of Commerce, 5285 Port Royal Road, Springfield, VA 22161.

This page intentionally left blank

FOREWORD AND ACKNOWLEDGMENTS

This report contains an assessment of the geotechnical status of the Waste Isolation Pilot Plant (WIPP). During the excavation of the principal underground access and experimental areas, the status was reported quarterly. Since 1987, when the initial construction phase was completed, reports have been published annually. This report presents and analyzes data collected from July 1, 2006, to June 30, 2007.

This Geotechnical Analysis Report (GAR) was written to meet the needs of several audiences. This report satisfies the requirements presented in the WIPP Hazardous Waste Facility Permit¹ (HWFP) and the Certification of Compliance² with Subparts B and C, Title 40 *Code of Federal Regulations* (CFR) Part 191, "Environmental Radiation Protection Standards for Management and Disposal of Spent Nuclear Fuel, High-Level and Transuranic Radioactive Wastes." It focuses on the geotechnical performance of the various components of the underground facility, including the shafts, shaft stations, access drifts, and waste disposal areas. The results of investigations of excavation effects and other geotechnical studies are also included.

The report compares the geotechnical performance of the repository to the design criteria. It describes the techniques that were used to acquire the data and the performance history of the instruments. The depth and breadth of the evaluation of the different components of the underground facility vary according to the types and quantities of data available and the complexity of the recorded geotechnical responses. Graphic documentation of data and tabular documentation of instrument history can be provided upon request.

This GAR was prepared by Washington TRU Solutions LLC (WTS) for the U.S. Department of Energy (DOE), Carlsbad Field Office (CBFO), in Carlsbad, New Mexico. Work was supported by the DOE under Contract No. DE-AC29-01AL66444.

¹ New Mexico Environment Department (NMED), 2006, "Waste Isolation Pilot Plant Hazardous Waste Facility Permit," NM4890139088-TSDF, Santa Fe, NM

² U.S. Environmental Protection Agency, 1998, "Criteria for the Certification and Recertification of the Waste Isolation Pilot Plant's Compliance with the Disposal Regulations: Certification Decision," Federal Register, Vol. 63, No. 95, pp. 27354, May 18, 1998, Washington, DC

This page intentionally left blank

TABLE OF CONTENTS

1.0	INTRODUCTION	15
1.1	Location and Description	15
1.2	Mission.....	18
1.3	Development Status	18
1.4	Purpose and Scope of Geomechanical Monitoring Program	19
1.4.1	Instrumentation	20
1.4.2	Data Acquisition	21
1.4.3	Data Evaluation.....	21
1.4.4	Data Errors.....	22
2.0	GEOLOGY.....	23
2.1	Regional Stratigraphy	23
2.1.1	Permian.....	23
2.1.1.1	Castile Formation	23
2.1.1.2	Salado Formation	25
2.1.1.3	Rustler Formation.....	25
2.1.1.4	Dewey Lake Redbeds	25
2.1.2	Triassic.....	26
2.1.2.1	Dockum Group	26
2.1.3	Quaternary	26
2.1.3.1	Gatuña Formation, Mescalero Caliche, and Surficial Sediments	26
2.2	Underground Facility Stratigraphy	27
2.2.1	Disposal Horizon Stratigraphy of Panels 1, 2, 7, and 8.....	27
2.2.2	Disposal Horizon Stratigraphy of Panels 3, 4, 5, and 6.....	28
2.2.3	Northeast Area Stratigraphy.....	30
3.0	PERFORMANCE OF SHAFTS AND KEYS.....	33
3.1	Salt Shaft	33
3.1.1	Shaft Observations.....	35
3.1.2	Instrumentation	35
3.2	Waste Shaft	38
3.2.1	Shaft Observations.....	40
3.2.2	Instrumentation	40
3.3	Exhaust Shaft	42
3.3.1	Exhaust Shaft Observations.....	43
3.3.1.1	Video Camera	43
3.3.1.2	Shaft Inspection Observations	43
3.3.2	Instrumentation	52
3.4	Air Intake Shaft	54
3.4.1	Shaft Performance	55
4.0	PERFORMANCE OF SHAFT STATIONS	57
4.1	Salt Shaft Station	57
4.1.1	Modifications to Excavation and Ground Control Activities	57
4.1.2	Instrumentation	57

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

4.2	Waste Shaft Station	60
4.2.1	Modifications to Excavation and Ground Control Activities	60
4.2.2	Instrumentation	62
4.3	Air Intake Shaft Station	64
4.3.1	Modifications to Excavation and Ground Control Activities	64
4.3.2	Instrumentation	64
5.0	PERFORMANCE OF ACCESS DRIFTS	65
5.1	Modifications to Excavation and Ground Control Activities	65
5.2	Instrumentation	65
5.2.1	Borehole Extensometers	65
5.2.2	Convergence Points	65
5.3	Analysis of Convergence Point and Extensometer Data	67
5.4	Excavation Performance	72
6.0	PERFORMANCE OF WASTE DISPOSAL AREA	73
6.1	History	73
6.2	Modifications to Excavations and Ground Control Activities	74
6.3	Instrumentation	74
6.4	Excavation Performance	77
6.5	Analysis of Extensometer and Convergence Point Data	78
7.0	GEOSCIENCE PROGRAM	79
7.1	Borehole Inspections	79
7.2	Fracture Mapping	83
8.0	SUMMARY	85
9.0	REFERENCES	87

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

LIST OF TABLES

Table 1-1 – Geomechanical Instrumentation System.....	20
Table 3-1 – Water Removed from the Exhaust Shaft Catch Basin and the Interception Well System	50
Table 4-1 – Vertical Closure Rates in the Salt Shaft Station	60
Table 4-2 – Summary of Roof Extensometers in Waste Shaft Station	62
Table 4-3 – Horizontal Closure Rates in the Waste Shaft Station	64
Table 5-1 – Summary of Modifications and Ground Control Activities in the Access Drifts July 1, 2006, through June 30, 2007	66
Table 5-2 – New and Replaced Convergency Points Installed in the	66
Table 5-3 – Greater than 10 Percent Increases in Annual Vertical Convergence Rates in the Access Drifts	70
Table 6-1 – Summary of Modifications and Ground Control Activities in the Waste Disposal Area from July 1, 2006, to June 30, 2007	74
Table 8-1 – Comparison of Excavation Performance to System Design Requirements.....	86

This page intentionally left blank

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

LIST OF FIGURES

Figure 1-1 – WIPP Location	16
Figure 1-2 – Underground Mining and Waste Disposal Configuration as of June 30, 2007	17
Figure 2-1 – Regional Geology.....	24
Figure 2-2 – Repository Level Stratigraphy of Panels 1, 2, 7, and 8	29
Figure 2-3 – Repository Level Stratigraphy of Panels 3, 4, 5, and 6	30
Figure 3-1 – Salt Shaft Stratigraphy	34
Figure 3-2 – Salt Shaft Instrumentation (Without Shaft Key)	36
Figure 3-3 – Salt Shaft Key Instrumentation.....	37
Figure 3-4 – Waste Shaft Stratigraphy	39
Figure 3-5 – Waste Shaft Instrumentation (Without Shaft Key)	41
Figure 3-6 – Waste Shaft Key Instrumentation.....	42
Figure 3-7 – Exhaust Shaft Stratigraphy.....	45
Figure 3-8 – Sample Intake of Exhaust Shaft Air Monitoring System	46
Figure 3-9 – Diagram of Exhaust Shaft Fixtures and Seepage Zones (Upper 200 ft) ..	47
Figure 3-10 – Location of Interception Wells and Storage Containers	48
Figure 3-11 – Exhaust Shaft Instrumentation (Without Shaft Key)	53
Figure 3-12 – Exhaust Shaft Key Instrumentation	54
Figure 3-13 – Air Intake Shaft Stratigraphy	56
Figure 4-1 – Salt Shaft Station Stratigraphy	58
Figure 4-2 – Salt Shaft Station Instrumentation after Roof Beam Excavation	59
Figure 4-3 – Waste Shaft Station Stratigraphy	61
Figure 4-4 – Waste Shaft Station Instrumentation after Wall Trimming.....	63
Figure 5-1 – Typical Convergence Point Array Configurations Showing Anchor Designations	68
Figure 6-1 – Location of Panel 3 Geotechnical Instruments	75
Figure 6-2 – Location of Panel 4 Geotechnical Instruments	76
Figure 6-3 – Location of Panel 5 Geotechnical Instruments	77
Figure 7-1 – Example of Observation Borehole Layout at Lower Horizon	81
Figure 7-2 – Example of Observation Borehole Layout at Upper Horizon	81
Figure 7-3 – Typical Fracture Patterns at Lower Horizon	82
Figure 7-4 – Typical Fracture Patterns at Upper Horizon	82

This page intentionally left blank

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

ACRONYMS AND ABBREVIATIONS

ASTM	American Society for Testing and Materials
bp	before present
bsc	below shaft collar
CAO	Carlsbad Area Office
CBFO	Carlsbad Field Office
CFR	Code of Federal Regulations
CH	contact-handled
cm	centimeter(s)
DOE	U.S. Department of Energy
EPA	U.S. Environmental Protection Agency
ft	foot (feet)
GAR	Geotechnical Analysis Report
GIS	geomechanical instrumentation system
HWFP	Hazardous Waste Facility Permit
in	inch(es)
km	kilometer(s)
kPa	kilopascal(s)
kVA	kilovolt ampere(s)
LANL	Los Alamos National Laboratory
lb	pound(s)
m	meter(s)
Ma	million years
MB	marker bed
μin	10 ⁻⁶ inch(es)
NMED	New Mexico Environment Department
OMB	orange marker bed
psi	pound(s) per square inch
RH	remote-handled
SPDV	Site and Preliminary Design Validation

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

TRU	transuranic
WIPP	Waste Isolation Pilot Plant
WTS	Washington TRU Solutions LLC
yr(s)	year(s)

1.0 INTRODUCTION

This Geotechnical Analysis Report (GAR) presents and interprets geotechnical data from the underground excavations at the Waste Isolation Pilot Plant (WIPP). The data, which are obtained as part of a regular monitoring program, are used to characterize conditions, to compare actual performance to the design assumptions, and to evaluate and forecast the performance of the underground excavations.

GARs have been available to the public since 1983. During the Site and Preliminary Design Validation (SPDV) Program, the architect/engineer for the project produced these reports quarterly to document the geomechanical performance during and immediately after early excavations of the underground facility. Since completion of the construction phase of the project in 1987, the management and operating contractor for the facility has prepared these reports annually. This report describes the performance and condition of selected areas from July 1, 2006, to June 30, 2007. It is divided into nine chapters.

Chapter 1 provides background information on WIPP, its mission, and the purpose and scope of the geomechanical monitoring program. Chapter 2 describes the local and regional geology of the WIPP site. Chapters 3 and 4 describe the geomechanical instrumentation in the shafts and shaft stations, present the data collected by that instrumentation, and provide interpretation of these data. Chapters 5 and 6 present the results of geomechanical monitoring in the two main portions of the WIPP underground (the access drifts and the waste disposal area). Chapter 7 discusses the results of the Geoscience Program, which include fracture mapping and borehole observations. Chapter 8 summarizes the results of geomechanical monitoring and compares the current excavation performance to the design requirements. Chapter 9 lists references.

1.1 Location and Description

WIPP is located in southeastern New Mexico, 26 miles (42 kilometers [km]) east of Carlsbad (Figure 1-1). The surface facilities were built on the flat to gently rolling terrain that is characteristic of the Los Medaños area. The underground facility is being excavated approximately 2,150 feet (ft) (655 meters [m]) beneath the surface in the Salado Formation. Figure 1-2 shows a plan view of the underground configuration of WIPP as of June 30, 2007.

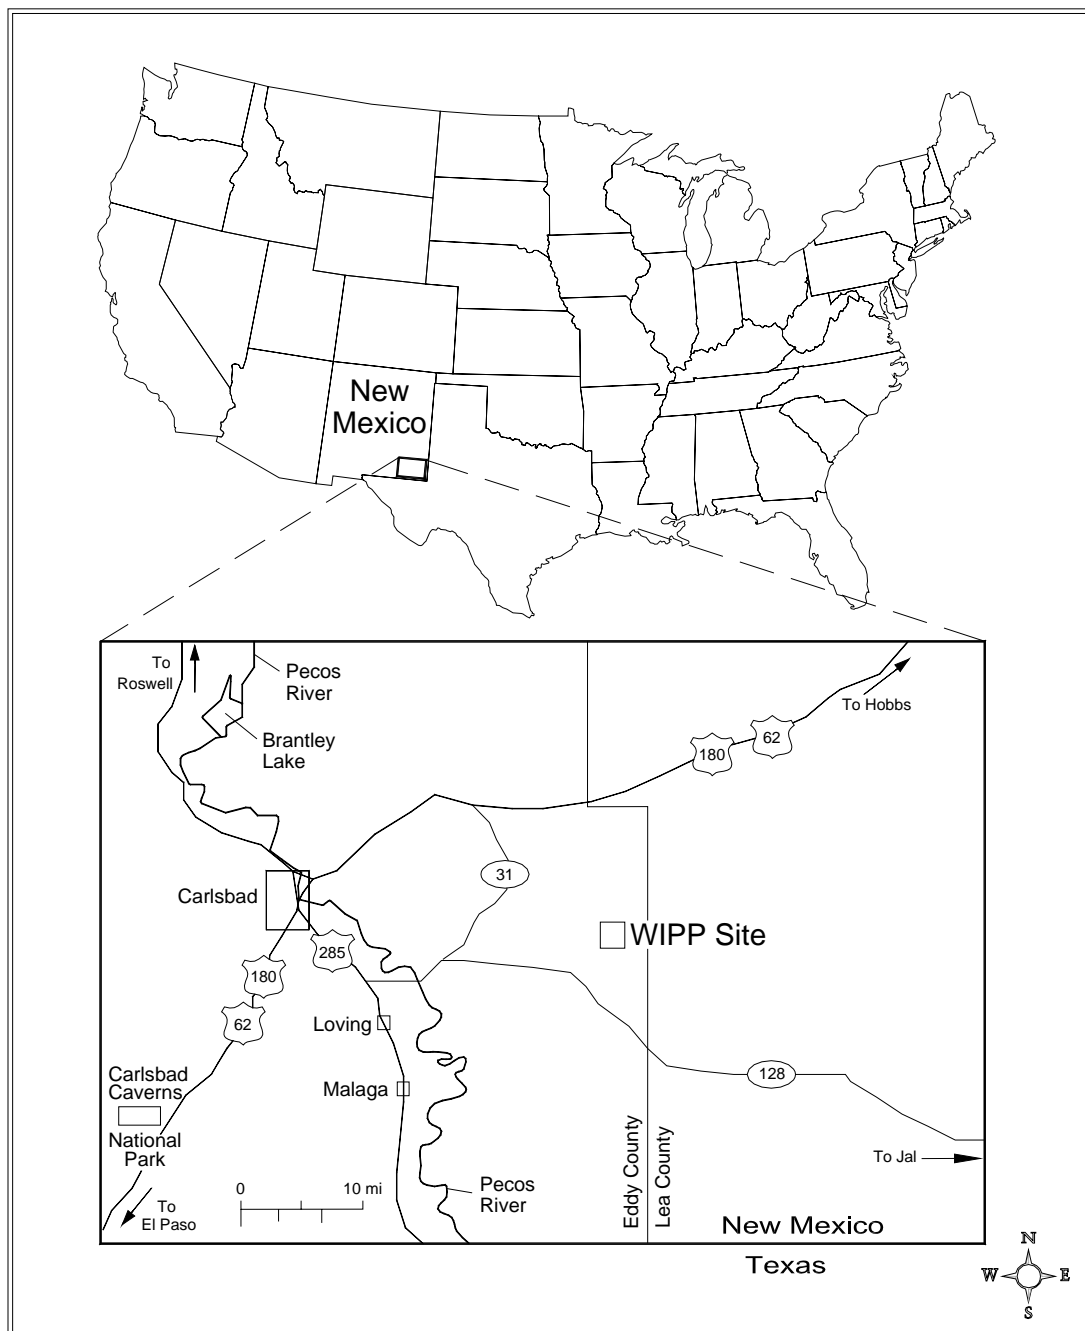


Figure 1-1 – WIPP Location

Geotechnical Analysis Report for July 2006 – June 2007 **DOE/WIPP-08-3177, Vol. 1**

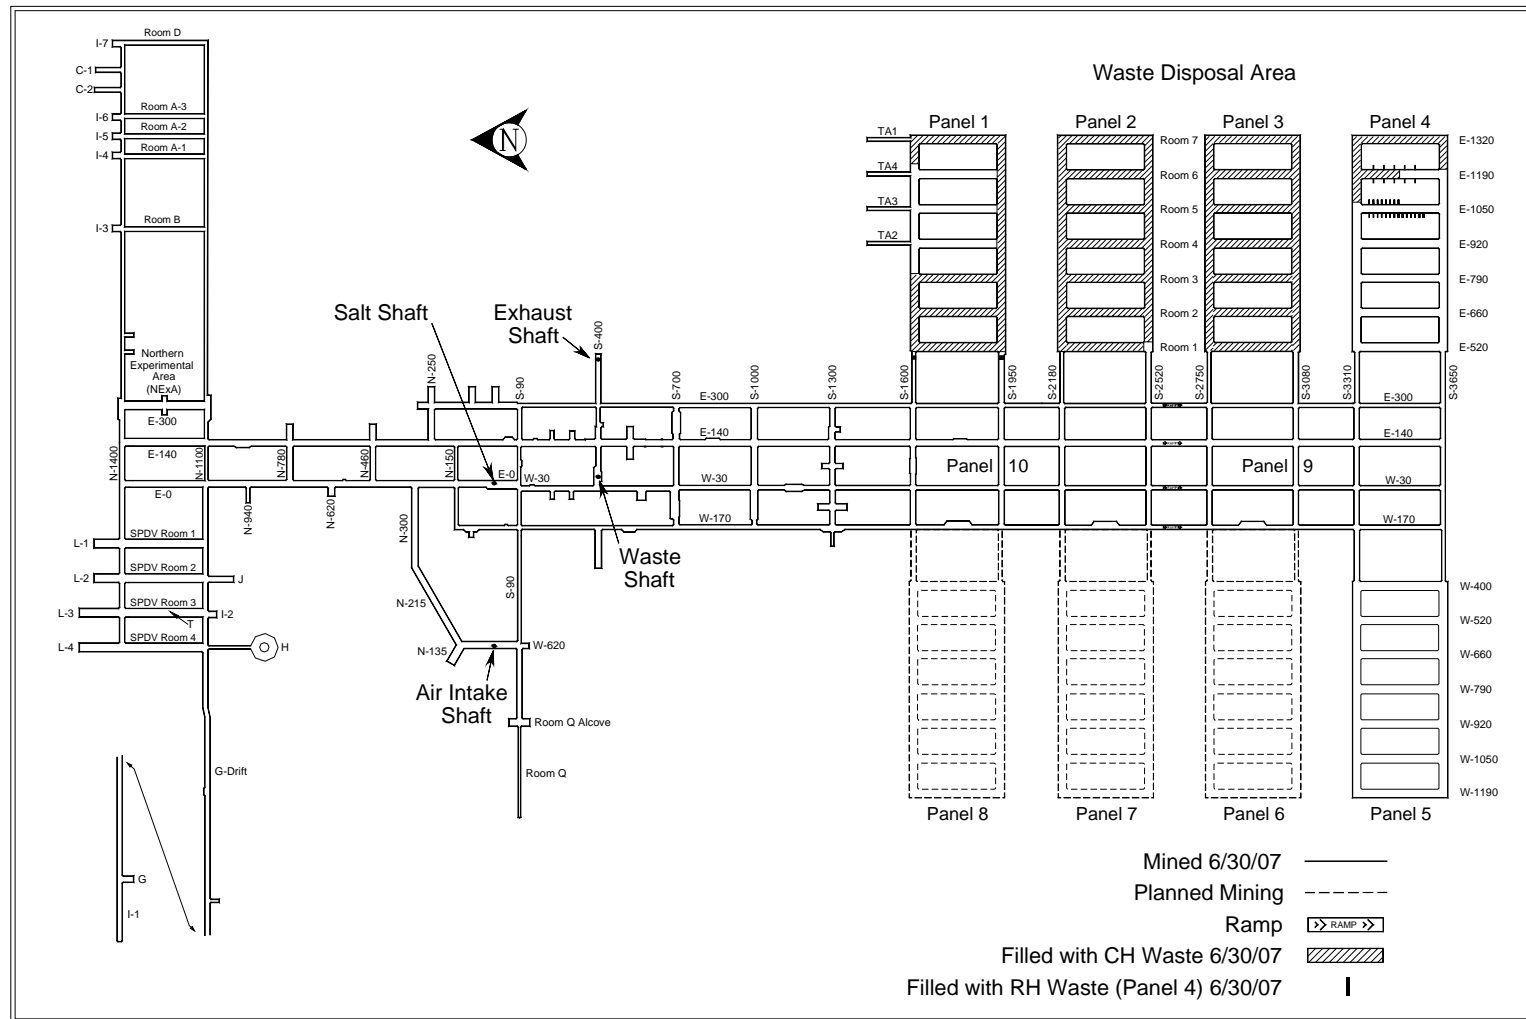


Figure 1-2 – Underground Mining and Waste Disposal Configuration as of June 30, 2007

1.2 Mission

In 1979 Congress authorized WIPP (Public Law 96-164, National Security and Military Applications of Nuclear Energy Authorization Act of 1980) to provide ". . . a research and development facility to demonstrate the safe disposal of radioactive wastes resulting from the defense activities and programs of the United States exempted from regulation by the Nuclear Regulatory Commission." To fulfill this mission, the U.S. Department of Energy (DOE) constructed a full-scale facility to demonstrate both technical and operational principles of the permanent disposal of transuranic (TRU) and TRU mixed wastes. Technical aspects are those concerned with the design, construction, and performance of the subsurface excavations. Operational aspects refer to the receiving, handling, and emplacement of TRU wastes in the facility. The facility was first used for *in situ* studies and experiments without the use of radioactive waste. WIPP now receives, handles, and permanently disposes of TRU waste and TRU mixed waste.

1.3 Development Status

To fulfill its mission, the DOE developed WIPP in a phased manner. The goal of the SPDV phase, begun in 1980, was to characterize the site and obtain *in situ* geotechnical data from underground excavations to determine whether site characteristics and *in situ* conditions were suitable for permanent disposal. During this phase, the Salt Shaft, a ventilation shaft, a drift to the southernmost extent of the proposed waste disposal area, a four-room experimental panel, and access drifts were excavated. Surface-based geological and hydrological investigations were also conducted. The data obtained from the SPDV investigations were reported in the "Summary of the Results of the Evaluation of the WIPP Site and Preliminary Design Validation Program" (DOE, 1983).

Based upon the favorable results of the SPDV investigations, additional activities were initiated in 1983. These included the construction of surface structures, conversion of the ventilation shaft for use as the Waste Shaft, excavation of the Exhaust Shaft, development of additional access drifts to the waste disposal area, excavation of the Air Intake Shaft, and excavation of additional experimental rooms to support research and development. Geotechnical data acquired during this phase were used to evaluate the performance of the excavations in the context of established design criteria (DOE, 1984). Results of these evaluations were reported in Geotechnical Field Data Reports (DOE, 1985; DOE, 1986a) and were summarized in the Design Validation Final Report (DOE, 1986b).

The Design Validation Final Report concluded that the facility, including waste disposal areas, could be developed and operated to fulfill the long-term mission of WIPP (DOE, 1986b). All available information validated the design of underground openings to safely accommodate the permanent disposal of waste under routine operating conditions.

Panel 1 mining began in 1986 and was completed in 1988. Panel 1 was intended to receive waste for an initial operations demonstration and pilot plant phase that was

scheduled to start in October 1988. However, the demonstration and pilot plant phase was not conducted because waste disposal operations had to wait until permits were acquired.

In October 1996, the DOE submitted to the U.S. Environmental Protection Agency (EPA) a compliance certification application in accordance with 40 CFR Parts 191 and 194, which addressed the long-term (10,000-year) performance criteria for the disposal system. On May 18, 1998, the EPA published the final certification that allowed for the receipt of TRU waste at WIPP. Immediately before this certification, the DOE Carlsbad Area Office (CAO) completed an Operational Readiness Review, which is required by the DOE before the start-up or a process change of any nuclear facility. As a result of the review, the CAO notified the Energy Secretary on April 1, 1998, that WIPP was operationally ready to receive waste. On March 26, 1999, the first shipment of TRU waste was received from Los Alamos National Laboratory (LANL). By the end of June 2007, many additional generator sites had shipped waste to WIPP. The cleanup of several small-quantity generator sites, as well as one large-quantity site (Rocky Flats Environmental Technology Site) is now complete.

Waste disposal in Panels 1, 2, and 3 is complete. These panels contain only CH waste. The first RH waste shipment arrived January 24, 2007. Panel 4 is the first to receive both CH and RH waste. As of June 30, 2007, Room 7 of Panel 4 was filled, and Rooms 5-6 were being filled. Mining of Panel 5 started during this reporting period.

1.4 Purpose and Scope of Geomechanical Monitoring Program

As specified in the WIPP HWFP (NMED, 2006), the purpose of the geomechanical monitoring program is to obtain *in situ* data to support the continuous assessment of the design for underground facilities.

Specifically, the program provides for:

- Early detection of conditions that could affect operational safety.
- Evaluation of underground openings closure to ensure adequate access while the openings are actively being used.
- Guidance for design modifications and remedial actions.
- Data for interpreting whether the behavior of underground openings stays within the established design criteria.

Data taken by or input into the geomechanical instrumentation system (GIS) are evaluated and reported in this GAR. This annual report fulfills the requirements set forth in Section IV.F.1 and Attachment M2, Section M2-5b(2) of the WIPP HWFP (NMED, 2006), and 40 CFR §191.14, "Assurance Requirements," implemented through the certification criteria, 40 CFR Part 194.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

The Geomechanical Monitoring Program generates the data for four of the compliance monitoring parameters:

- Creep closure and stresses
- Extent of deformation
- Initiation of brittle deformation
- Displacement of deformation features

Convergence measurements and borehole extensometers provide data on salt creep closure induced by rock excavation. Data on the extent of deformation are generated through borehole extensometers and borehole observations. Fracture mapping of the excavation surface, as well as borehole observations, are used to provide data on the initiation of brittle deformation. Displacement of deformation features in the underground facility is monitored by comparing the results of geologic mapping in newly mined areas to the expected stratigraphy.

The GIS provides data that are collected, processed, and stored for analysis. The following subsections briefly describe the major components of the GIS.

1.4.1 Instrumentation

Instrumentation installed for measuring the geomechanical response of the shafts, drifts, and other underground openings includes convergence points, convergence meters, extensometers, rock bolt load cells, pressure cells, strain gauges, piezometers, and joint meters. Table 1-1 lists a summary of the specifications for geomechanical instrumentation.

Table 1-1 – Geomechanical Instrumentation System

Instrument Type	Measures	Range^a	Resolution^a
Sonic probe borehole extensometer	Cumulative deformation	0–2 in	0.001 in
Convergence point (tape extensometer)	Cumulative deformation	2–50 ft	0.001 in
Wire convergence meter	Cumulative deformation	0–3.5 ft	0.001 in
Embedded strain gauge	Cumulative strain	0–3000 μ in/in	1 μ in/in
Spot-welded strain gauge	Cumulative strain	0–2500 μ in/in	1 μ in/in
Rock bolt load cell	Load	0–50 tons	40 lb
Earth pressure cell	Pressure	0–1000 psi	1 psi
Piezometer	Fluid pressure	0–500 psi	0.5 psi
Joint meter	Cumulative deformation	0–4 in	0.001 in
Vibrating wire borehole extensometer	Cumulative deformation	0–4 in	0.001 in
Wire borehole extensometer	Cumulative deformation	0–20 in	0.001 in
Linear potentiometric borehole extensometer	Cumulative deformation	0–6 in	0.001 in

^a Manual readout boxes for the instruments were manufactured to output measurements in English units. Range and resolution measurement units have not been converted to metric units. Measurements from these instruments have been converted for presentation elsewhere in this report.

1.4.2 Data Acquisition

Geomechanical instruments are read either manually, using portable devices, or remotely by electronically polling the stations from the surface in accordance with approved operating procedures. Remotely read instruments are connected to one of the underground data-loggers, and readings are collected by initiating the appropriate polling routine. Upon completion of a verification process, data are transferred to a computer database. Manual readout devices are taken to instrument locations underground. Data are recorded on data sheets and later entered into an electronic database, along with remotely acquired data.

The underground data acquisition system consists of instruments, polling devices, and a communications network. Instruments are connected to polling devices that are installed in electrical enclosures near the instrument locations. Polling devices are connected by a data link to a surface computer.

Whether acquired manually or remotely, geomechanical data are entered into the database files of the GIS data processing system. The data processing system consists of computer programs that are used to enter, reduce, and transfer the data to permanent storage files. Additional routines allow access to the permanent storage files for numerical analysis, tabular reporting, and graphical plotting. Copies of the instrumentation database and data plots are available upon request³.

1.4.3 Data Evaluation

Rounding and significant digits are used in the data tables of this document. The reference document is American Society for Testing and Materials (ASTM) document ASTM E 29–06b, "Standard Practice for Using Significant Digits in Test Data to Determine Conformance with Specification."⁴

Closure measurements are acquired manually from convergence point anchors and remotely from convergence meters. Data are presented in plots of closure versus time. Closure rate data are calculated and presented as part of the data analysis.

Borehole extensometers provide relative displacement data from instrumented rods or wires anchored at various depths. Displacements are measured relative to a fixed point. The deepest anchor is fixed in the least disturbed ground and is used as the reference point. Plots show displacement versus time for individual anchors relative to the reference point. Typically, the plots show greater relative movement near the collar, (i.e., the opening of the hole). Displacement rate data for the hole collar relative to the deepest anchor are presented in the data analysis.

³ Instrumentation data and data plots are presented in "Geotechnical Analysis Report for July 2006-June 2007 Supporting Data" (DOE/WIPP-08-3177 Volume 2).
The document is available upon request from the National Technical Information Service. See page 3 for details and addresses.

⁴ Copyright by ASTM, Reproduction authorized per License Agreement with Washington TRU Solutions LLC.

The annualized closure rate is calculated as follows:

$$\text{rate}(\text{inches} / \text{year}) = (cfi_2 - cfi_1) / (\text{date}_2 - \text{date}_1) \times 365.25 \text{ days} / \text{year}$$

where cfi = the change from the initial reading (inches)

cfi_1 = cfi reading closest to the beginning of the reporting period

cfi_2 = cfi reading closest to the end of the reporting period

Rock bolt load cells are used to determine bolt support performance. Plots show load versus time for each instrumented bolt.

Earth pressure cells and strain gauges are used to determine the stresses and deformation in and around the shaft liners. Data are depicted in time-based plots.

Piezometers are used to measure the gauge pressure of groundwater and are installed in the shafts at varying elevations to monitor the hydraulic head acting on the shaft liners. Data are plotted as pressure versus time.

Joint meters, installed perpendicular to a crack, monitor the dilation of the crack with time. Data are presented as displacement versus time.

1.4.4 Data Errors

GIS data are processed through a comprehensive database management system. Whether acquired manually or remotely, GIS data are processed and permanently stored according to approved procedures. On occasion, erroneous readings can occur. There are several possible explanations for erroneous readings, including the following:

- The measuring device was misread.
- The reading was recorded incorrectly.
- The measuring device was not functioning within specifications.

When a reading is believed to be erroneous, an immediate evaluation of the suspect reading is performed, and a second reading is collected. If the second reading falls in line with the instrument trend, the first reading is discarded and the second reading is entered in the database. If the second reading and subsequent readings remain out of the instrument trend, the ground conditions in the vicinity of the instrument are assessed to determine the reason for the discrepancy. In addition, the reading frequency may be increased. This process to correct erroneous readings is documented and filed for future reference.

2.0 GEOLOGY

This chapter provides a summary of the stratigraphy of the WIPP region and the site. Readers desiring further geologic information may consult the "Geological Characterization Report, WIPP Site, Southeastern New Mexico" (Powers et al., 1978). This report was developed as a source document on the geology of the WIPP site for individuals, groups, or agencies seeking basic information on geologic history, hydrology, geochemistry, or detailed information, such as physical and chemical properties of repository rocks. A more recent survey of WIPP stratigraphy is included in Holt and Powers (1990).

2.1 Regional Stratigraphy

The stratigraphy in the vicinity of the WIPP site includes rocks of Permian (295 to 250 million years [Ma] before present [bp]), Triassic (250 to 203 Ma), and Quaternary (1.75 Ma to present) ages. The descriptions of formations provided in this section are given in order of deposition (oldest to youngest), beginning with the Castile Formation (Figure 2-1).

2.1.1 Permian

The Permian system in southwestern North America is divided into four series. The last of these, the Ochoan Series, contains the host rock in which the WIPP repository is located. The Ochoan Series is of mostly marine origin and consists of four formations: three evaporite formations (the Castile, the Salado, and the Rustler) and one redbeds formation (the Dewey Lake). The Ochoan evaporites overlie marine limestones and sandstones of the Guadalupian Series (Delaware Mountain Group). The younger redbeds represent a transition from the lower evaporite deposition to fluvial deposition on a broad, low-relief, fluvial plain. The Permian rocks are overlain by fluvial deposits of the Triassic and Quaternary periods.

2.1.1.1 Castile Formation

The Castile Formation, lowermost of the four Ochoan formations, is approximately 1,250 ft (380 m) thick in the WIPP vicinity. Lithologically, the Castile is the least complex of the evaporite formations and is composed chiefly of interbedded anhydrite and halite, with limestone present in minor amounts.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

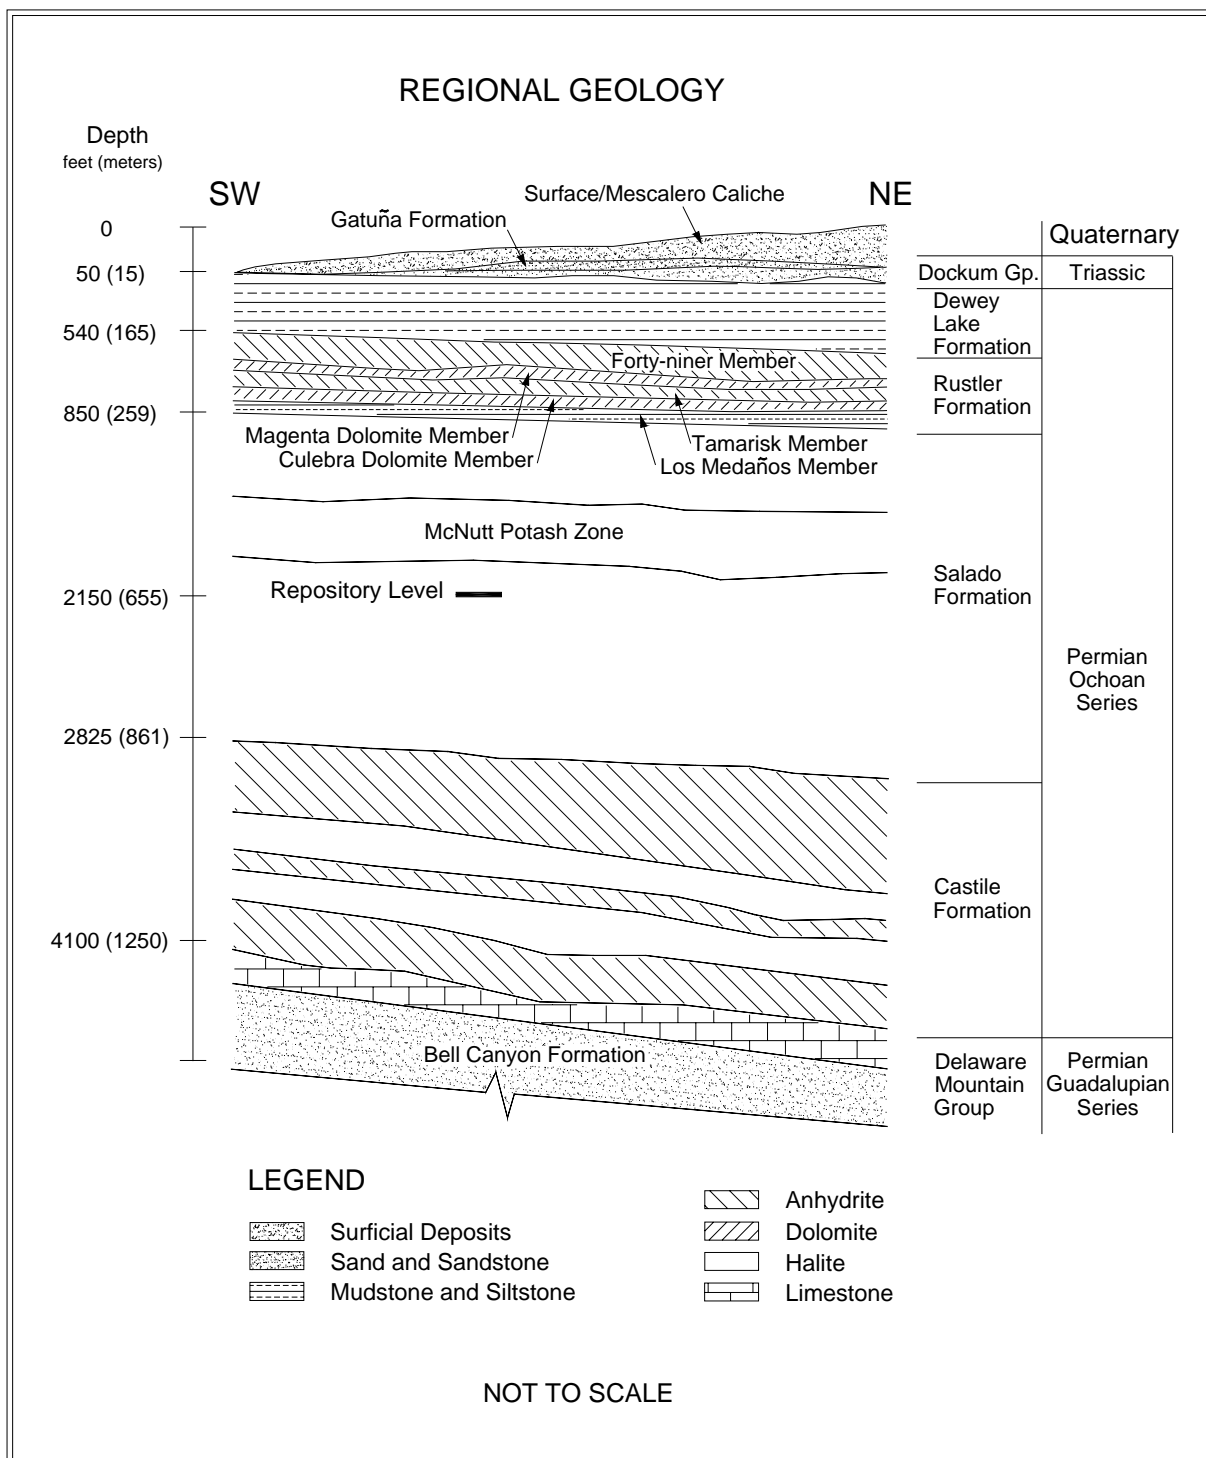


Figure 2-1 – Regional Geology

2.1.1.2 Salado Formation

The Salado Formation comprises nearly 2,000 ft (610 m) of evaporites, primarily halite. The formation is subdivided into three informal members: the unnamed lower member, the McNutt potash zone, and the unnamed upper member. Each member contains similar amounts of halite, anhydrite, and polyhalite and is differentiated on the basis of soluble potassium- and magnesium-bearing minerals. The WIPP disposal horizon is located within the unnamed lower member, 2,150 ft (655 m) below the surface.

2.1.1.3 Rustler Formation

The Rustler Formation is subdivided into five members, starting from its base: the Los Medaños Member, the Culebra Dolomite Member, the Tamarisk Member, the Magenta Dolomite Member, and the Forty-niner Member.

In the vicinity of the WIPP site, the Rustler is approximately 310 ft (95 m) thick and thickens to the east. The lower portion (Los Medaños Member) contains primarily fine sandstone to mudstone with lesser amounts of anhydrite, polyhalite, and halite. Bedded and burrowed siliciclastic sedimentary rocks with cross-bedding and fossil remains signify the transition from the strongly evaporitic environments of the Salado to the brackish lagoonal environments of the Rustler (Holt and Powers, 1990).

The upper portion of the Rustler contains interbeds of anhydrite, dolomite, and mudstone. The Culebra Dolomite member is generally brown, finely crystalline, and locally argillaceous. The Culebra contains rare to abundant vugs with variable gypsum and anhydrite filling and is the most transmissive hydrologic unit within the Rustler. The Tamarisk Member consists of lower and upper sulfate units separated by a unit that varies laterally from mudstone to mainly halite. The Magenta Dolomite Member is a gypsiferous dolomite with abundant primary sedimentary structures and well-developed algal features. The Forty-niner Member consists of lower and upper sulfate units separated by a mudstone that displays sedimentary features and bedding. East of the site area, halite correlates with the mudstone. The Culebra and Magenta Dolomite members are persistent and serve as important marker units.

2.1.1.4 Dewey Lake Redbeds

The Dewey Lake Redbeds is the uppermost of the Ochoan Series formations. Within the series, the Dewey Lake represents a transition from the lower marine evaporite deposition to fluvial deposition on a broad, low-relief, fluvial plain. The redbeds, approximately 475 ft (145 m) thick, consist of predominantly reddish-brown interbedded fine-grained sandstone, siltstone, and claystone. The formation is differentiated from other formations by its lithology and distinctive color (both of which are remarkably uniform), and sedimentary structures, including horizontal- and cross-laminae and ripple marks. The redbeds also contain locally abundant greenish-gray reduction spots and gypsum-filled fractures. The formation thickens from west to east due to eastward dips and erosion to the west.

2.1.2 Triassic

The only Triassic rocks present in the WIPP region belong to the Dockum Group.

2.1.2.1 Dockum Group

The Dockum Group consists of fine-grained floodplain sediments and coarse alluvial debris of Triassic age. At the WIPP site, the Dockum Group pinches out near the center of the site and thickens eastward as an erosional wedge. Local subdivisions of the Dockum Group are the Santa Rosa Sandstone and the Chinle Formation; however, only the Santa Rosa occurs in the vicinity of the site. The Santa Rosa consists primarily of poorly sorted sandstone with conglomerate lenses and thin mudstone partings and contains impressions and remnants of fossils. These rocks have more variegated hues than the underlying uniformly colored Dewey Lake.

2.1.3 Quaternary

Quaternary Period deposits include the Gatuña Formation, Mescalero Caliche, and surficial sediments.

2.1.3.1 Gatuña Formation, Mescalero Caliche, and Surficial Sediments

The Gatuña Formation (ranging in age from approximately 1.3 Ma to 600,000 years bp) (Powers and Holt, 1993) is a stream-laid deposit overlying the Dockum Group in the WIPP vicinity. At the site center, the formation consists of approximately 13 ft (4 m) of poorly consolidated sand, gravel, and silty clay. The Gatuña Formation is light red and mottled with dark stains. The unit contains abundant calcium carbonate, but is poorly cemented. Sedimentary structures are abundant (Powers and Holt, 1993, 1995).

The Mescalero Caliche (approximately 500,000 years bp) is approximately 4 ft (1.2 m) thick in the WIPP vicinity. The Mescalero is a hard, resistant soil horizon that lies beneath a cover of wind-blown sand. The horizon is petrocalcic, or very strongly cemented with calcium carbonate. Petrocalcic horizons form slowly beneath a stable landscape at the average depth of infiltration of soil moisture and indicate stability and integrity of the land surface. Many of the surface buildings at WIPP are founded on top of the Mescalero Caliche.

Surficial sediments include sandy soils developed from eolian material and active dune areas. The Berino Series (a soil type) covers about 50 percent of the site and consists of deep sandy soils that developed from wind-worked material of mixed origin. Based on sample analyses, the Berino soil from the WIPP site formed 330,000 ± 75,000 years bp.

2.2 Underground Facility Stratigraphy

The WIPP disposal horizon lies near the midpoint of the Salado Formation. The Salado was deposited in a shallow saline lagoon environment, which progressed through numerous inundation and desiccation cycles that are reflected in the formation. An "ideal" cycle progresses upward as follows: a basal layer consisting predominantly of claystone, followed by a layer of sulfate, which is in turn followed by a layer of halite. The entire sequence is capped by a bed of argillaceous (clay-rich) halite accumulated during a period of mainly subaerial exposure.

A regional system used for numbering the more significant sulfate beds within the Salado designates these beds as marker beds (MBs), counted from MB100 near the top of the formation to MB144 near the base. The repository is located between MB138 and MB139 (Figure 2-2) within a sequence of laterally continuous depositional cycles as described above. Within this sequence, layers of clay and anhydrite that are locally designated (as shown) can have a significant impact on the geomechanical performance of the excavations. Clay layers provide surfaces along which slip and separation can occur, whereas anhydrite acts as a brittle unit that does not deform plastically.

In the vicinity of the WIPP, the stratigraphy is fairly continuous and uniform. Beds generally dip towards the south-southeast at a slope of approximately 3 percent.

2.2.1 Disposal Horizon Stratigraphy of Panels 1, 2, 7, and 8

This disposal horizon contains Panels 1, 2, 7, and 8, all the shaft areas, the shop areas, the SPDV areas (which are now closed), and all the access drifts to S-2620 (the four main entries that extend south rise in a ramp that starts at S-2620 and ends at S-2740). Panels 7 and 8 have not yet been excavated.

Most underground excavations are located within this disposal horizon (Figure 2-2). In it, the Orange Marker Bed (OMB) lies near the middle of the rib (i.e., the excavation wall). The OMB is a laterally consistent unit of moderate to light reddish-orange translucent halite about 6 inches (in) (15 centimeters [cm]) thick that is used as a point of reference during excavation.

MB139 lies approximately 5 ft (1.5 m) below the excavation floor. MB139 is a 20-to-32 in (50-to-80 cm) thick layer of polyhalitic anhydrite. The top of the anhydrite undulates up to 15 in (38 cm), while the bottom is sub-horizontal and is underlain by clay "E". Above MB139 is a unit of halite that terminates at the base of the OMB. Within this unit, polyhalite is locally abundant and decreases upward, while argillaceous material increases upward.

Above the OMB, a thin band of argillaceous halite gives way to a thick sequence of clear halite that becomes increasingly argillaceous upward and is capped by clay "F". Clay "F" occurs as a thin layer occasionally interrupted by partings and breaks and is readily visible in the upper ribs of disposal horizon excavations. Above clay "F", another sequence of halite begins that, as in lower sequences, becomes increasingly

argillaceous upward. This sequence terminates at the clay "G"/Anhydrite "b" interface, approximately 6.5 ft (2 m) above the roof of most disposal horizon excavations, forming a roof beam that typically acts as a structural unit. The roof of some disposal horizon excavations (e.g., the E-140 drift between S-1000 and 1950) has been excavated to the upper contact of Anhydrite "b". In this case, a roof beam is formed by the next depositional sequence beginning with Anhydrite "b" and progressing upward to the clay "H"/Anhydrite "a" interface, approximately 6.5 ft (2 m) above the upper contact of Anhydrite "b".

2.2.2 Disposal Horizon Stratigraphy of Panels 3, 4, 5, and 6

Field observations and computer modeling indicated that moving the disposal horizon stratigraphically upwards (so that the roof was located at clay "G") would improve long-term ground conditions and provide a more stable roof configuration without significantly impacting repository performance. In 2000, the decision was made to implement this change by moving the mining horizon up approximately six feet. Subsequently, in 2000 and 2001, ramps were mined in the W-170, W-30, E-140, and E-300 drifts between S-2620 and S-2750 (Figure 1-2). As a result, the disposal horizon for Panels 3, 4, 5, and 6, and the associated connecting drifts, lies above the horizon for the other panels (Figure 2-3). Panel 5 is being excavated. Panel 6 has not yet been excavated.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

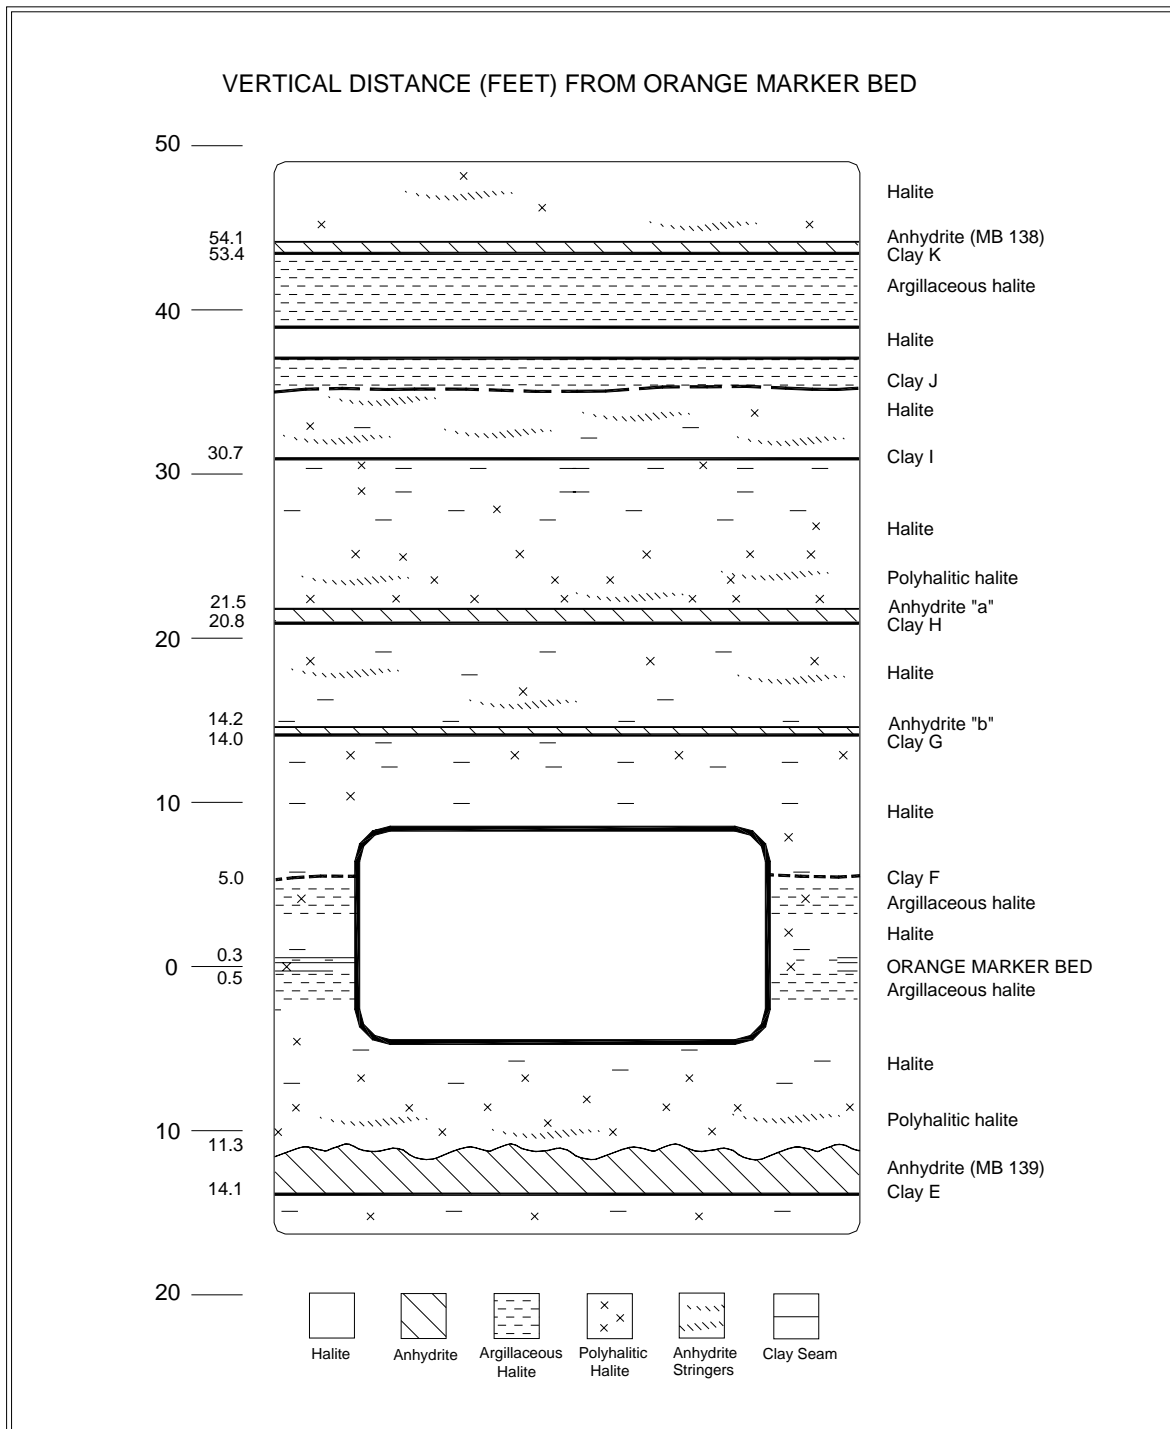


Figure 2-2 – Repository Level Stratigraphy of Panels 1, 2, 7, and 8

In this horizon (see Figure 2-3), the OMB lies at or below the floor. MB139 lies about 12 ft (3.7 m) below the floor. The roof is immediately above Anhydrite "b". Clay "G"/Anhydrite "b" is used as the mining reference during excavation of this disposal horizon.

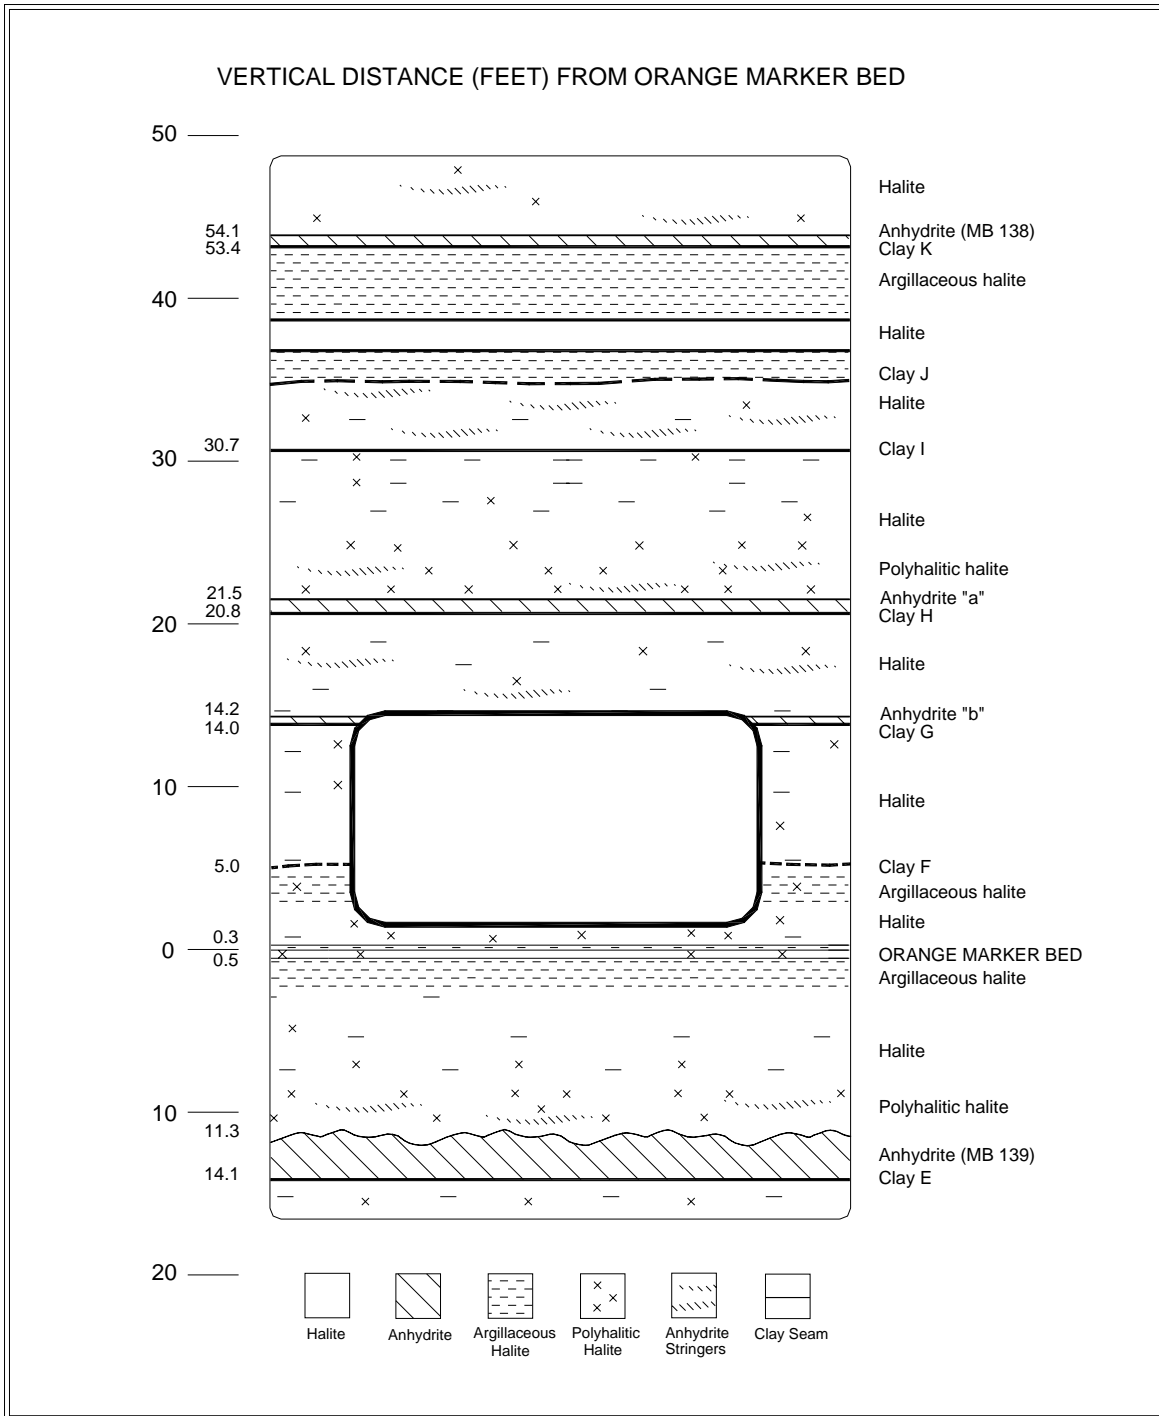


Figure 2-3 – Repository Level Stratigraphy of Panels 3, 4, 5, and 6

2.2.3 Northeast Area Stratigraphy

All of the Northeast Area, a former experimental area, is now deactivated and closed to access. These excavations lie at a higher stratigraphic level than the disposal excavations. Floors are at Anhydrite "b". As in the lower units, the halite intervals between the clay seams/anhydrite beds contain relatively pure halite that becomes

increasingly argillaceous upward. Above clay "I", two more halite intervals complete the underground facility stratigraphy. Clay "J", at the top of the first of these intervals, may occur as a distinct seam or merely an argillaceous zone. Clay "K" tops the second interval and is overlain by anhydrite MB138.

This page intentionally left blank

3.0 PERFORMANCE OF SHAFTS AND KEYS

Four shafts connect the surface with the WIPP underground. They are the Salt Shaft, which is used primarily for removing excavated salt from the underground and is used for transporting personnel and material; the Waste Shaft, which is used primarily for transporting TRU waste to the underground and for transporting personnel and materials; the Exhaust Shaft, which is used to exhaust the ventilation air from the underground; and the Air Intake Shaft, which is the primary source of fresh air ventilation to the underground. This chapter describes the geomechanical performance of these shafts.

Although through the years much of the instrumentation installed in the shafts has failed, there are no plans to replace it. The project has a good understanding of the expected movements in the shafts. Monitoring results up to the point of instrument failure did not indicate unusual shaft movements or displacements. Continued periodic visual inspections confirm the expected shaft performance and provide necessary observations to evaluate shaft performance. Replacement of failed instrumentation will not provide significant additional information.

3.1 Salt Shaft

The first construction activity undertaken during the SPDV Program was the excavation of the Exploratory Shaft. This shaft was subsequently referred to as the Construction and Salt Shaft and is currently designated the Salt Shaft (see Figure 1-2). The shaft was drilled from July 4 to October 24, 1981, and geologically mapped in the spring of 1982 (DOE, 1983). Figure 3-1 presents the stratigraphy in the Salt Shaft.

The Salt Shaft is lined from the surface to 846 ft (258 m) with steel casing having an inside diameter of 10 ft (3-m). The thickness of the steel liner (including external stiffener rings) increases from 0.62 in (1.6 cm) at the top to 1.5 in (3.8 cm) at the key. Cement grout was placed between the liner and rock face. The 10-ft (3-m) diameter extends through the concrete shaft key to 880 ft (268 m). The shaft key is a 37.5 ft (11.4-m) long, reinforced-concrete structure that begins 3.5 ft (1.07 m) above the bottom of the steel liner. From the key to the bottom at 2,298 ft (700 m), the shaft has a nominal diameter of 12 ft (4 m).

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

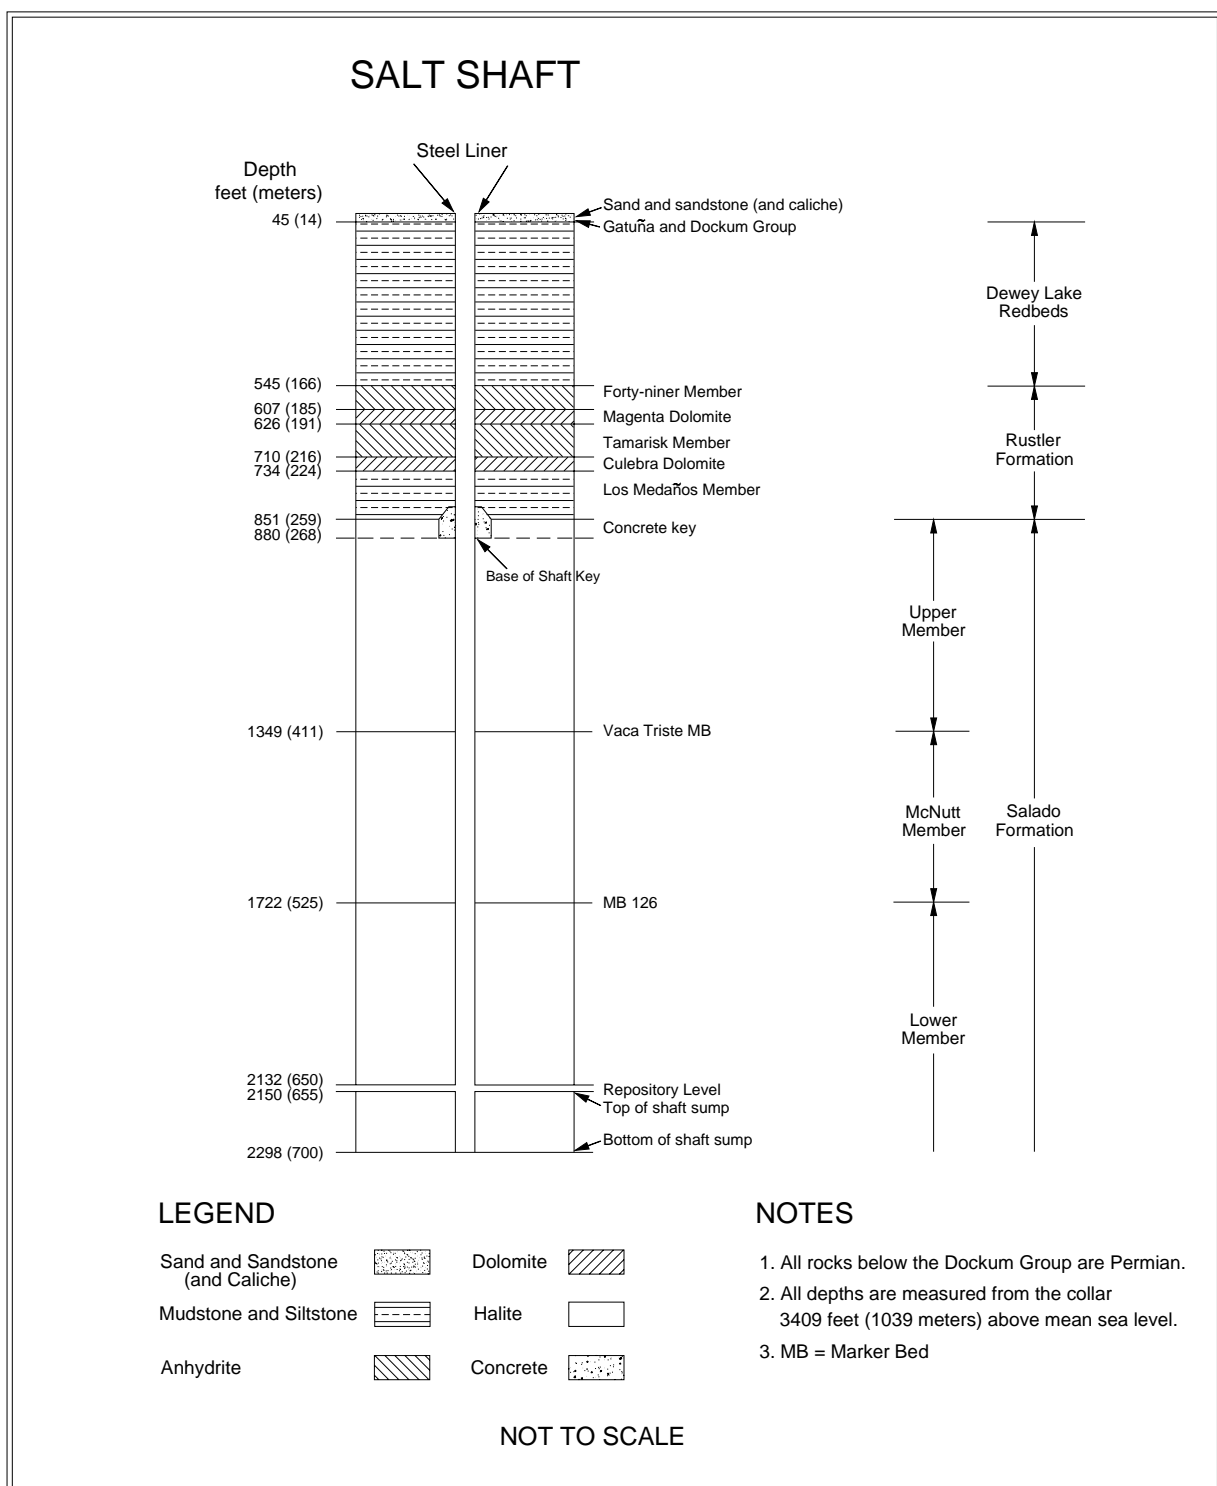


Figure 3-1 – Salt Shaft Stratigraphy

Wire mesh anchored by rock bolts is installed in sections of the lower shaft as a safety screen to contain rock fragments that may become detached. The shaft extends approximately 140 ft (43 m) below the repository horizon in order to accommodate the skip loading equipment and to act as a sump.

3.1.1 Shaft Observations

Underground operations personnel conduct weekly visual shaft inspections. These inspections are performed principally to assess the condition of the hoisting and mechanical systems, but they also include examining the shaft walls for water seepage, loose rock, or sloughing. Visual shaft inspections during this reporting period found that the Salt Shaft was in satisfactory condition. Only routine ground control activities were required.

3.1.2 Instrumentation

Geomechanical instruments (radial convergence points, extensometers, and piezometers) were installed at various levels in the Salt Shaft from April through July of 1982 (Figure 3-2). In the shaft key, instruments included strain gauges, pressure cells, and piezometers. Radial convergence points were installed prior to outfitting. Upon completion of shaft outfitting, no more readings were taken. Figures 3-2 and 3-3 show the instrument locations.

Eleven of the 12 piezometers continue to provide data. The fluid pressures recorded at the end of this reporting period range from approximately 70 pounds per square inch (psi) (483 kilopascals [kPa]) at the 802-ft (244-m) level in the Los Medaños Member to 177 psi (1,220 kPa) at the 691-ft (211-m) level in the Magenta Dolomite Member. The recorded pressures for this reporting period are generally consistent with the readings from the previous reporting period. The fluid pressure on the shaft liner will continue to be monitored on a regular basis.

Four earth pressure cells were installed in the key section of the Salt Shaft during concrete emplacement at the 860-ft (262-m) level. These instruments measure the normal stress between the concrete key and the Salado Formation as salt creep loads up the key structure. Three of the four earth pressure cells continue to provide data. These instruments have indicated essentially no contact pressure since their installation (readings resemble instrument drift at a zero pressure). The contact pressures recorded by the instruments for this reporting period ranged from -22 to 5 psi (-152 to 34 kPa).

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

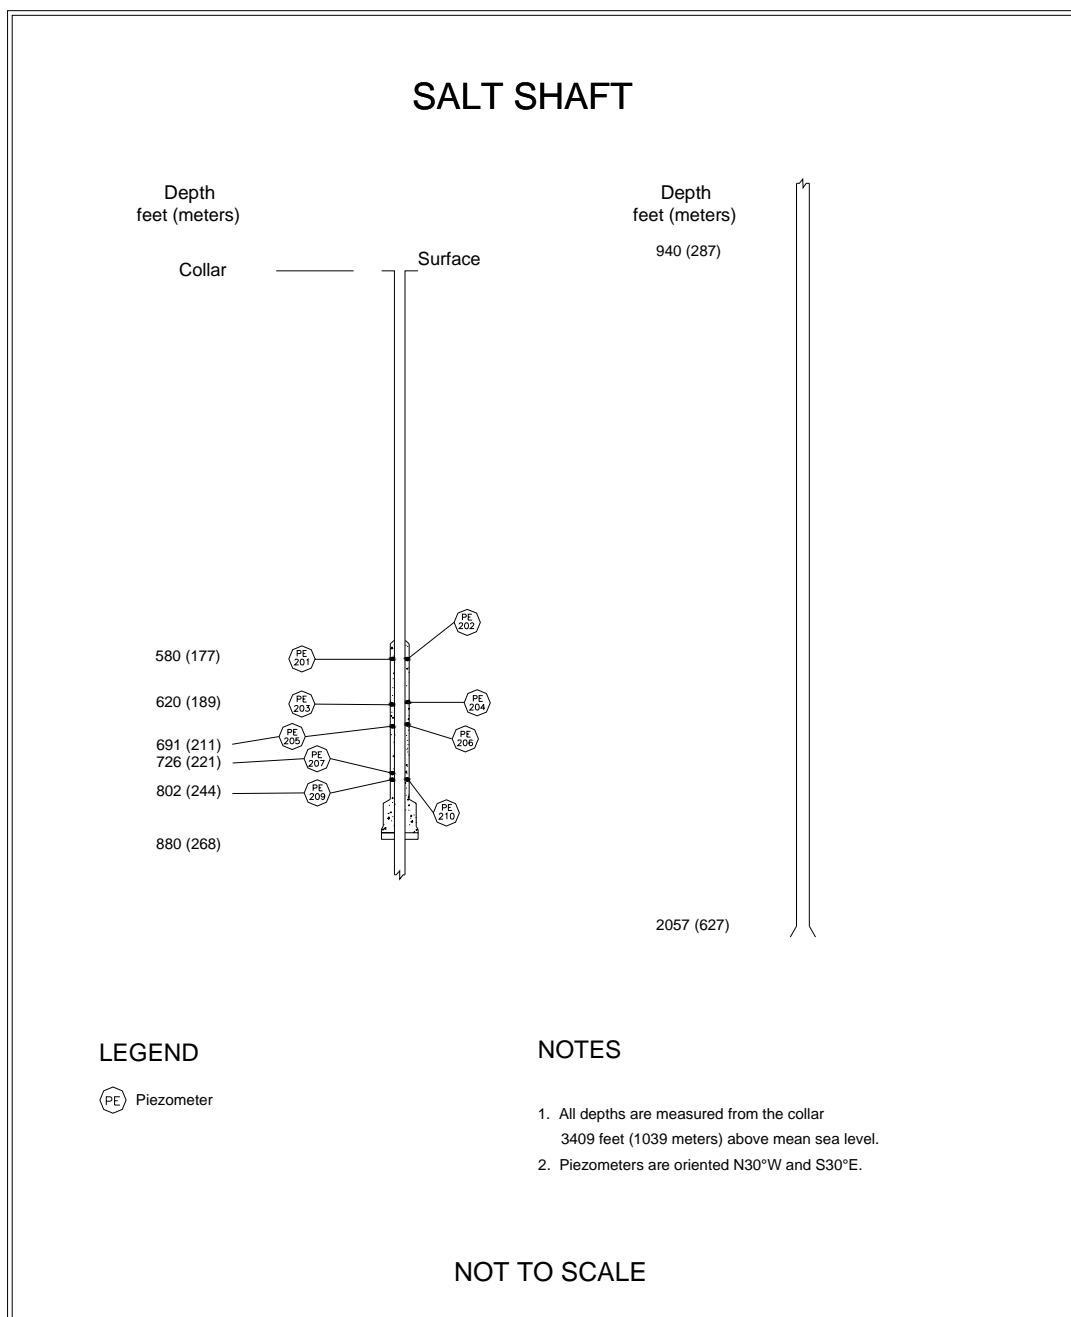


Figure 3-2 – Salt Shaft Instrumentation (Without Shaft Key)

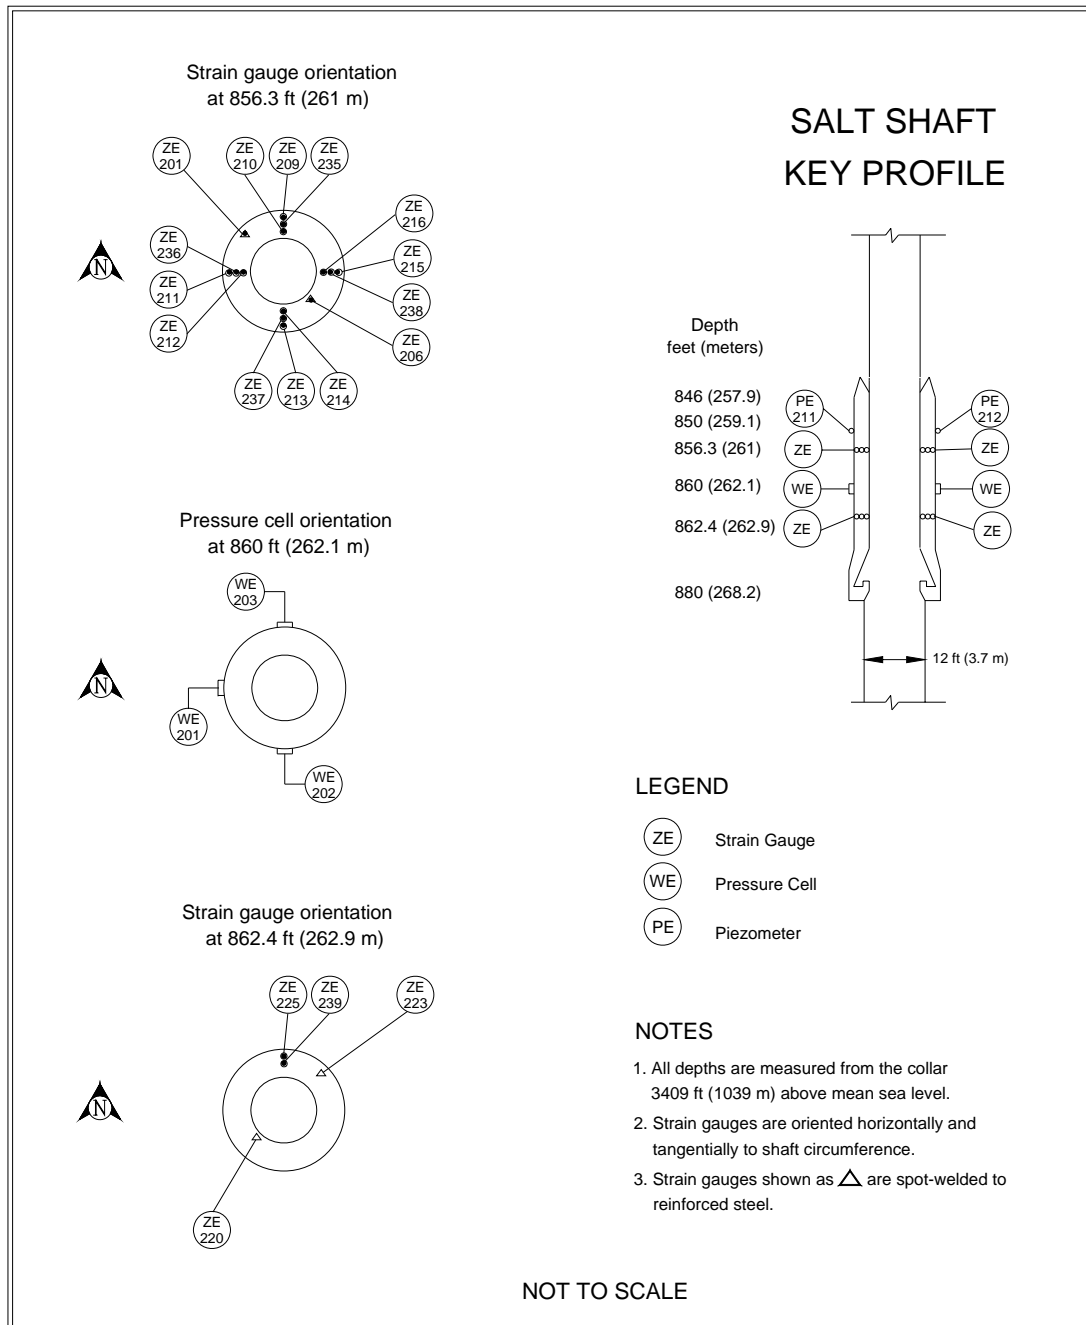


Figure 3-3 – Salt Shaft Key Instrumentation

Sixteen spot-welded and twenty-four embedment strain gauges were installed on and in the shaft key concrete at both the 856.3-ft (261-m) level and at the 862.4-ft (263-m) level. Four spot-welded strain gauges are still functioning at these levels. Maximum strains at the 856.3-ft (261-m) level were 672 and 739 microstrain. Strains at the 862.4-ft (262.9-m) level were 620 and 856 microstrain. The strains from the 12 embedment strain gauges at the 856.3-ft (261-m) level ranged from -826 to 999 microstrain. The strains from the two embedment strain gauges at the 862.4-ft (262.9-m) level were 217 to 358 microstrain. The strains recorded by the spot-welded strain gauges and the embedment strain gauges during this reporting period are very similar to the strains recorded by these instruments at the end of the previous reporting period.

3.2 Waste Shaft

As part of the SPDV Program, a 6-ft (2-m) diameter ventilation shaft, now referred to as the Waste Shaft, was excavated from December 1981 through February 1982 (see Figure 1-2). This shaft, in combination with the Salt Shaft, provided a two-shaft underground air circulation system. From October 11, 1983, to June 11, 1984, the shaft was enlarged to a diameter of 20 to 23 ft (6 to 7 m) and lined above the key. Stratigraphic mapping (Figure 3-4) was conducted during shaft enlargement from December 9, 1983, to June 5, 1984 (Holt and Powers, 1984).

The Waste Shaft is lined with non-reinforced concrete having a 19 ft (6 m) inside diameter from the surface to the top of the key at 837 ft (255 m). Liner thickness increases from 10 in (25 cm) at the surface to 20 in (51 cm) at the key. The key is 63 ft (19 m) long and 4.25 ft (1.3 m) thick and is constructed of reinforced concrete. The bottom of the key is 900 ft (274 m) below the surface. The diameter of the shaft is 20 ft (6 m) at the bottom of the key and increases to 23 ft (7 m) just above the shaft station. The shaft below the key is lined with wire mesh anchored by rock bolts. The diameter of 23 ft (7 m) extends to a depth of approximately 2,286 ft (697 m), with the shaft sump comprising the lower 119 ft (36 m) of that interval.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

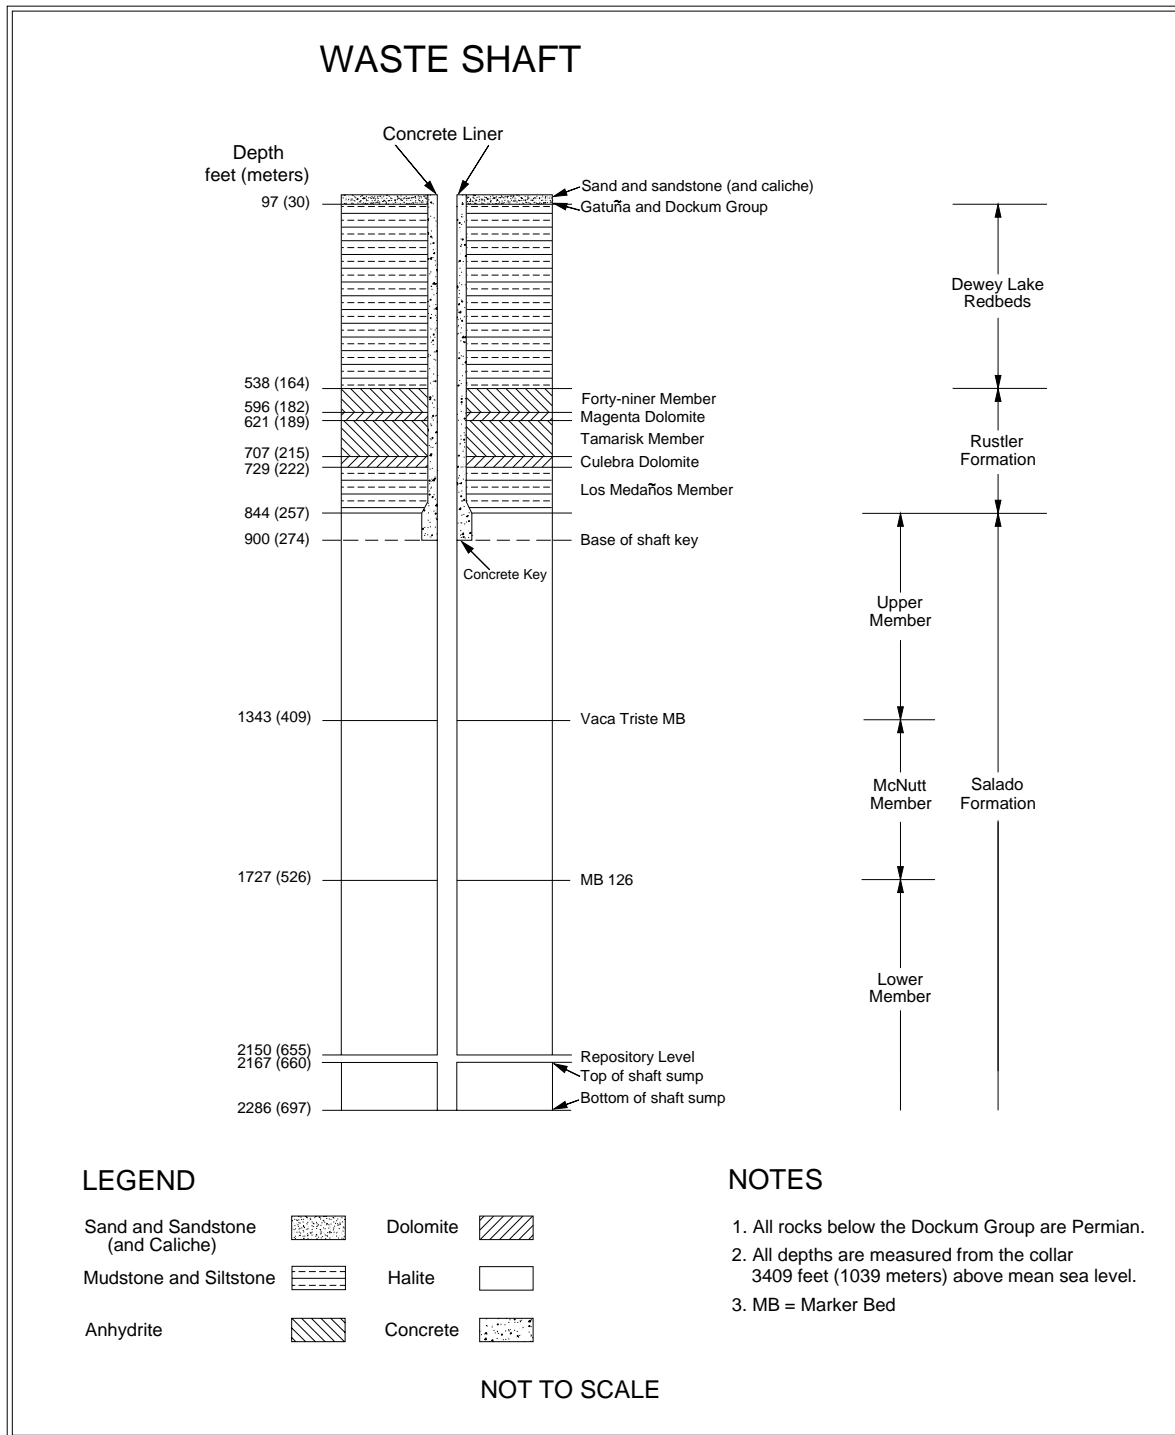


Figure 3-4 – Waste Shaft Stratigraphy

3.2.1 Shaft Observations

Underground operations personnel conduct weekly visual shaft inspections, principally to assess the condition of the hoisting and mechanical systems, but also include observation of the shaft walls for water seepage, loose rock, or sloughing. The visual shaft inspections found that the Waste Shaft was in satisfactory condition. No ground control activities other than routine maintenance were required.

3.2.2 Instrumentation

Radial convergence points, extensometers, piezometers, and earth pressure cells were installed in the Waste Shaft between August 27 and September 10, 1984. Radial convergence points were installed prior to the outfitting. Upon completion of shaft outfitting, no more radial convergence readings were taken. Figures 3-5 and 3-6 show the instrument locations.

Nine multiposition borehole extensometers were installed in arrays 1,071 ft (326 m), 1,566 ft (477 m), and 2,059 ft (628 m) below the surface as shown in Figure 3-5. Each array consists of three extensometers. Currently, six out of nine extensometers remain functional; however, no data have been collected during this reporting period due to the malfunction of the data-logger. Since the type of extensometers installed in the shaft over 22-years ago are no longer manufactured, remote data acquisition equipment for these extensometers are also unavailable, although a method of acquiring the extensometer data (which would use an available manual electronic readout), is being considered. Since the manual readout is not designed to read instruments over the distances required in the shaft, interfacing and excitation issues will need to be resolved.

Twelve piezometers were installed in the lined section of the Waste Shaft on September 7 and 8, 1984, to monitor fluid pressure behind the shaft liner and the key section in the shaft. Data continue to be received from 10 piezometers. The maximum recorded fluid pressure during this reporting period is 141 psi (972 kPa) at the 717-ft (219-m) level. The pressure readings this reporting period were consistent with the readings from the previous reporting period with a mean change in pressures of less than 2 psi (14 kPa).

Four earth pressure cells were installed in the key section of the Waste Shaft during concrete emplacement between March 23 and April 3, 1984. Three are still working. These instruments measure the normal stress between the concrete key and the Salado Formation as salt creep loads the key structure. The contact pressures recorded by the instruments for this reporting period ranged from 76 to 107 psi (524 to 738 kPa).

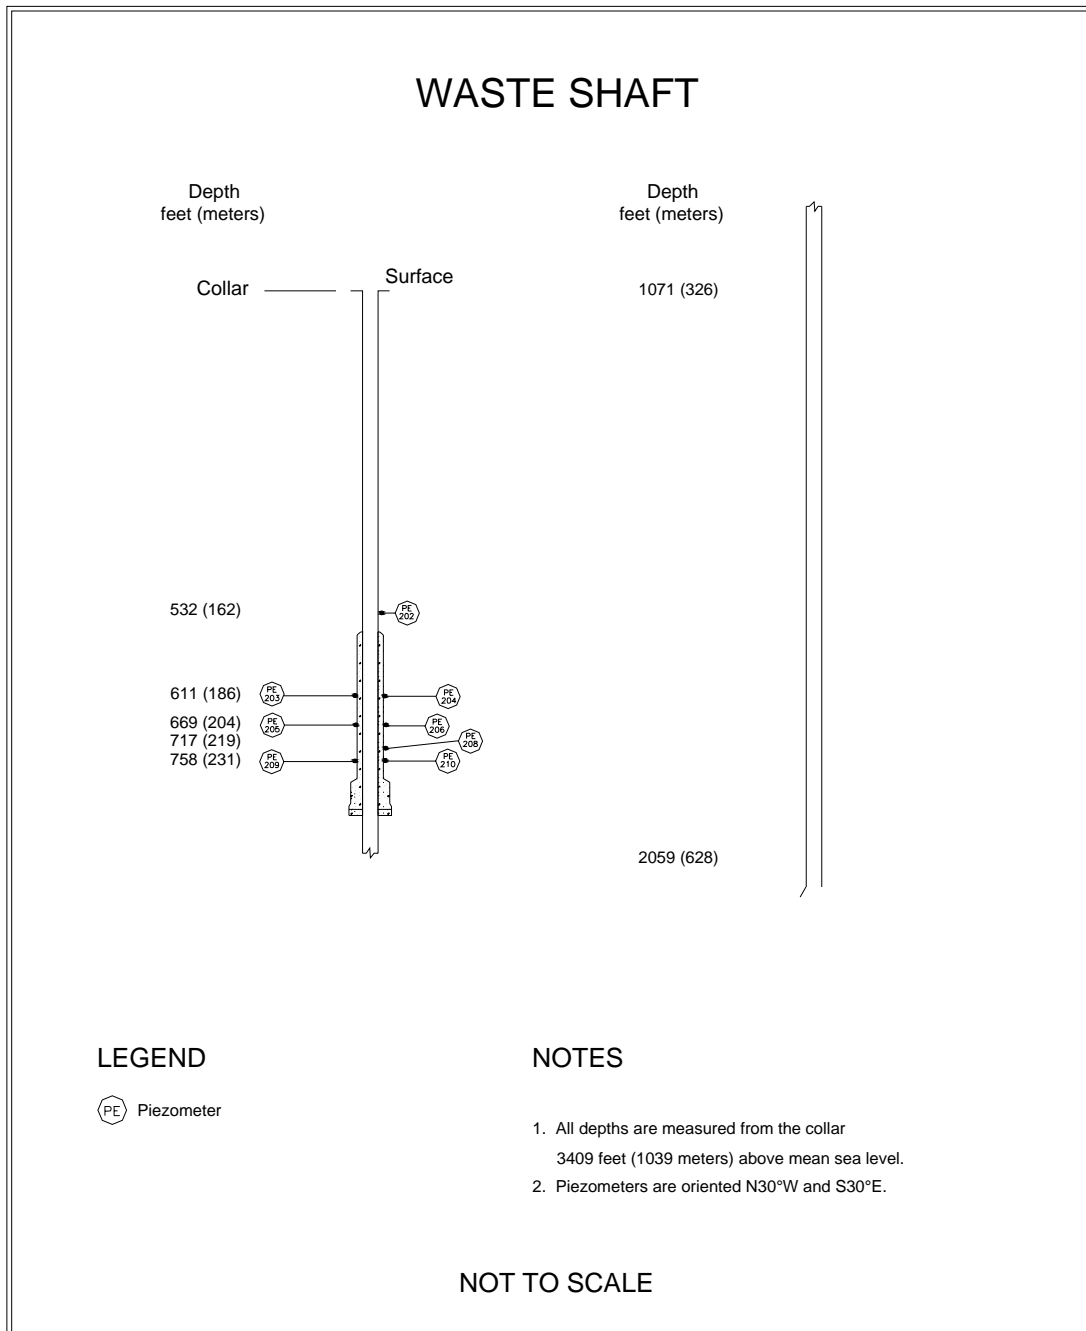


Figure 3-5 – Waste Shaft Instrumentation (Without Shaft Key)

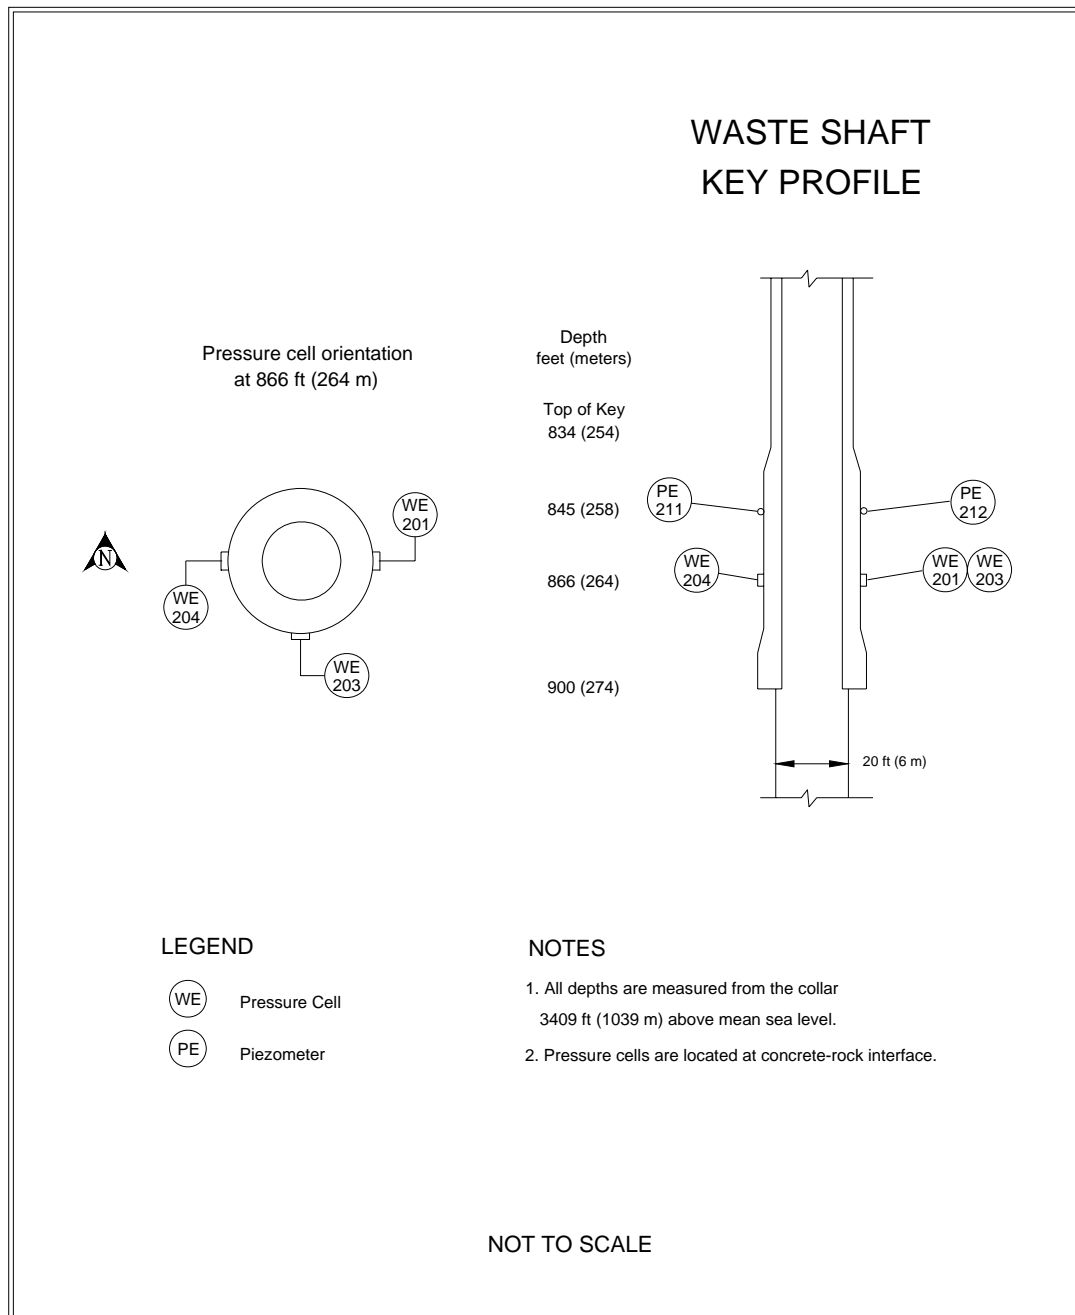


Figure 3-6 – Waste Shaft Key Instrumentation

3.3 Exhaust Shaft

The Exhaust Shaft was drilled from September 22, 1983, to November 29, 1984, to establish a route from the underground to the surface for exhaust air (Figure 1-2). Stratigraphic mapping was conducted from July 16, 1984, to January 18, 1985 (DOE, 1986c). Figure 3-7 illustrates the Exhaust Shaft stratigraphy.

The Exhaust Shaft is lined with non-reinforced concrete from the surface to the top of the shaft key at 844 ft (257 m). The liner thickness increases from 10 to 16 in (25 to 41 cm) over that interval. The key is 63 ft (19 m) long and 3.5 ft (1 m) thick. The shaft diameter below the key is 15 ft (5 m), and the interval below the key is lined with wire mesh anchored by rock bolts. The shaft terminates at the facility horizon, approximately 2,150 ft (655 m) deep. This shaft has no sump.

3.3.1 Exhaust Shaft Observations

Quarterly Exhaust Shaft video inspections were conducted according to approved WIPP procedures. Inspections were performed to evaluate the condition and to verify the integrity of the shaft. The shaft was examined for cracks, corrosion, salt buildup, leaks, and debris. In addition, inspections examined the condition of anchors, brackets, and down-hole equipment. Between July 2006 and June 2007, four quarterly shaft inspections were conducted on August 22, 2006; November 14, 2006; March 2, 2007; and May 23, 2007.

3.3.1.1 Video Camera

Video inspections use a custom-designed vertical-drop color camera in an aerodynamic housing, suspended by a dual-armored cable, with pan, tilt, and zoom capability. The cable contains five copper conductors and two multi-mode optical fibers. It is reeled out by a winch mounted in a control van. Inspections are recorded electronically.

3.3.1.2 Shaft Inspection Observations

Quarterly video inspection observations concentrate on four major areas: air monitoring components, shaft liner, shaft walls, and equipment support and cabling. The air monitoring components consist of one air-velocity and three air-monitoring devices as shown in Figure 3-8. The video inspection includes examination of each device, including the transport assembly, guide tubes, the sample intake, and the support brackets that extend from Station "A" above the shaft to the Exhaust Shaft collar. Air monitoring components extend from the collar 21 ft into the shaft. Video inspections indicate that the air-sampling components can accumulate salt buildup of up to several inches thick.

The Exhaust Shaft liner is examined for cracks, seepage, and general shaft stability. Currently, there are three principal zones of seepage in the shaft. The first is about 50 to 55 ft below the shaft collar (bsc). The second is about 60 to 65 ft bsc. The third is about 75 to 80 ft bsc, as shown in Figure 3-9. Monitoring of seepage horizons started before 1995. Water entering the shaft through these cracks is believed to originate from a perched aquifer at the base of the Santa Rosa Formation that is being recharged as the result of surface modifications at the site. The fluid level in the Santa Rosa near the shaft is about 43 to 44 ft below the surface. Based on examination of inspection videos, the flow rate into the shaft during this reporting period is estimated at about 1 to 1-1/2 gallons per minute, most of which is carried out of the shaft with the exhaust air. Seepage cracks are confined primarily to the eastern side of the shaft wall.

When fluid was detected seeping into the Exhaust Shaft, a catch basin was designed and installed at the base of the shaft to intercept water and prevent it from draining into the Waste Shaft Sump. Fluid was removed from the catch basin from March 1996 through October 2005 as needed. The catch basin was damaged in 2004 by fallen debris, either salt or instrumentation cables or both. A new catch basin was fabricated and installed in December 2004. This basin was damaged in August 2005, most likely the result of fallen debris. An interception well system was installed between November 2005 and March 2006 to replace the catch basin. Interception wells were drilled down-gradient in S-400 between E-140 and E-300 (Figure 3-10). The interception well system consists of four 30-ft deep 9-7/8-in diameter holes with a submersible pump and pressure transmitter in each. Fluid is pumped from each borehole to a series of storage containers in S-550. A data-acquisition system monitors the fluid level in each hole, turning the pump on or off between set limits as needed.

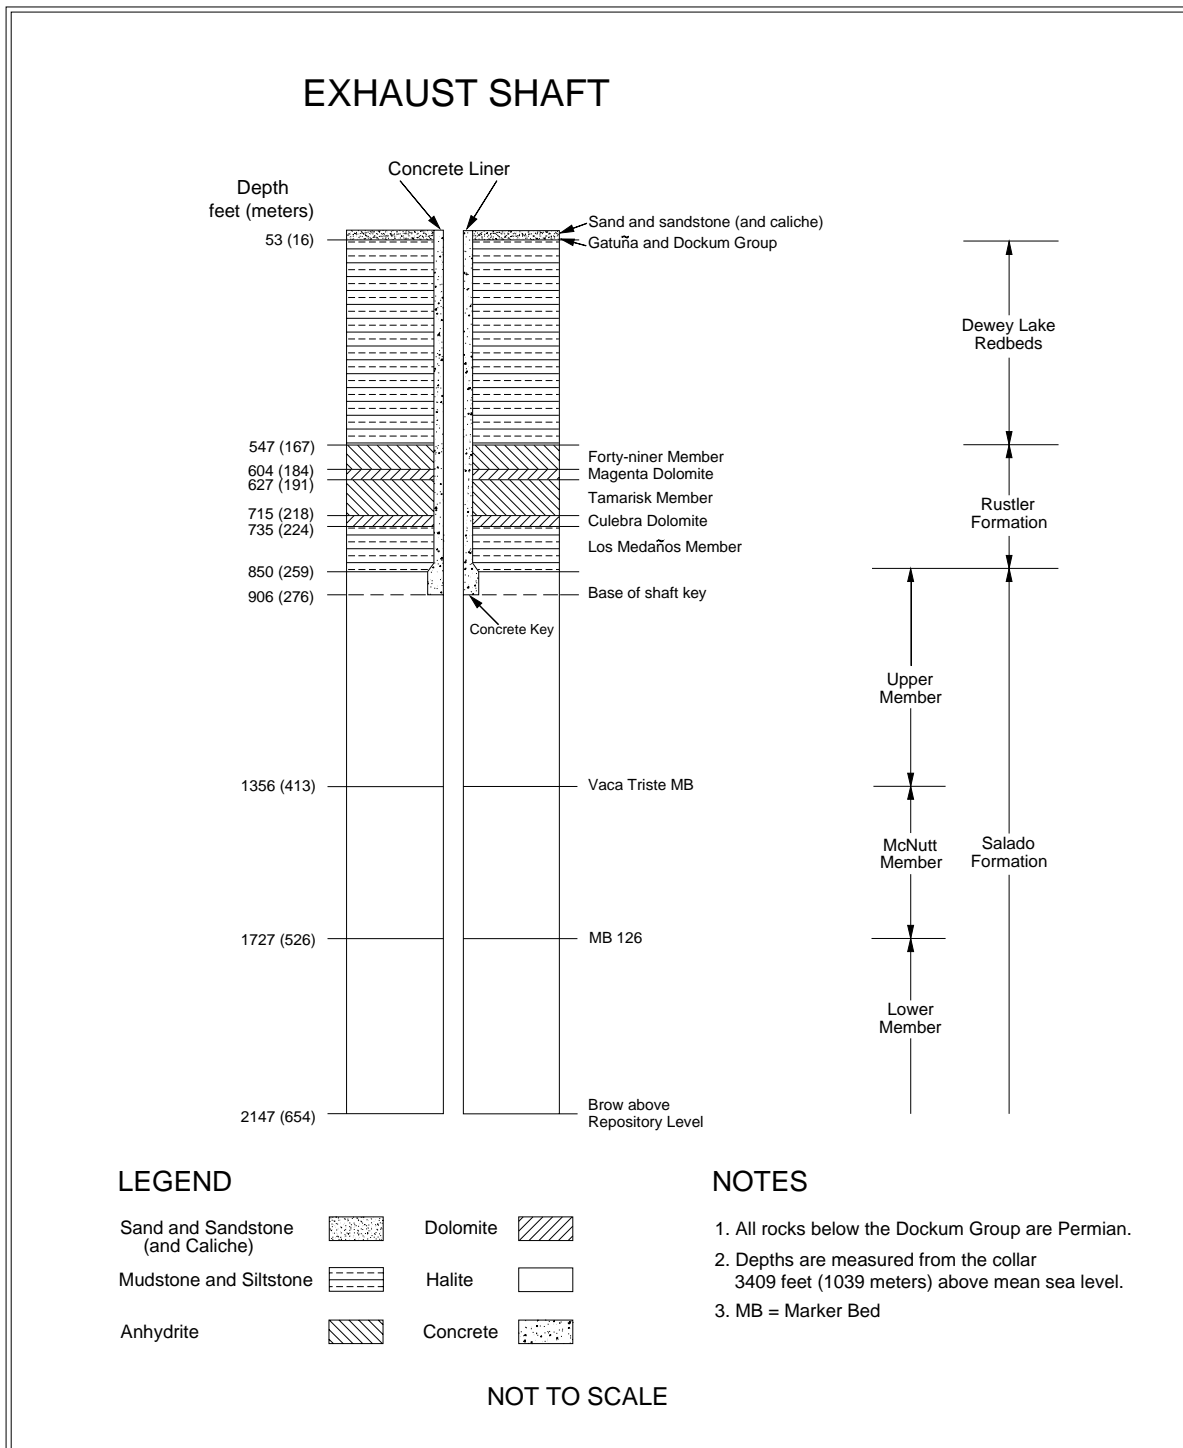


Figure 3-7 – Exhaust Shaft Stratigraphy


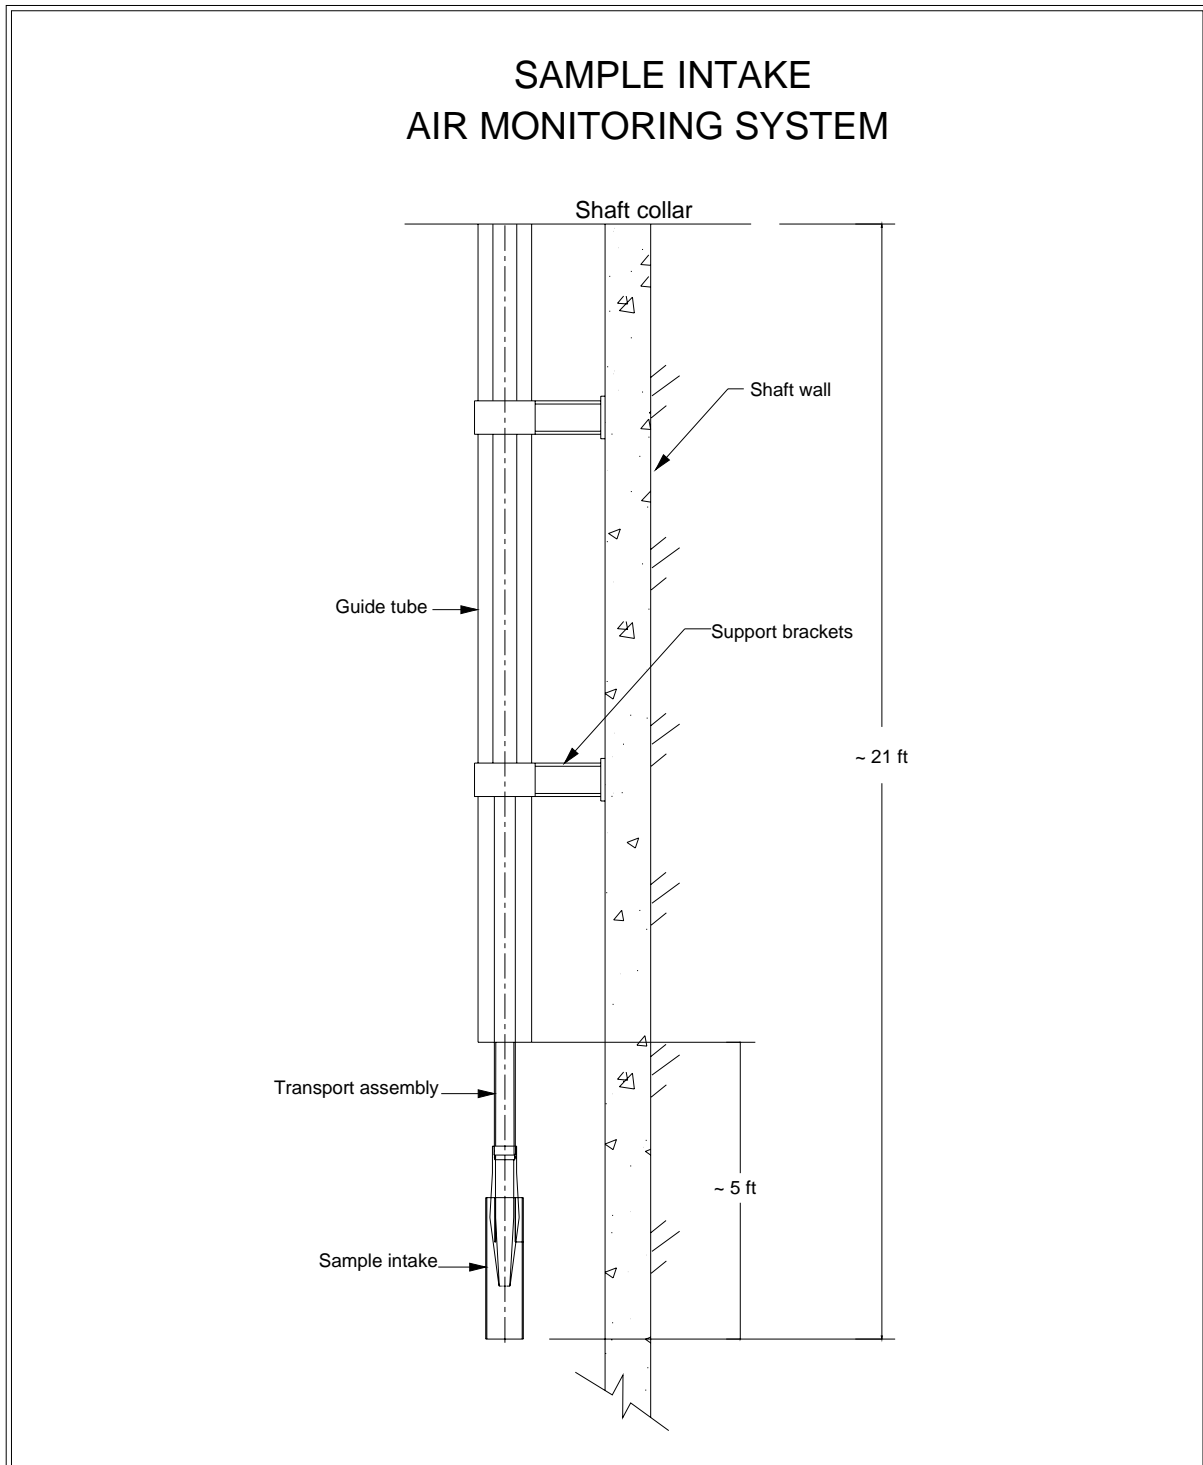


Figure 3-8 – Sample Intake of Exhaust Shaft Air Monitoring System

DIAGRAM OF EXHAUST SHAFT FIXTURES (200' UPPER PORTION)

Exhaust Shaft "unrolled" looking North

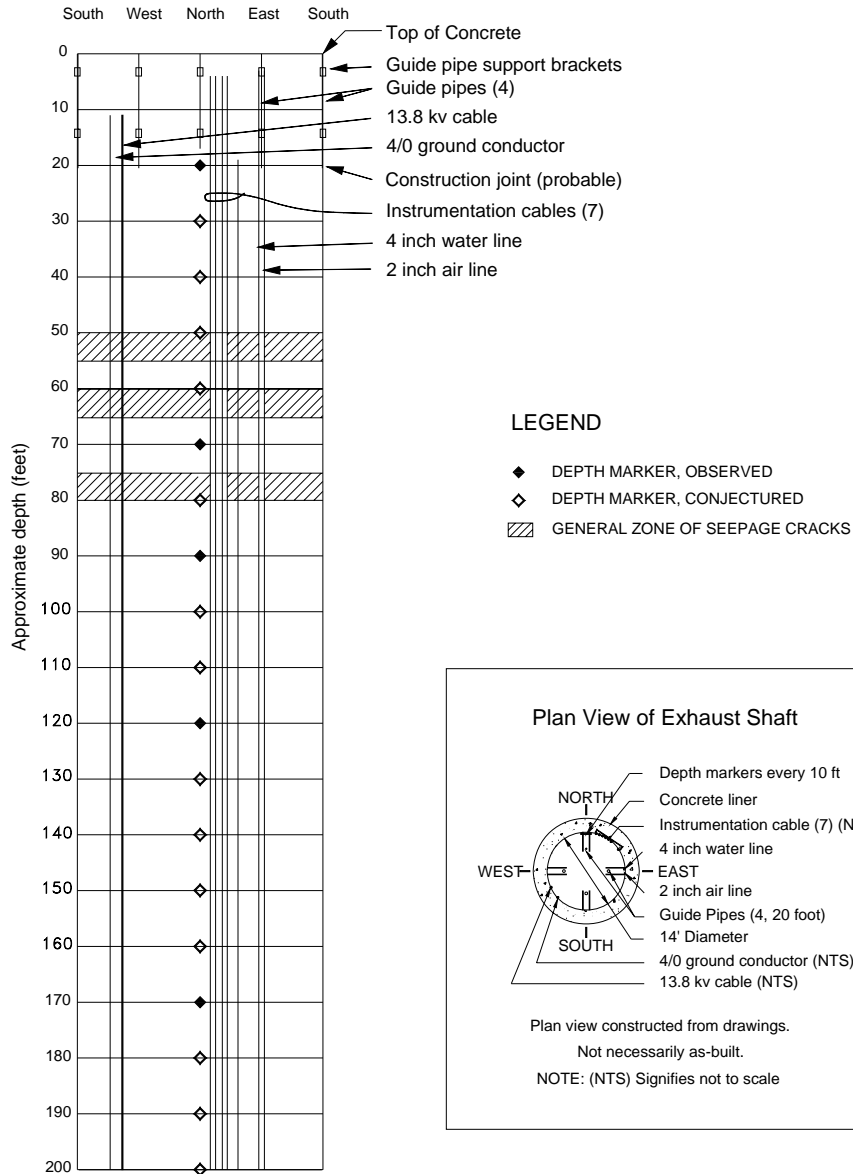

NOT TO SCALE

Figure 3-9 – Diagram of Exhaust Shaft Fixtures and Seepage Zones (Upper 200 ft)

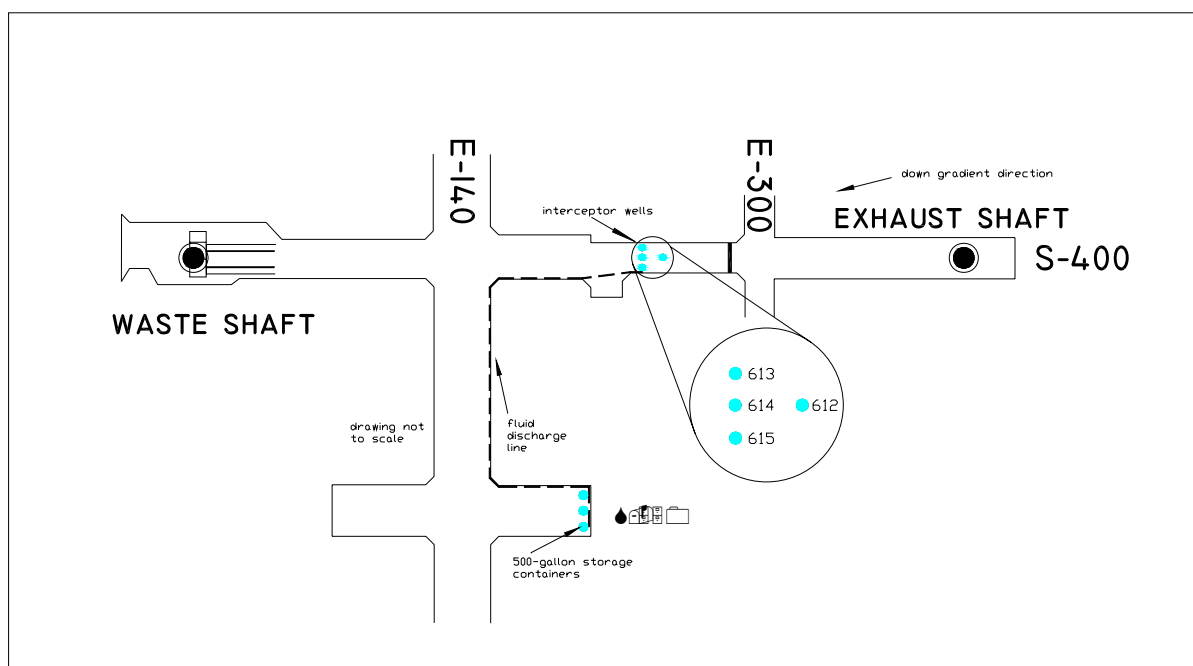


Figure 3-10 – Location of Interception Wells and Storage Containers

Table 3-1 presents the volume of fluid removed from the catch basin from July 1997 through June 2006, and by the interception well system from July 2006 through June 2007. The largest reported volumes are typically associated with periods of reduced ventilation and increased humidity. For a discussion of the factors affecting the quantity of fluid produced in the Exhaust Shaft, refer to DOE/WIPP 00-2000, *Brine Generation Study*.

The shaft walls were examined for salt buildup, cracks, moisture, and encrustations, with particular attention paid to power cables, instrument cables, air lines and waterlines and the three water rings at the base of the Magenta and Culebra members of the Rustler Formation and the bottom of the shaft key. The condition of the shaft wall varies depending on airflow, humidity, temperature, and underground mining activities. During this reporting period, there was significant mining activity in Panel 5 and the south access drifts. The principal areas in the shaft with significant salt buildup were the three water rings at the Magenta, the Culebra, and the key, and along upper portions of the shaft generally associated with power cables, support brackets, instrument cables, and the air lines and waterlines.

Though the Magenta and Culebra water rings are encrusted with salt buildup, no water appears to emanate from the liner or water rings. Most of the seepage was observed along the east face of the shaft wall near the instrumentation cables and the air lines and waterlines in the upper section of the shaft. Though the presence of water is an inconvenience requiring periodic disposal, at this time it does not appear to have created any hazard or affected the structural integrity of the shaft. However, brine increases the probability of corrosion and deterioration of utility hangers and brackets. There are no visible signs of dissolution of the salt below the key.

The video inspection also focused on the installed utilities and support brackets. These include a 13.8 kVA power cable that is no longer active and the grounding cable on the west wall of the shaft, the instrumentation cables on the northeast wall of the shaft, and the 4-in air-line and the 2-in waterline on the east wall of the shaft. In the August 19, 2006, video, salt buildups 6 to 12 in thick were noted surrounding the inactive power cable about 112 to 150 ft bsc. Later video inspections show that salt crust sloughing extended to about 135 ft bsc between the August and November inspections.

Sporadic salt buildup continues on all cables. The long-term implication of salt buildup is increased loading on cables and cable hangers, accompanied by intermittent falls of debris. The 4-in compressed air-line and the 2-in water-line extend from the surface to the bottom of the shaft. At present, neither line is being used. The integrity of the brackets holding the air-line and water-line was difficult to assess because of salt buildup; however, there was no indication that the brackets were broken. Instrumentation cable breaks were observed in the shaft; however, most of these breaks affected abandoned cables, with negligible impact on shaft monitoring and operations.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

Table 3-1 – Water Removed from the Exhaust Shaft Catch Basin and the Interception Well System

July 1997 - June 1998		July 1998 - June 1999		July 1999 - June 2000		July 2000 - June 2001		July 2001 - June 2002		July 2002 - June 2003	
Date	Gallons	Date	Gallons	Date	Gallons	Date	Gallons	Date	Gallons	Date	Gallons
7/18/1997	275	7/1/1998	770	7/19/1999	110	7/3/2000	220	7/31/2001	165	7/2/2002	165
7/28/1997	660	7/7/1998	330	12/13/1999	165	7/15/2000	110	8/21/2001	1,595	7/8/2002	440
8/1/1997	550	7/14/1998	220	2/21/2000	110	9/18/2000	330	9/13/2001	330	7/9/2002	495
8/4/1997	715	7/16/1998	275	5/16/2000	715	10/24/2000	110	10/15/2001	770	7/10/2002	660
8/8/1997	770	7/23/1998	165	6/7/2000	165	3/7/2001	110	10/30/2001	220	7/30/2002	220
8/11/1997	660	7/24/1998	220	6/12/2000	275	3/21/2001	165	4/29/2002	275	9/17/2002	165
8/15/1997	475	7/27/1998	825	6/19/2000	440	4/10/2001	220	6/11/2002	550	9/24/2002	330 Sludge
8/18/1997	330	7/28/1998	330	6/22/2000	330	4/17/2001	220	6/22/2002	330	3/25/2003	220 Sludge
8/22/1997	330	8/3/1998	495	6/30/2000	165	4/24/2001	110	TOTAL	4,235	5/27/2003	55
8/25/1997	1045	8/10/1998	1265	TOTAL	2,475	5/22/2001	110			6/3/2003	220
8/25/1997	110 Sludge	8/21/1998	330			5/22/2001	440 Sludge			6/25/2003	330
9/2/1997	220	8/24/1998	990			6/12/2001	1100			TOTAL	3,300
9/15/1997	605	8/27/1998	1155			6/13/2001	110				
9/22/1997	550	9/1/1998	330			6/13/2001	110				
10/13/1997	825	10/5/1998	385			TOTAL	3,025				
10/20/1997	220	10/26/1998	660								
11/3/1997	275	11/23/1998	110								
11/10/1997	385	2/1/1999	385								
11/17/1997	385	2/10/1999	110								
11/24/1997	330	5/4/1999	330								
12/10/1997	440	5/11/1999	110								
12/12/1997	550	5/24/1999	605								
1/2/1998	220	5/26/1999	165								
1/12/1998	605	5/28/1999	165								
2/2/1998	660	6/1/1999	165								
2/16/1998	605	6/4/1999	165								
3/16/1998	605	6/10/1999	165								
5/4/1998	660	6/10/1999	165 Sludge								
5/11/1998	550	6/16/1999	165								

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

Table 3-1 – Water Removed From the Exhaust Shaft Catch Basin and the Interception Well System (Continued)

July 1997 - June 1998		July 1998 - June 1999		July 1999 - June 2000		July 2000 - June 2001		July 2001 - June 2002		July 2002 - June 2003	
Date	Gallons	Date	Gallons	Date	Gallons	Date	Gallons	Date	Gallons	Date	Gallons
5/18/1998	495	6/21/1999	1,705								
5/20/1998	110	6/23/1999	275								
6/1/1998	330	6/30/1999	605								
6/10/1998	90	TOTAL	14,135								
6/15/1998	385										
6/22/1998	165										
TOTAL	16,185										

July 2003 - June 2004		July 2004 - June 2005		July 2005 - June 2006		July 2006 - June 2007					
Date	Gallons	Date	Gallons	Date	Gallons	Date	Gallons				
7/8/2003	605	11/29/2004	660 Sludge	8/1/2005	1,100	7/11/2006	250				
7/9/2003	550	12/6/2004	275 Sludge	8/15/2005	880	8/116/2006	420				
7/17/2003	165	1/3/2005	440	10/10/2005	715 Sludge	8/17/2006	400				
8/12/2003	275	1/4/2005	220	TOTAL	2,675	9/1/2006	420				
10/14/2003	165	1/10/2005	385			9/7/2006	420				
10/20/2003	440	5/16/2005	660			9/18/2006	840				
10/21/2003	330	6/1/2005	660			11/10/2006	150				
11/23/2003	220	6/6/2005	220			11/15/2006	400				
11/23/2003	660 Sludge	6/20/2005	440			1/30/2007	310				
TOTAL	3,300	6/27/2005	220			5/11/2007	75				
		TOTAL	4,180			6/20/2007	200				
						TOTAL	3,885				

3.3.2 Instrumentation

The Exhaust Shaft was equipped with geomechanical instrumentation in two stages. Earth pressure cells were installed behind the liner key in November 1984. Piezometers and nine multiposition borehole extensometers were installed during November and December 1985. Figures 3-11 and 3-12 show the instrument locations.

Nine piezometers remain in working condition. The fluid pressure readings from the working piezometers at the end of the reporting period range from -2 psi (-14 kPa) at 544-ft (166-m) to 141 psi (972 kPa) at 721-ft (220-m). Maximum pressure readings from the working piezometers during this reporting period were consistent with maximum readings from the previous reporting period.

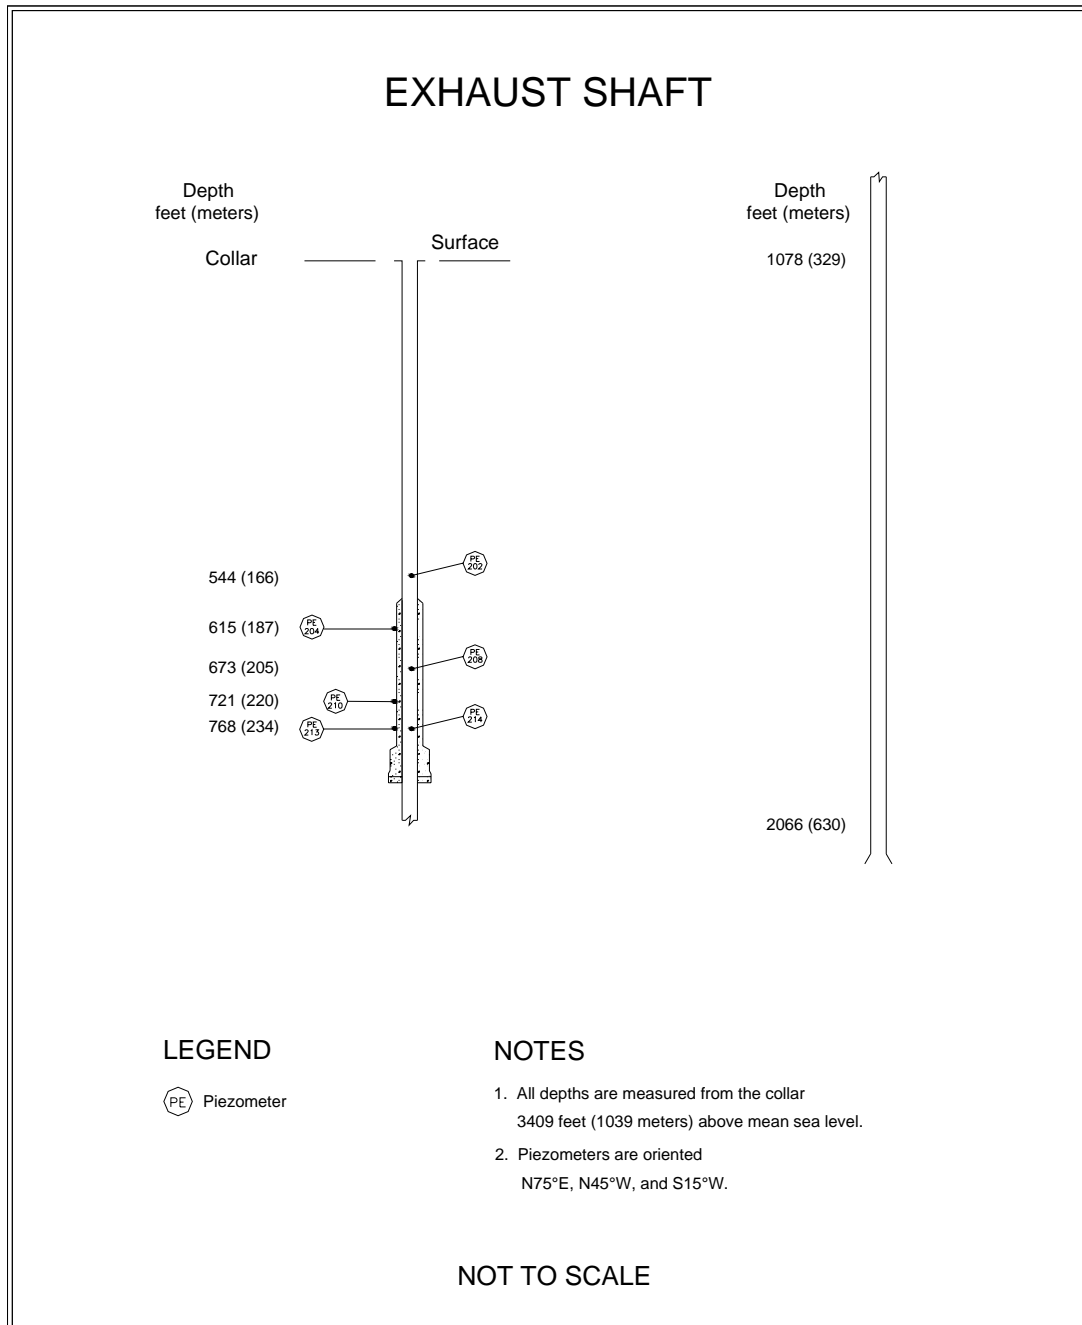


Figure 3-11 – Exhaust Shaft Instrumentation (Without Shaft Key)

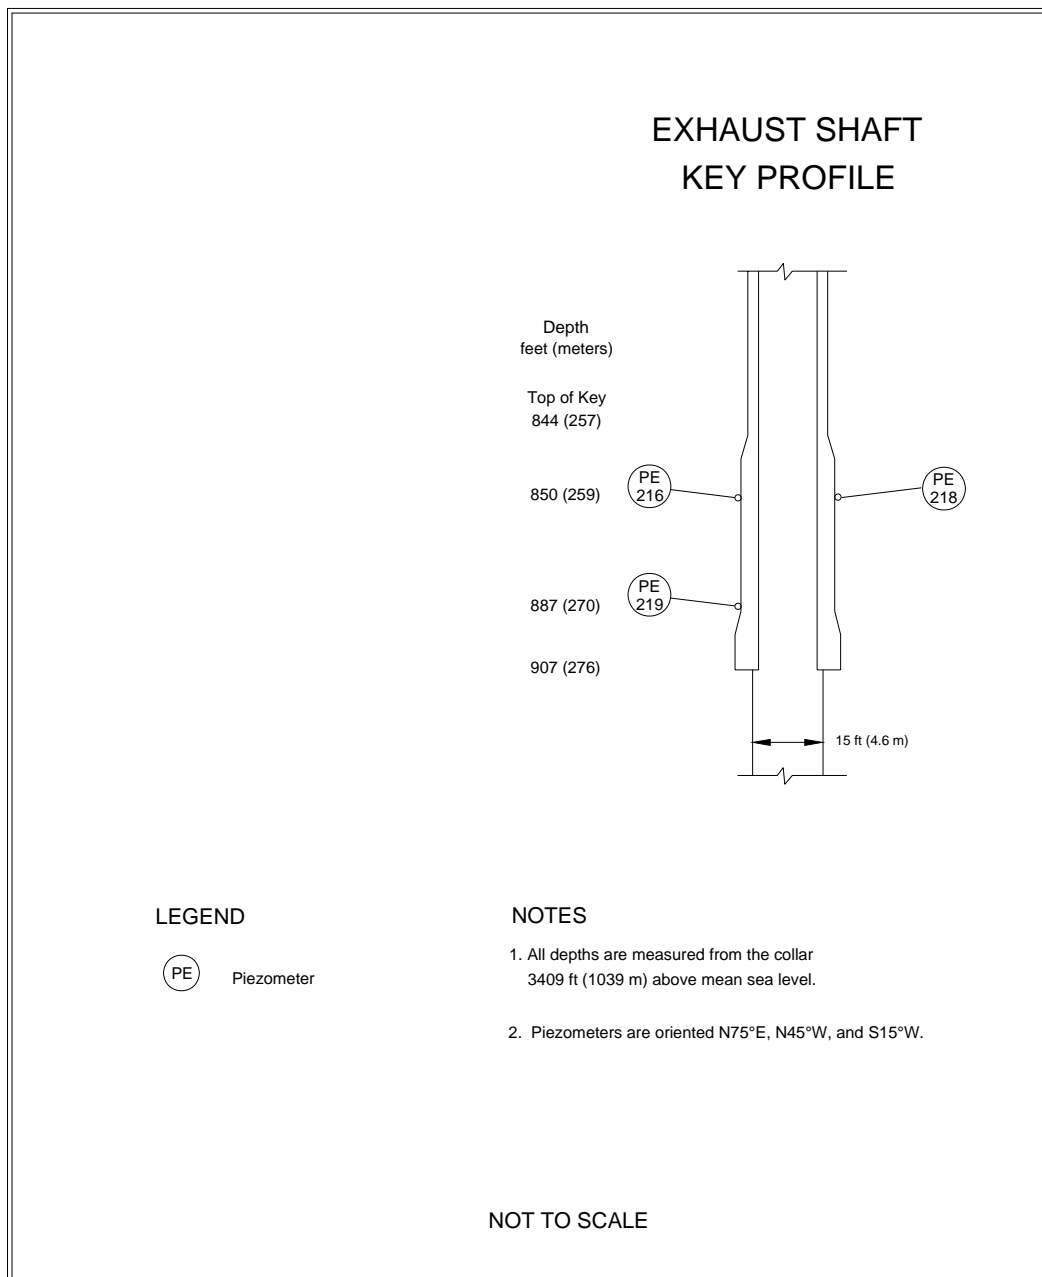


Figure 3-12 – Exhaust Shaft Key Instrumentation

3.4 Air Intake Shaft

The Air Intake Shaft was drilled from December 4, 1987, to August 31, 1988, to establish a primary route for surface air to enter the repository (see Figure 1-2). The stratigraphy was mapped from September 14, 1988, to November 14, 1989 (Holt and Powers, 1990). Figure 3-13 summarizes the Air Intake Shaft stratigraphy.

The Air Intake Shaft is lined with non-reinforced concrete from the surface to the bottom of the shaft key at 903 ft (275 m). The Air Intake Shaft key is 81 ft (25 m) long with an

inside diameter of 16 ft (5 m). The shaft diameter below the key is 20 ft (6 m), and the shaft below the key is unlined to the facility horizon at 2,150 ft (655 m). The shaft walls are bolted and meshed from just below the key all the way down to the shaft station. The Air Intake Shaft has no sump.

3.4.1 Shaft Performance

Weekly visual inspections were performed on the Air Intake Shaft during this reporting period, and the shaft was found to be in satisfactory condition. No ground control activities other than routine maintenance were required during this reporting period.

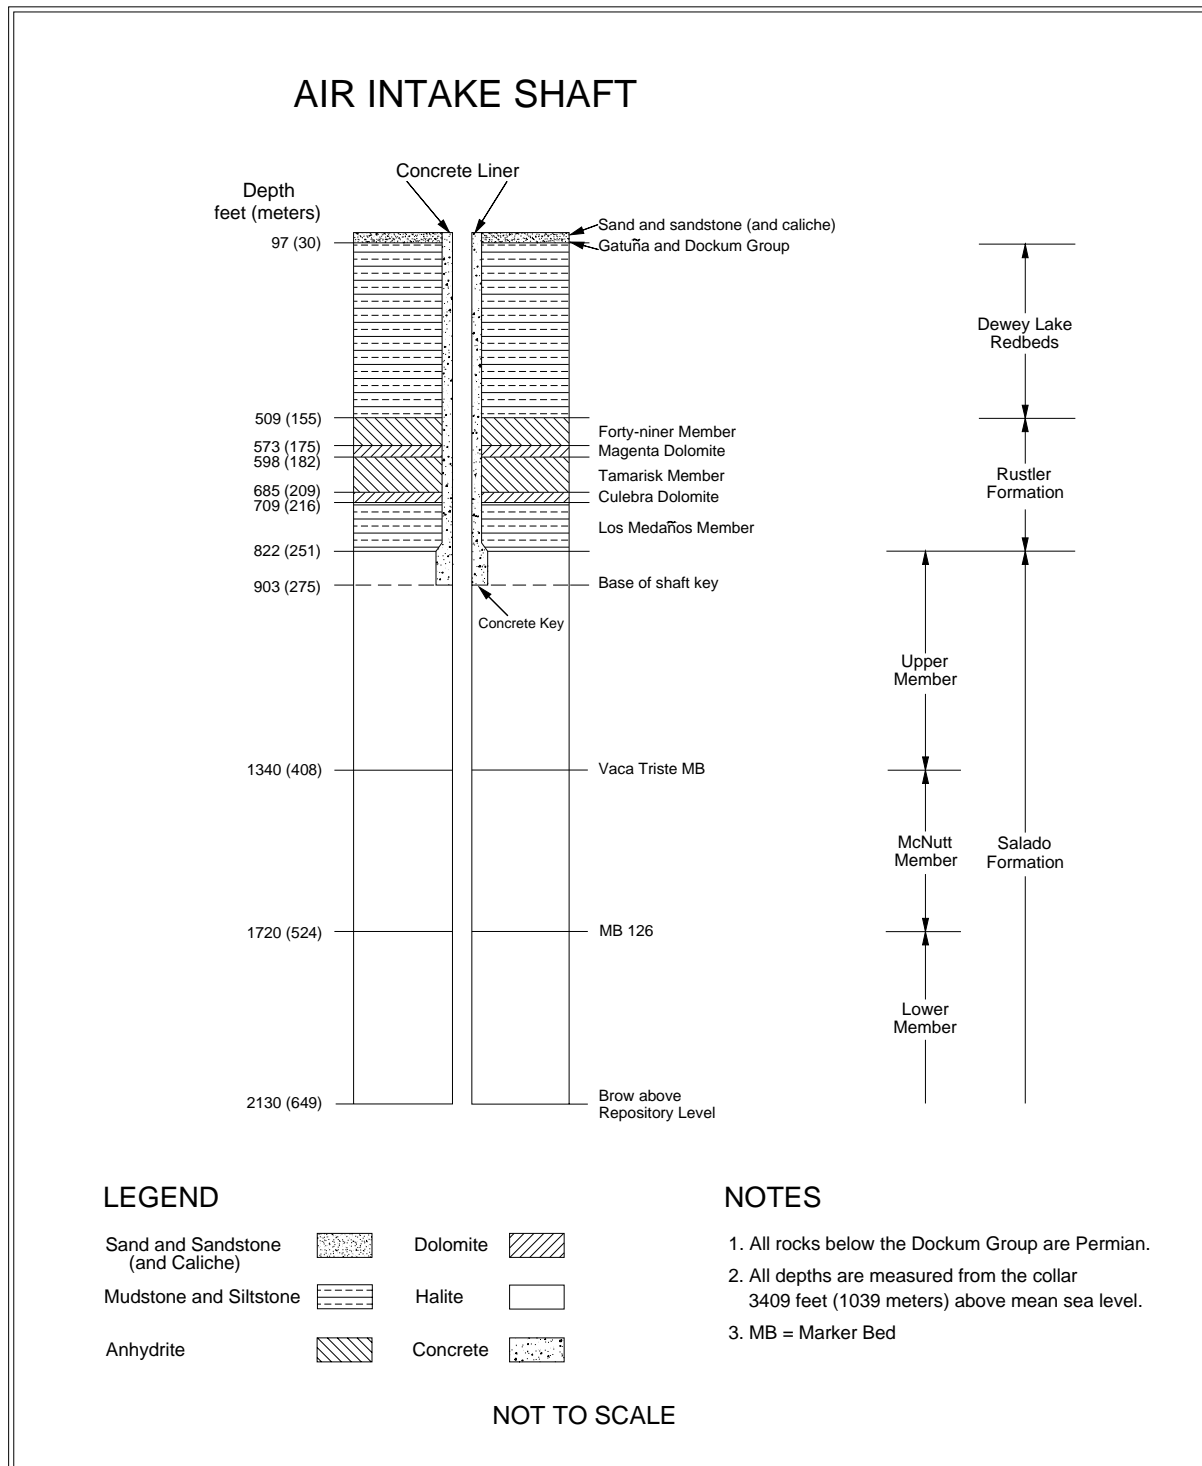


Figure 3-13 – Air Intake Shaft Stratigraphy

4.0 PERFORMANCE OF SHAFT STATIONS

This chapter describes the instrumentation and geomechanical performance of the shaft stations at the base of the Salt Shaft, the Waste Shaft, and the Air Intake Shaft. The Exhaust Shaft does not have an enlarged shaft station and, therefore, is not included in this chapter.

4.1 Salt Shaft Station

The Salt Shaft Station was excavated by drilling and blasting between May 2 and June 3, 1982. In 1987 the station was enlarged by removing the roof beam up to Anhydrite "b" between S-90 and N-20 using a mechanical scaler. In 1995, the remaining roof beam at the north end of the station was also removed up to Anhydrite "b". The station area south of the shaft is 90 ft (27.5 m) long and 32 to 38 ft (10 to 12 m) wide. The height of the station south of the shaft is 18 ft (5.5 m). The station dimensions north of the shaft are approximately 30 ft (9 m) long, 32 to 35 ft (10 to 11 m) wide, and 18 ft (5.5 m) high. The shaft extends approximately 140 ft (43 m) below the facility horizon to accommodate the skip loading equipment and to act as a sump. Figure 4-1 shows a generalized cross section of the station.

4.1.1 Modifications to Excavation and Ground Control Activities

No significant modifications were performed in the Salt Shaft Station during this reporting period. Ground control was performed as routine maintenance.

4.1.2 Instrumentation

Geomechanical instrumentation was installed in the Salt Shaft Station between June 1982 and February 1983, with subsequent reinstallation of extensometers and convergence points as necessary. Figure 4-2 shows the instrument locations after the roof beam was taken down.

Four vertical convergence point arrays are currently monitored. Table 4-1 summarizes the vertical closure rates in the Salt Shaft Station from July 2006 through June 2007. Salt Shaft Station vertical closure rates indicate that the rates are slightly higher than during the previous reporting period.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

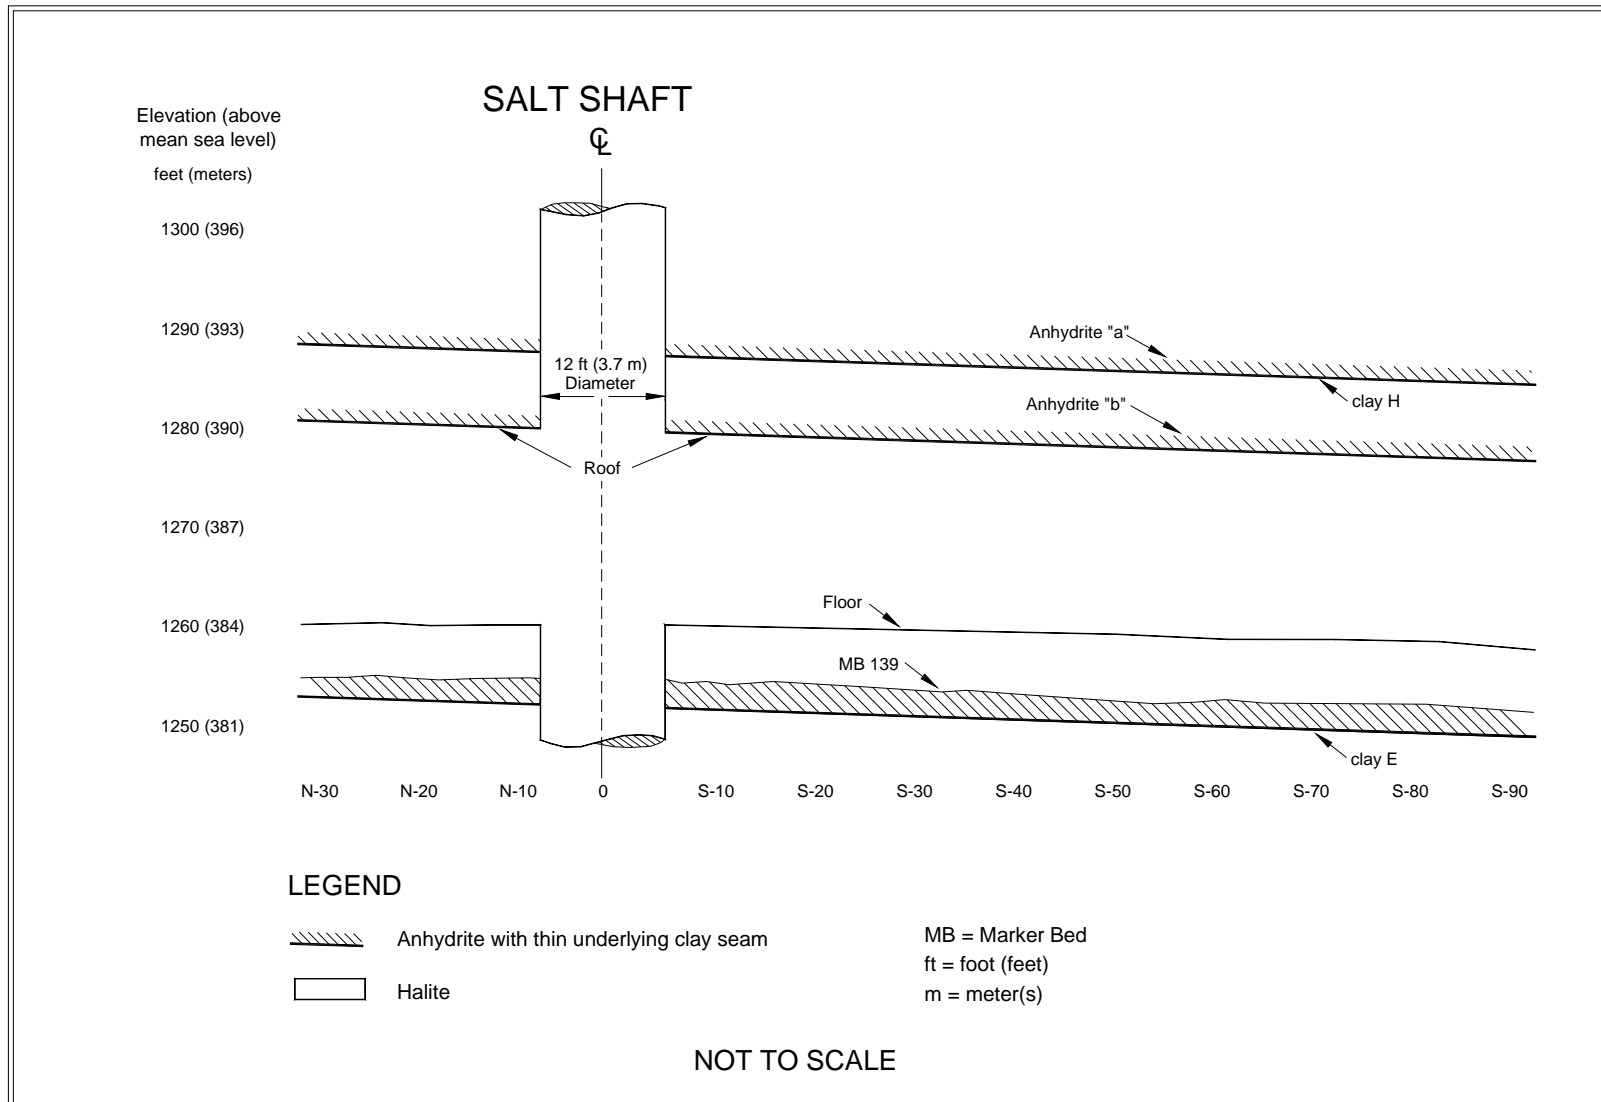


Figure 4-1 – Salt Shaft Station Stratigraphy

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

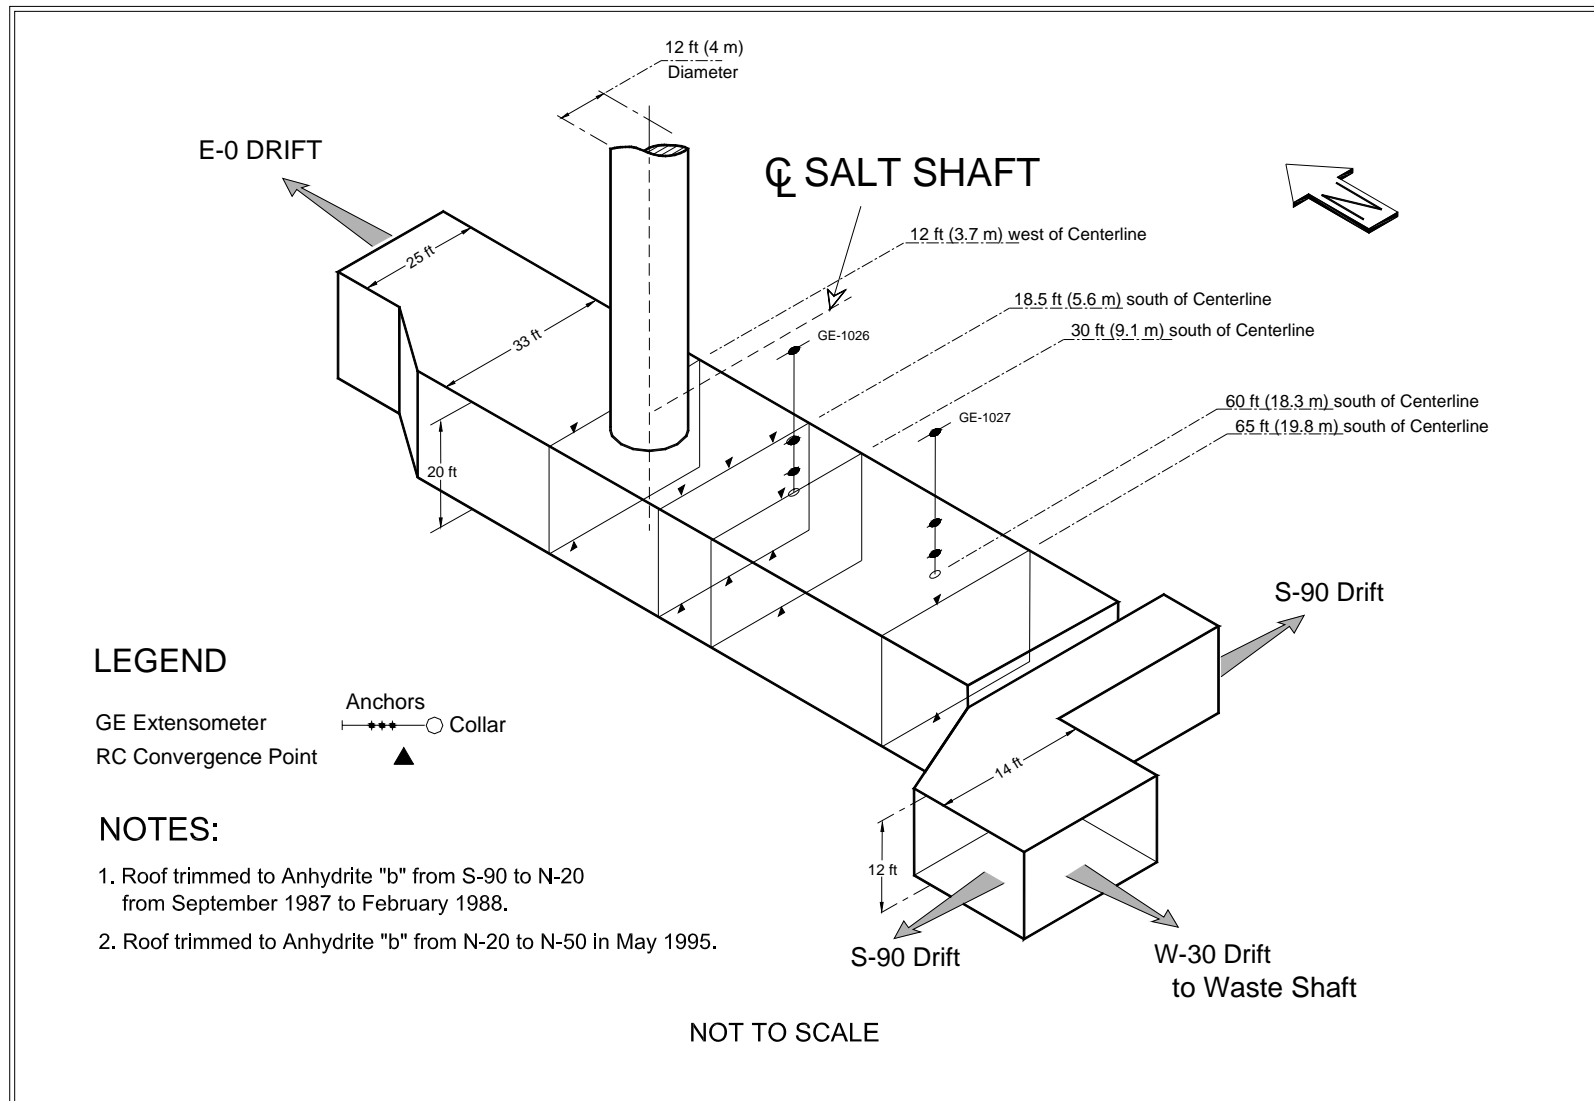


Figure 4-2 – Salt Shaft Station Instrumentation after Roof Beam Excavation

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

Table 4-1 – Vertical Closure Rates in the Salt Shaft Station

Location	Chord [*]	Last Reading	Total Cumulative Displacement Inches (cm.)	Closure Rate 2006 to 2007 in/yr (cm/yr)	Closure Rate 2005 to 2006 in/yr (cm/yr)	Rate Change Percent ^a	Comments
E0, S18	A-E	06/11/07	31.063 (78.900)	1.51 (3.84)	1.36 (3.45)	11	
E0, S18	B-D	06/11/07	31.703 (80.526)	1.64 (4.17)	1.50 (3.81)	9	
E0, S18	F-H	06/11/07	20.075 (50.991)	1.03 (2.62)	0.95 (2.41)	8	
E0, S30	A-C	06/11/07	45.699 (116.075)	1.55 (3.94)	1.46 (3.71)	6	
E0, S65	A-C	06/11/07	40.716 (103.419)	1.15 (2.92)	1.02 (2.59)	13	

^{*} Chord is defined in "Geotechnical Analysis Report for July 2006–June 2007 Supporting Data."

^a Increase in convergence rate is calculated from the difference between the 2006–2007 rate and the 2005–2006 rate.

4.2 Waste Shaft Station

The Waste Shaft Station was initially excavated with a continuous miner as a ventilation connection to a 6-ft (2-m) diameter exhaust shaft in November 1982. In 1984, the station was enlarged to a height of 15 to 20 ft (4.5 to 6 m) and a width of 20 to 30 ft (6 to 9 m). The station is approximately 150 ft (46 m) long. In 1988, the station walls were trimmed, and concrete was placed on the floor. Since 1988, the Waste Shaft Station has undergone three major floor renovations. A 53-ft (16-m)-long section of the reinforced concrete was removed in February 1991, in 1995 an additional 30-ft (9-m) section was removed, and in 2000 floor maintenance included trimming of the floor and reinstallation of the rails supported by segmented concrete panels on a crushed rock backfill. Figure 4-3 shows a cross-section of the Waste Shaft Station.

4.2.1 Modifications to Excavation and Ground Control Activities

Bolt tails were trimmed, and some cable shoe anchors were replaced to provide additional operating clearance for waste handling operations.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

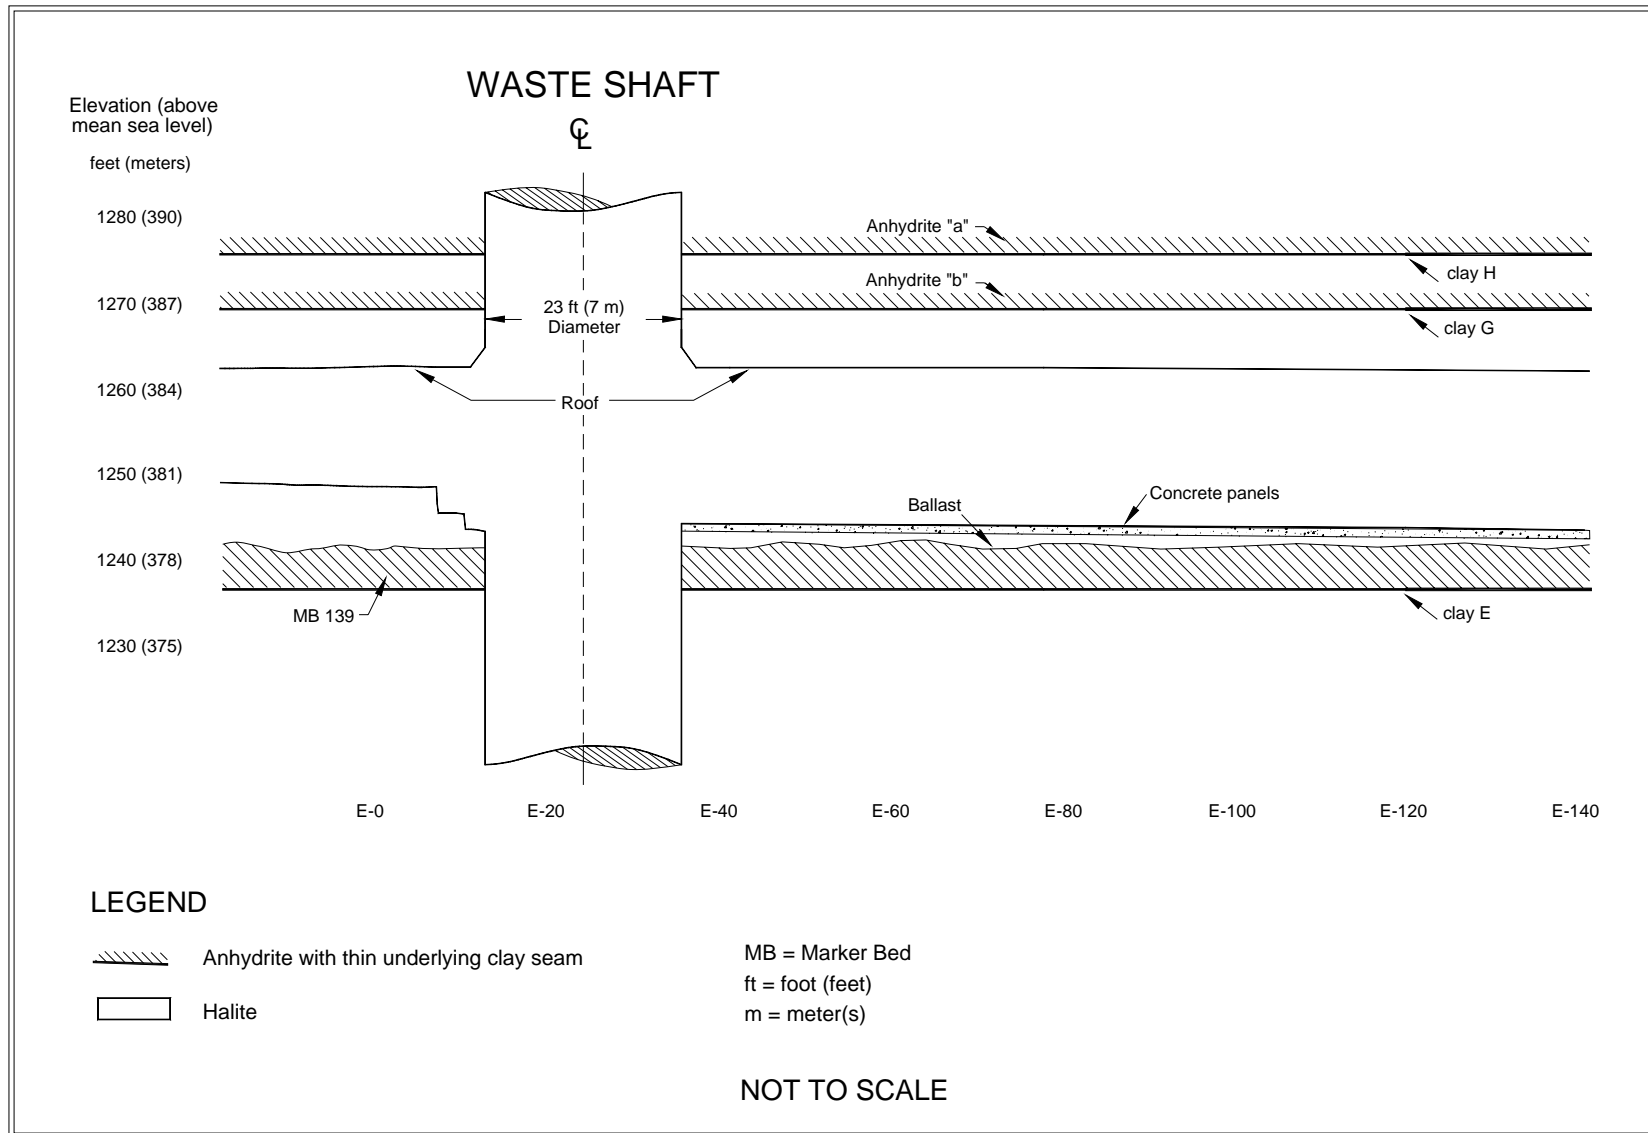


Figure 4-3 – Waste Shaft Station Stratigraphy

4.2.2 Instrumentation

Instruments were initially installed in the Waste Shaft Station between November 12 and December 2, 1982. Figure 4-4 illustrates the locations after enlargement. Three extensometers in the Waste Shaft Station are currently being monitored. In addition, horizontal convergence is being monitored at E-30 and E-90.

Table 4-2 summarizes the recent history of the roof extensometers in the Waste Shaft Station. Extensometer 51X-GE-00268 (W-30) is installed in a borehole drilled into the roof of the station. Extensometers 51X-GE-00356 and 51X-GE-00357 monitor fracture dilation along the shaft wall above the east brow.

Table 4-2 – Summary of Roof Extensometers in Waste Shaft Station

Instrument	Location	Last Reading	Collar Displacement Relative to Deepest Anchor in (cm)	Displacement Rate 2006 to 2007 in/yr (cm/yr)	Displacement Rate 2005 to 2006 in/yr (cm/yr)	Rate Change Percent ^a	Comments
51X-GE-00268	S400, W30	06/11/07	9.383 (23.833)	0.25 (0.64)	0.28 (0.71)	-11%	
51X-GE-00356	Waste Shaft Brow	06/25/07	0.233 (0.592)	0.08 (0.20)	0.08 (0.20)	0%	
51X-GE-00357	Waste Shaft Brow	05/05/07	0.509 (1.293)	0.20 (0.51)	0.20 (0.51)	0%	

^a Change is calculated from the difference between the 2006–2007 rate and the 2005–2006 rate.

Table 4-3 summarizes the annual horizontal closure rates calculated from convergence point data for this reporting period. The data indicate an increase in the horizontal closure rates at both E-30 and E-90 of 11 percent relative to the previous annual closure rates.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

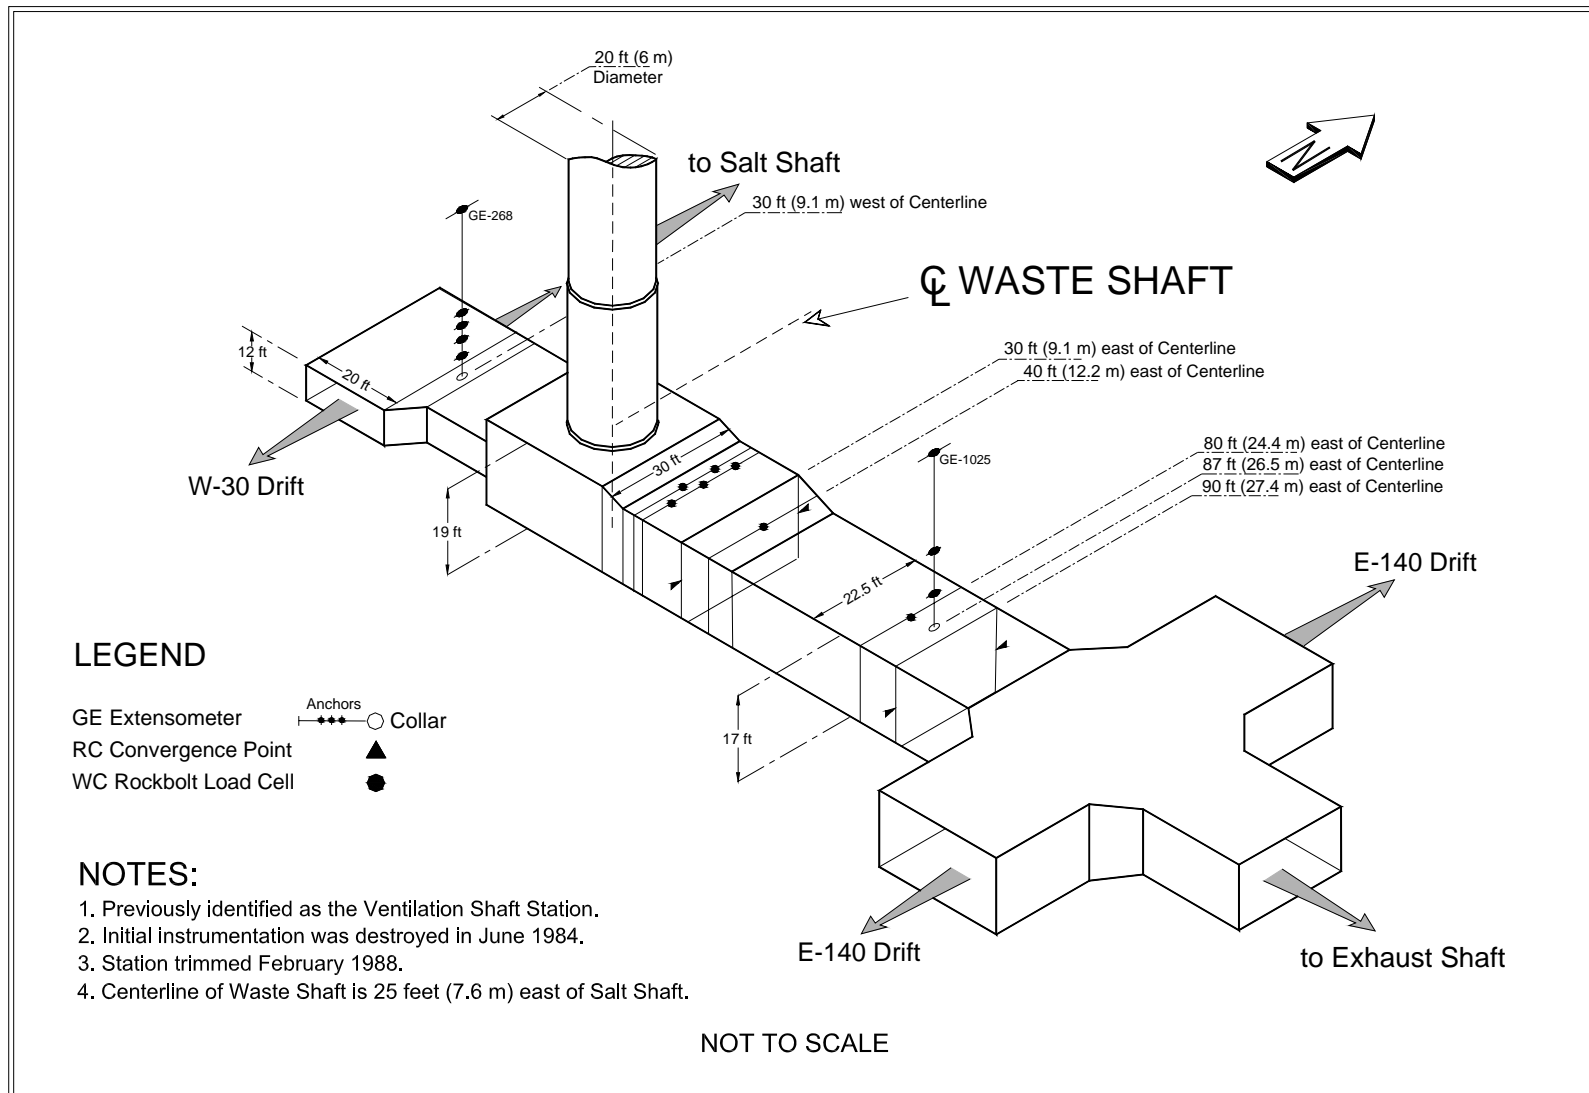


Figure 4-4 – Waste Shaft Station Instrumentation after Wall Trimming

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

Eighteen rock bolt load cells are installed in the roof and brow of the Waste Shaft Station. The loads on 12 of these rock bolt load cells are monitored regularly. Ten load cells are used to monitor loading on the brow cable support anchor shoes. Load cells at E-40 and E-80 are used to monitor the performance of the threaded bar anchorage.

Table 4-3 – Horizontal Closure Rates in the Waste Shaft Station

Location	Chord [*]	Last Reading	Total Cumulative Displacement Inches (cm)	Closure Rate 2006 to 2007 in/yr	Closure Rate 2005 to 2006 in/yr	Rate change Percent ^a	Comments
S400, E30	C-H	05/29/07	19.238 (48.865)	0.91 (2.31)	0.82 (2.08)	11%	
S400, E90	C-G	05/29/07	21.980 (55.829)	1.05 (2.67)	0.95 (2.41)	11%	

^{*}Chord is defined in "Geotechnical Analysis Report for July 2006–June 2007 Supporting Data."

^a Increase in convergence rate is calculated from the difference between the 2006–2007 rate and the 2005–2006 rate.

4.3 Air Intake Shaft Station

The Air Intake Shaft Station was excavated in late 1987 and early 1988, using a continuous miner. The Air Intake Shaft is furnished with a work platform and a small cage that can be raised and lowered to perform routine ground maintenance. The principal purpose of that equipment is to provide emergency access.

4.3.1 Modifications to Excavation and Ground Control Activities

No ground control activities were performed in the Air Intake Shaft Station other than routine roof and rib maintenance and replacement of failed roof bolts.

4.3.2 Instrumentation

Radial convergence point and extensometer instrumentation data near the Air Intake Shaft Station are presented in Chapter 5.0 as part of the discussion on the performance of the access drifts. Twenty rock bolt load cells installed in the Air Intake Shaft Station area are monitored regularly.

5.0 PERFORMANCE OF ACCESS DRIFTS

This chapter describes the geomechanical performance of the central underground access drifts. The Waste Disposal Area is discussed in Chapter 6.0. Four major north-south drifts in the WIPP underground are intersected by shorter east-west cross-drifts. Drift dimensions range from 13 ft (4 m) to 21 ft (6.4 m) high and from 14 ft (4.3 m) to 33 ft (9.2 m) wide.

5.1 Modifications to Excavation and Ground Control Activities

Access drifts into Panel 5 were completed during this reporting period. Trimming, scaling, and floor milling activities were performed as necessary in many areas. Table 5-1 summarizes these activities. It also summarizes ground control activities (e.g., rock bolting and installing wire mesh) in various locations in the access drifts.

5.2 Instrumentation

This section discusses instrumentation details and locations for each instrumentation type.

5.2.1 Borehole Extensometers

One new extensometer was installed during this reporting period in the E-300 North Experimental Area. This extensometer replaced a similar installation in the same location. All operating underground extensometers continue to be monitored. Thirty-seven borehole extensometers continue to be monitored.

5.2.2 Convergence Points

Figure 5-1 shows typical convergence point array configurations. Instrumentation installed during this reporting period was limited to the replacement of convergence point arrays in previously mined areas and the installation of new monitoring arrays in the newly mined areas. New and replacement convergence points were installed in 30 locations throughout the WIPP underground access drifts because of mining and trimming activities. Horizontal and vertical convergence point arrays were installed at various locations. Most of these installations were located in the southern access drifts. Convergence points within the access drifts are read manually at least every two months, with more frequent monitoring in some areas. Table 5-2 lists the new and replacement convergence points that were installed during this reporting period.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

**Table 5-1 – Summary of Modifications and Ground Control Activities in the
Access Drifts July 1, 2006, through June 30, 2007**

Location	Work Activity
E140 Drift	Trimmed floor between S400 and approximately S600. Trimmed floor between S90 and N260. Installed supplemental 12-ft resin-anchored bolts and mats between existing mats from S2520 to S2750. Installed supplemental 12-ft resin-anchored bolts and mats between existing mats from S2180 to S2520.
E300 Drift Maintenance Shop Area	Installed double lanyards on resin-anchored bolts to reduce the risk of broken bolts falling. Trimmed floor in maintenance shop between E140 and E300.
E300 Experimental Area (N1100 – N1400)	Installed 12-ft resin-anchored bolts and mats.
S400 Drift Shaft Station Area	Trimmed excess bolt tails to provide additional working height for RH operations in the station. Replaced large existing cable shoes with lower profile cable anchor shoes.
N1400	Installed 4-ft mechanically anchored bolts and chain-link mesh in alcove east of E300.
S90	Installed 4-ft mechanically anchored bolts and chain-link mesh on ribs.
S1300 Shop Area	Installed 4-ft mechanically anchored bolts and chain link mesh on roof and ribs.
S2750	Installed substantial and isolation barriers in Panel 3 access.
S3080	Installed substantial and isolation barriers in Panel 3 access.
W30 Drift	Installed 12-ft resin-anchored bolts and mats to support the brow at S2650.
W170 Drift	Installed 12-ft resin-anchored bolts and mats at the S2900 truck bypass. Installed 12-ft resin-anchored bolts and mats to support the ramp area brow at S2650.

**Table 5-2 – New and Replaced Convergency Points Installed in the
Access Drifts July 1, 2006, through June 30, 2007**

Location	N/R	Field Tag#	Chord	Date Installed
E140, N150	R	E140-N150-4	A-C (Vertical)	09/15/06
E140, N220	R	E140-N220-3	A-C (Vertical)	09/27/06
E140, N355	R	E140-N355-2	A-C (Vertical)	09/27/06
E140, N5	R	E140-N5-6	A-C (Vertical)	09/15/06
E140, S1775	R	E140-S1775-3	I-E (Horizontal)	03/08/07
E140, S460	R	E140-S460-5	A-C (Vertical)	01/05/07
E140, S550	R	E140-S0550-5	A-C (Vertical)	01/05/07
E140, S90	R	E140-S90-4	A-C (Vertical)	09/15/06
E300, N1262	R	E300-N1262-3	A-C (Vertical)	06/22/07

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

**Table 5-2 – New and Replaced Convergency Points Installed in the
Access Drifts July 1, 2006, through June 30, 2007**

Location	N/R	Field Tag [#]	Chord [*]	Date Installed
E300, N170	R	E300-N170-2	H-F (Vertical)	09/27/06
E300, N170	R	E300-N170-2	A-E (Vertical)	09/27/06
E300, N250	R	E300-N250-3	A-C (Vertical)	10/31/06
E300, S3480	N	E300-S3480	A-C (Vertical)	09/14/06
E300, S3480	N	E300-S3480	B-D (Horizontal)	09/14/06
N250, E220	R	N250-E220-2	B-D (Horizontal)	09/27/06
N250, E220	R	N250-E220-2	A-E (Vertical)	09/27/06
N250, E220	R	N250-E220-2	H-F (Vertical)	09/27/06
S1300, W100	R	S1300-W100-3	A-C (Vertical)	09/14/06
S3310, W100	R	S3310-W100-3	A-C (Vertical)	01/19/07
S3650, E220	N	S3650-E220	A-C (Vertical)	10/19/06
S3650, E55	N	S3650-E55	A-C (Vertical)	10/27/06
W30, S120	R	W30-S120-2	A-C (Vertical)	12/14/06
W30, S250	R	W30-S250-5	A-C (Vertical)	12/14/06
W30, S400	R	W30-S400-2	A-C (Vertical)	12/14/06
W30, S500	R	W30-S500-2	A-C (Vertical)	12/14/06
W30, S700	R	W30-S700-3	A-C (Vertical)	12/14/06
W30, S700	R	W30-S700-4	A-C (Vertical)	01/05/07
W30, S850	R	W30-S850-2	H-F (Vertical)	01/05/07
W30, S850	R	W30-S850-3	B-D (Horizontal)	01/05/07
W30, S850	R	W30-S850-3	A-E (Vertical)	01/05/07

N = New installation.

R = Replacement installation (i.e., instrument replaces older instrument that has failed or has been mined out).

[#] This column is a combination of the convergence point location followed by a "-X", where X represents the reinstallation number, when applicable,

^{*} A unique letter is assigned to each convergence array element around a particular opening. Chord refers to a particular array pair. The various array lettering schemes are shown in Figure 5-1.

5.3 Analysis of Convergence Point and Extensometer Data

Convergence point data are obtained by measuring the change in distance between fixed points anchored into the rock across an opening, either from rib-to-rib or from roof-to-floor. Extensometer data are obtained by measuring the displacement from the reference head anchor (collar) to each fixed anchor of the extensometer. These measurements are made, at a minimum, every two months throughout the WIPP underground, except when convergence points are not accessible. Convergence rates and extensometer displacement rates indicate how an excavation is performing; rates that decrease or are relatively constant typify stable excavations, whereas increasing rates may indicate some type of developing instability or may be the response to nearby mining.

Where possible, annual closure rates were calculated from convergence point array data gathered in the access drifts. A complete tabulation of these convergence point data and calculated closure rates is presented in the supporting data document for this report. Locations with increases in annual vertical closure rates of greater than 10 percent are shown in Table 5-3.

TYPICAL CONVERGENCE POINT ARRAY CONFIGURATIONS

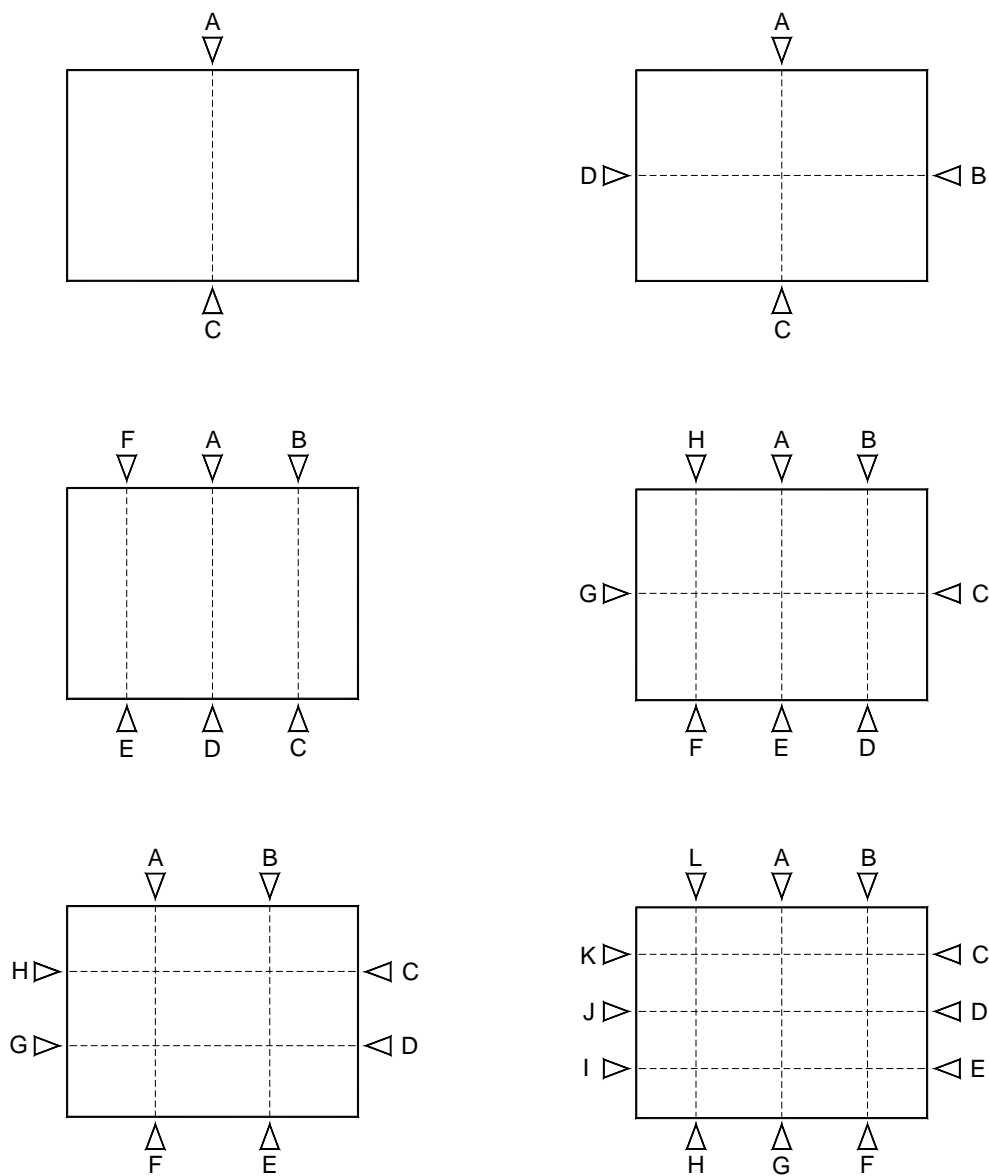


Figure 5-1 – Typical Convergence Point Array Configurations Showing Anchor Designations

Extensometer displacement rates and convergence rates are routinely plotted against time, and comparisons are made through time to identify any acceleration. Annual convergence rates are calculated by determining the difference between the first and last readings of the reporting period and dividing the difference by the time between the two readings (in years). Instruments that indicate acceleration are analyzed to determine the significance of the acceleration. Factors considered during the analysis include magnitude of the respective rates, percentage increase, convergence history, and any recent excavation in the vicinity.

Thirty-seven borehole extensometers continue to be monitored at various locations in the access drifts. Where displacement data were available, annual displacement rates were calculated for each active installation and compared to the annual displacement rates from the previous reporting period. Approximately 50 percent of the instruments are installed in the E-140 drift to monitor the waste transport route. Many of the E-140 extensometers indicate movement in the roof beam that may be attributed to shallow fracturing and the effects of anhydrite stringer separations in the roof. Lateral deformation in the roof beam may influence the extensometer readings causing an increase in the measured displacement. Although the borehole extensometer data indicate continued deformation and breakup of the lower beam, the roof bolt anchorage zone remains competent.

Further analysis of the convergence rate accelerations has shown many of them to be minor and generally related to roof beam fracturing. Other areas, such as the southern portions of the access drifts, had closure rate increases that can be directly attributed to the mining of Panel 5 and associated drifts.

Closure rates have increased in various locations by more than ten percent since the last reporting period. These locations are assessed in greater detail to determine the cause of the closure rate increase. Most of these locations are in the south access drifts near Panel 5. The increased rates were primarily observed in the W-170 and W-30 drifts. Increased closure rates were observed in E-140 from S-700 to S-1000 and from S-1300 to S-2750. They are probably caused by a combination of the effects of Panel 5 mining and continued ageing and deterioration of the roof beam.

The closure rates observed in E-140 from S-1300 to S-3080 are in an area where the roof beam has been mined to clay "G". The rate of increase in this area may be attributed to roof beam separations formed along shallow anhydrite stringers in the roof. These separations result in the formation of thin roof beams that can easily be deformed toward the opening. Tensile fractures generally develop on the roof surface in areas of maximum deformation.

The rate increases observed in other areas may be attributable to various reasons. The effect of nearby mining or significant trimming appears to have caused the rate increases in W-30 from S-90 to S-1000 and in E-140 from S-90 to N-250. Field observations in these areas do not indicate any significant deterioration that may have caused these increases.

Geotechnical Analysis Report for July 2006 – June 2007

DOE/WIPP-08-3177, Vol. 1

**Table 5-3 – Greater than 10 Percent Increases in Annual Vertical Convergence Rates
in the Access Drifts**

Location	Chord*	Last Reading Date	Cumulative Displacement Inches (cm.)	Closure Rate 2006 to 2007 in/yr (cm/yr)	Closure Rate 2005 to 2006 in/yr (cm/yr)	Rate Change Percent ^a	Comments
E0, N460	A-C	06/11/07	31.791 (80.75)	1.85 (4.70)	1.63 (4.14)	13	
E0, N626	A-C	06/11/07	50.175 (127.45)	2.04 (5.18)	1.78 (4.52)	15	
E140, N460	A-C	06/19/07	31.551 (80.14)	1.75 (4.45)	1.58 (4.01)	11	
E140, N220	A-C	06/19/07	27.548 (69.97)	2.29 (5.82)	1.41 (3.58)	62	Floor trimming.
E140, N150	A-C	06/19/07	21.068 (53.51)	2.56 (6.50)	1.05 (2.67)	144	Floor trimming.
E140, N5	A-C	06/19/07	33.677 (85.54)	2.34 (5.94)	1.24 (3.15)	89	Floor trimming.
E140, S90	A-C	05/31/07	18.871 (47.93)	1.58 (4.01)	1.13 (2.87)	40	Floor trimming.
E140, S460	A-C	05/29/07	44.064 (111.92)	2.07 (5.26)	1.75 (4.45)	18	
E140, S550	A-C	05/29/07	36.429 (92.53)	1.71 (4.34)	1.30 (3.30)	32	
E140, S1075	H-F	06/25/07	11.621 (29.52)	1.23 (3.12)	1.06 (2.69)	16	
E140, S1456	A-G	06/25/07	58.877 (149.55)	4.14 (10.52)	3.53 (8.97)	17	
E140, S1456	L-H	06/25/07	25.918 (65.83)	2.48 (6.30)	2.13 (5.41)	16	
E140, S2275	A-C	06/25/07	43.205 (109.74)	8.37 (21.26)	6.53 (16.59)	28	
E140, S2634	A-C	06/25/07	24.759 (62.89)	6.27 (15.93)	5.22 (13.26)	20	
E300, N170	H-F	06/08/07	21.038 (53.44)	1.40 (3.56)	1.26 (3.20)	11	
E300, N170	A-E	06/08/07	23.579 (59.89)	1.55 (3.94)	1.38 (3.51)	12	
E300, S45	A-E	06/08/07	19.495 (49.52)	1.15 (2.92)	1.04 (2.64)	11	
E300, S45	H-F	06/08/07	16.938 (43.02)	1.05 (2.67)	0.94 (2.39)	12	
E300, S45	B-D	06/08/07	16.093 (40.88)	1.16 (2.95)	0.95 (2.41)	22	
E300, S250	A-C	06/04/07	10.390 (26.39)	0.63 (1.60)	0.52 (1.32)	21	
E300, S850	A-E	04/09/07	13.385 (34.00)	0.48 (1.22)	0.43 (1.09)	12	
E300, S1150	A-E	04/09/07	15.015 (38.14)	0.60 (1.52)	0.53 (1.35)	13	
E300, S1150	B-D	04/09/07	10.669 (27.10)	0.42 (1.07)	0.35 (0.89)	20	
E300, S1150	H-F	04/09/07	10.235 (26.00)	0.43 (1.09)	0.36 (0.91)	19	
E300, S1450	A-C	06/04/07	6.610 (16.79)	0.71 (1.80)	0.64 (1.63)	11	
E300, S1687	A-C	06/04/07	6.919 (17.57)	0.84 (2.13)	0.76 (1.93)	11	
E300, S1775	A-C	06/04/07	6.404 (16.27)	0.71 (1.80)	0.62 (1.57)	15	
E300, S1862	A-C	06/04/07	6.781 (17.22)	0.80 (2.03)	0.71 (1.80)	13	
N140, E90	A-C	06/21/07	14.158 (35.96)	0.82 (2.08)	0.71 (1.80)	15	
N250, E220	H-F	06/08/07	19.509 (49.55)	1.47 (3.73)	1.06 (2.69)	39	Floor trimming.
N250, E220	A-E	06/08/07	25.342 (64.37)	2.37 (6.02)	1.48 (3.76)	60	Floor trimming.
S90, W400	A-C	11/29/06	14.534 (36.92)	0.74 (1.88)	0.58 (1.47)	28	
S90, W590	A-C	11/29/06	10.438 (26.51)	0.66 (1.68)	0.54 (1.37)	22	
S1300, E24	A-C	05/24/07	16.591 (42.14)	1.09 (2.77)	0.96 (2.44)	14	
S2750, E55	A-C	05/24/07	8.038 (20.42)	2.23 (5.66)	1.56 (3.96)	43	
S2750, W93	A-C	05/24/07	8.130 (20.65)	2.14 (5.44)	1.84 (4.67)	16	
S3080, E55	A-C	05/22/07	8.665 (22.01)	2.25 (5.72)	1.65 (4.19)	36	
S3080, W100	A-C	05/24/07	8.004 (20.33)	2.10 (5.33)	1.76 (4.47)	19	
S3310, E55	A-C	05/22/07	8.784 (22.31)	2.44 (6.20)	1.77 (4.50)	38	
S3310, W100	A-C	05/22/07	7.136 (18.13)	2.42 (6.15)	1.73 (4.39)	40	Nearby Panel 5 mining.
S3650, W100	A-C	05/21/07	3.261 (8.28)	2.29 (5.82)	1.51 (3.84)	52	Nearby Panel 5 mining.
W170, S850	B-D	05/14/07	12.392 (31.48)	0.58 (1.47)	0.49 (1.24)	18	

A unique letter is assigned to each convergence array element around a particular opening. Chord refers to a particular array pair.

The various array lettering schemes are shown in Figure 5-1.

^a Increase in convergence rate is calculated from the difference between the 2006–2007 rate and the 2005–2006 rate.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

**Table 5-3 – Greater than 10 Percent Increases in Annual Vertical Convergence Rates
in the Access Drifts (Continued)**

Location	Chord ^a	Last Reading Date	Cumulative Displacement Inches (cm)	Closure Rate 2006 to 2007 in/yr (cm/yr)	Closure Rate 2005 to 2006 in/yr (cm/yr)	Rate Change Percent ^a	Comments
W170, S850	H-F	05/14/07	11.333 (28.79)	0.51 (1.30)	0.43 (1.09)	19	
W170, S850	A-E	05/14/07	16.545 (42.02)	0.71 (1.80)	0.59 (1.50)	20	
W170, S1150	H-F	05/14/07	12.996 (33.01)	0.63 (1.60)	0.40 (1.02)	58	
W170, S1950	A-C	05/14/07	12.518 (31.80)	0.84 (2.13)	0.71 (1.80)	18	
W170, S2685	A-C	05/17/07	11.078 (28.14)	2.77 (7.04)	2.33 (5.92)	19	
W170, S2833	A-C	05/14/07	6.796 (17.26)	1.67 (4.24)	1.44 (3.66)	16	
W170, S2998	A-C	05/14/07	9.185 (23.33)	2.60 (6.60)	1.91 (4.85)	36	
W170, S3080	A-C	05/14/07	7.058 (17.93)	1.66 (4.22)	1.48 (3.76)	12	
W170, S3195	A-C	05/14/07	7.716 (19.60)	2.03 (5.16)	1.40 (3.56)	45	Nearby Panel 5 mining.
W170, S3310	A-C	05/14/07	8.644 (21.96)	3.52 (8.94)	1.38 (3.51)	155	Nearby Panel 5 mining.
W170, S3395	A-C	05/15/07	3.736 (9.49)	2.61 (6.63)	1.59 (4.04)	64	Nearby Panel 5 mining.
W170, S3480	A-C	05/15/07	4.110 (10.44)	2.91 (7.39)	1.73 (4.39)	68	Nearby Panel 5 mining.
W170, S3565	A-C	05/15/07	3.544 (9.00)	2.39 (6.07)	1.51 (3.84)	58	Nearby Panel 5 mining.
W170, S3650	A-C	05/21/07	4.680 (11.89)	3.22 (8.18)	1.21 (3.07)	166	Nearby Panel 5 mining.
W30, S120	A-C	06/11/07	20.687 (52.55)	1.13 (2.87)	0.88 (2.24)	28	Floor trimming.
W30, S250	A-C	06/11/07	26.835 (68.16)	1.30 (3.30)	0.84 (2.13)	55	Floor trimming.
W30, S400	A-C	06/11/07	18.383 (46.69)	1.04 (2.64)	0.73 (1.85)	42	Floor trimming.
W30, S500	A-C	06/11/07	23.164 (58.84)	1.23 (3.12)	0.73 (1.85)	68	Floor trimming.
W30, S700	A-C	06/11/07	30.182 (76.66)	1.68 (4.27)	0.86 (2.18)	95	Floor trimming.
W30, S850	A-E	06/11/07	17.903 (45.47)	0.98 (2.49)	0.58 (1.47)	69	Floor trimming.
W30, S850	B-D	06/11/07	12.229 (31.06)	0.73 (1.85)	0.38 (0.97)	92	Floor trimming.
W30, S850	H-F	06/11/07	13.351 (33.91)	0.78 (1.98)	0.39 (0.99)	100	Floor trimming.
W30, S1000	A-C	06/11/07	34.606 (87.90)	1.44 (3.66)	1.11 (2.82)	30	
W30, S1100	A-C	06/12/07	11.061 (28.10)	0.97 (2.46)	0.84 (2.13)	15	
W30, S1300	A-C	06/12/07	18.743 (47.61)	1.22 (3.10)	1.01 (2.57)	21	
W30, S1453	A-C	06/12/07	13.053 (33.16)	0.92 (2.34)	0.78 (1.98)	18	
W30, S1600	A-C	06/12/07	17.000 (43.18)	1.08 (2.74)	0.93 (2.36)	16	
W30, S1775	A-C	06/12/07	9.540 (24.23)	0.64 (1.63)	0.55 (1.40)	16	
W30, S1950	A-C	06/12/07	16.396 (41.65)	1.07 (2.72)	0.95 (2.41)	13	
W30, S2067	A-C	06/12/07	12.826 (32.58)	0.97 (2.46)	0.85 (2.16)	14	
W30, S2275	A-C	06/12/07	7.540 (19.15)	0.97 (2.46)	0.87 (2.21)	11	
W30, S2425	A-C	06/12/07	8.767 (22.27)	1.10 (2.79)	0.97 (2.46)	13	
W30, S2520	A-C	06/12/07	13.544 (34.40)	1.55 (3.94)	1.40 (3.56)	11	
W30, S2685	A-C	06/12/07	12.598 (32.00)	1.87 (4.75)	1.68 (4.27)	11	
W30, S2833	A-C	06/12/07	6.933 (17.61)	1.62 (4.11)	1.42 (3.61)	14	
W30, S2916	A-C	06/12/07	10.678 (27.12)	3.13 (7.95)	2.29 (5.82)	37	
W30, S2998	A-C	06/12/07	6.665 (16.93)	1.47 (3.73)	1.31 (3.33)	12	
W30, S3080	A-C	06/12/07	12.062 (30.64)	2.48 (6.30)	2.19 (5.56)	13	
W30, S3195	A-C	06/12/07	7.890 (20.04)	1.92 (4.88)	1.53 (3.89)	25	
W30, S3310	A-C	06/12/07	8.392 (21.32)	1.75 (4.45)	1.55 (3.94)	13	
W30, S3395	A-C	06/12/07	3.911 (9.93)	1.96 (4.98)	1.69 (4.29)	16	
W30, S3480	A-C	06/12/07	4.045 (10.27)	2.04 (5.18)	1.74 (4.42)	17	
W30, S3565	A-C	06/12/07	3.558 (9.04)	1.78 (4.52)	1.54 (3.91)	16	
W30, S3650	A-C	05/21/07	3.087 (7.84)	2.00 (5.08)	1.59 (4.04)	26	

A unique letter is assigned to each convergence array element around a particular opening. Chord refers to a particular array pair.

The various array lettering schemes are shown in Figure 5-1.

^a Increase in convergence rate is calculated from the difference between the 2006–2007 rate and the 2005–2006 rate.

5.4 Excavation Performance

Approximately 500 readings are collected and assessed regularly from convergence point arrays throughout the WIPP underground. Convergence rates continue to vary seasonally, typically increasing during the warmer and more humid summer months and decreasing during the cooler and drier winter months.

The performance of the access drift excavations during this reporting period was within acceptable criteria. "Acceptable criteria" means that a drift remains accessible, and the ground can be controlled by routine maintenance. Standard remedial ground control in some areas was required to maintain the performance of the excavations. The drifts remain stable and controlled. Most of the annualized rates remain steady, indicating stability. In some locations, where the rates are high, nearby mining activity is most likely the cause. In other locations, where necessary, additional ground control measures have been or will be installed.

6.0 PERFORMANCE OF WASTE DISPOSAL AREA

The Waste Disposal Area as of June 30, 2007, consists of Panels 1, 2, 3, and 4. Panels 1 and 2 were closed during previous reporting periods. Waste disposal in Panel 3 was completed in this period. Substantial barriers and bulkheads were installed in the exhaust and intake drifts to prevent access into the panel and to isolate this panel from the ventilation circuit. Waste is being disposed of in Panel 4. Panel 5 is being mined as shown in Figure 1-2.

6.1 History

Excavation of Panel 1 began in May 1986 with the mining of the access entries. Initially, the disposal rooms and drifts were developed as pilot drifts that were later excavated to nominal operational dimensions of 13 ft (4 m) high, 33 ft (10 m) wide, and 300 ft (91 m) long. Room 1 was completed to these dimensions in August 1986, and pilot drifts for Rooms 2 and 3 were excavated in January and February 1987. Rooms 2 and 3 were completed in February and March 1988, and Rooms 4 through 7 were completed in May 1988. Four short access drifts designed to lead to smaller test alcoves were excavated north off the S-1600 drift and Rooms 4-7 in June 1989. Only the access drifts to the alcoves were completed; the alcoves themselves were not excavated. Panel 1 waste emplacement (in Rooms 1, 2, 3, 7, adjacent areas of S-1600, and all of S-1950) is complete, and the panel is closed to all access. The Panel 1 access entries, S-1600 and S-1950, which extend from the E-300 drift to the isolation walls, remain open, and the instrumentation in this area will continue to be maintained and monitored.

Excavation of the Panel 2 waste disposal area began in September 1999 with the mining of access entries. Initially, the disposal rooms and drifts were developed as pilot drifts that were trimmed to finished dimensions. Room 1 was completed in January 2000, and pilot drifts for Rooms 2 and 3 were excavated in February 2000. Pilot drifts were completed for Rooms 4 through 6 in April 2000. The pilot drift for Room 7 was excavated in May 2000. All the rooms were excavated to final dimensions by August 2000. Waste emplacement in Panel 2 was completed during a prior reporting period, and the panel is closed to all access. The Panel 2 access entries, S-2150 and S-2520, which extend from the E-300 drift to the isolation walls, remain open, and the instrumentation in this area will continue to be maintained and monitored.

Excavation of Panel 3 waste disposal rooms began in May 2002 with the mining of access entries to Panel 3. As with Panel 2, initially, the disposal rooms and drifts were developed as pilot drifts that were trimmed to finished dimensions. All the rooms were excavated to final dimensions by the end of March 2004. Waste emplacement in Panel 3 was completed in February 2007.

Panel 4 access drift mining began in January 2005. The disposal rooms were initially developed as pilot drifts and were later trimmed to final dimensions. Mining was completed by June 2006. Waste has been emplaced in Room 7, and emplacement continues in Room 6. Panel 5 mining started and is continuing.

6.2 Modifications to Excavations and Ground Control Activities

There were no new excavations associated with Panels 1 through 4 during the reporting period. Waste disposal in Panel 3 was completed, and substantial and isolation barriers were installed in the access drifts. Mining of Panel 5 was started but not completed. Routine maintenance and ground control activities in the form of trimming, scaling, rock bolt replacement, and installing wire mesh were performed on ribs, floor, and roof throughout accessible areas of the disposal panels. Supplemental bolts were installed in Room 4 and the S-3310 drift between Rooms 1 and 3. RH holes were drilled horizontally into the ribs of Rooms 6, 5, and 4 for RH canister disposal. RH waste was emplaced in Rooms 6 and 5. Table 6-1 summarizes the ground control activities performed in the disposal panels during this reporting period.

6.3 Instrumentation

There were no changes to the Panel 3 instrumentation layout. Monitoring of manually read instruments continued until access was no longer available due to waste disposal. Remote monitoring of the borehole extensometers continued through this reporting period.

The instrumentation of Panel 4 was completed. Convergence points were installed in all of the disposal rooms, intersections, and at mid-pillar locations in the access drifts. A borehole extensometer was installed in the roof at each room center. Roof bolt load cells were installed at the center of each room and at selected locations in S-3310 and S-3650.

Instrumentation of the newly mined areas of Panel 5 was initiated during this reporting period. Extensometers were installed in the roof of Rooms 1 and 2.

Schematics of the geotechnical instrumentation layout in Panels 3, 4, and 5 are shown in Figures 6-1 through 6-3.

Table 6-1 – Summary of Modifications and Ground Control Activities in the Waste Disposal Area from July 1, 2006, to June 30, 2007

Location	Work Performed
Panel 3 entries, S-2750 and S-3080	Ceased waste disposal in panel. Installed substantial and isolation barriers in access drifts.
Panel 4, Room 4	Installed supplemental ground support.
Panel 4, S-3310 between Rooms 1 and 3	Installed supplemental ground support.
Panel 4, all rooms	Installed chain link and mesh along the roof/rib line
Panel 4, Room 1	Trimmed drummy ground on west rib and installed bolts and chain link.

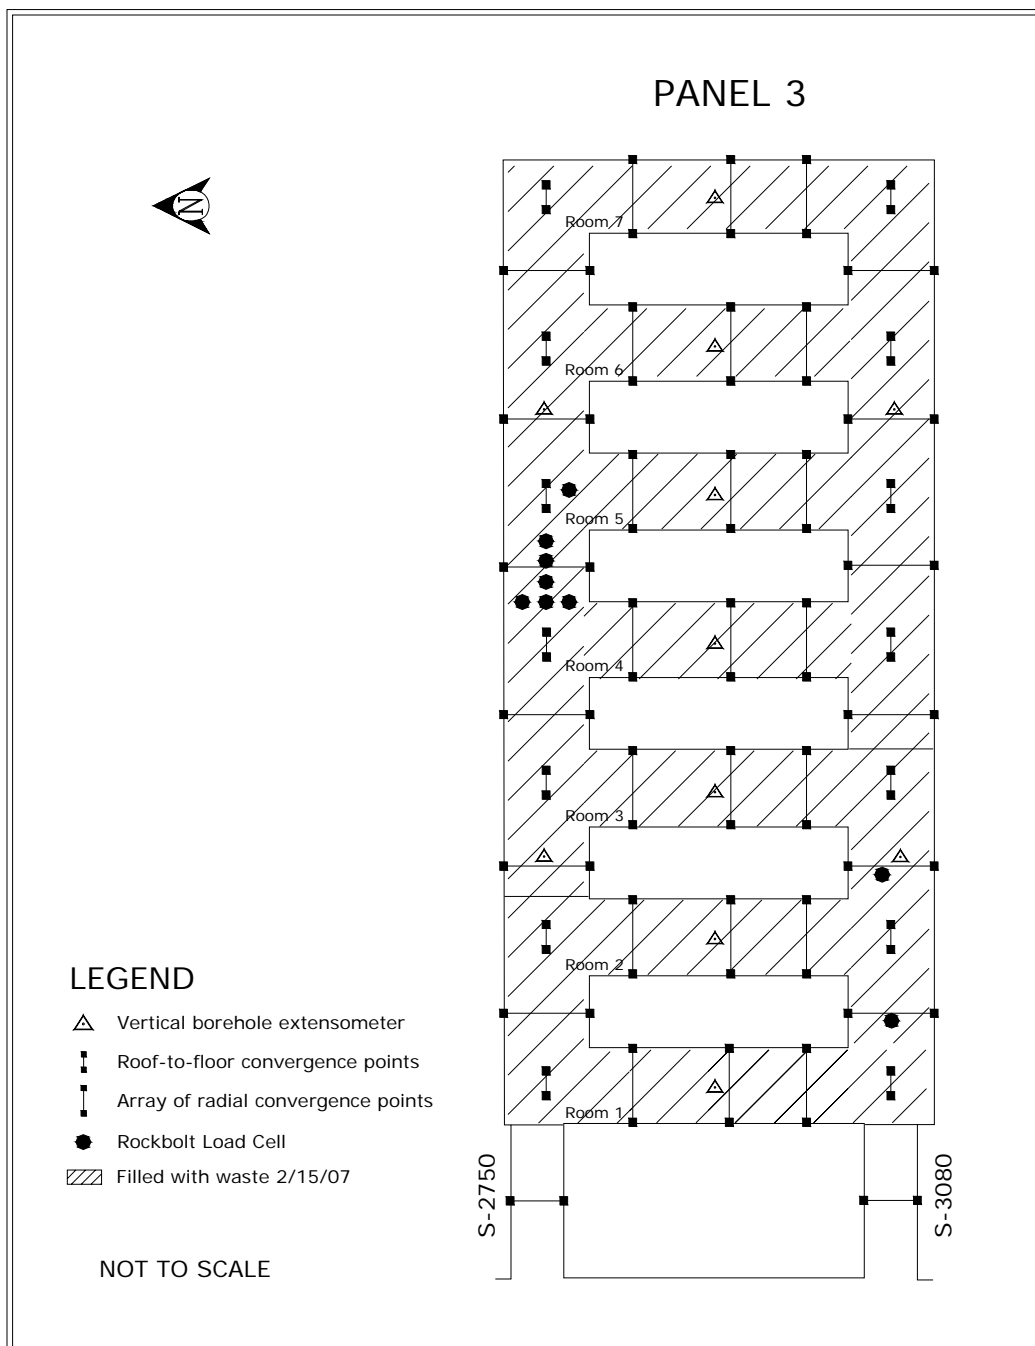


Figure 6-1 – Location of Panel 3 Geotechnical Instruments

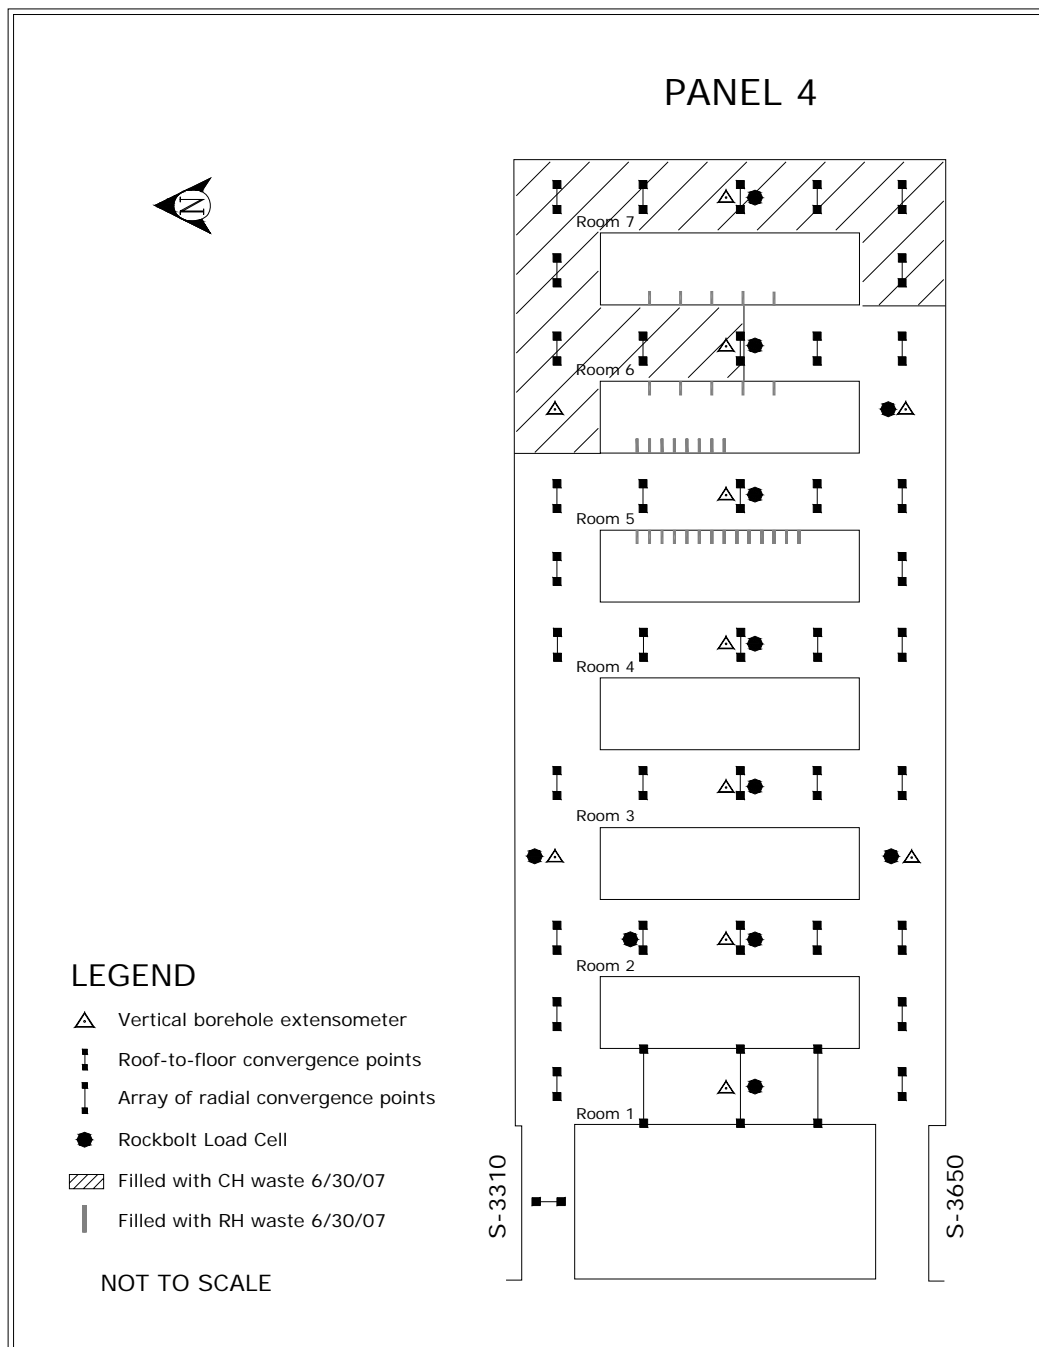


Figure 6-2 – Location of Panel 4 Geotechnical Instruments

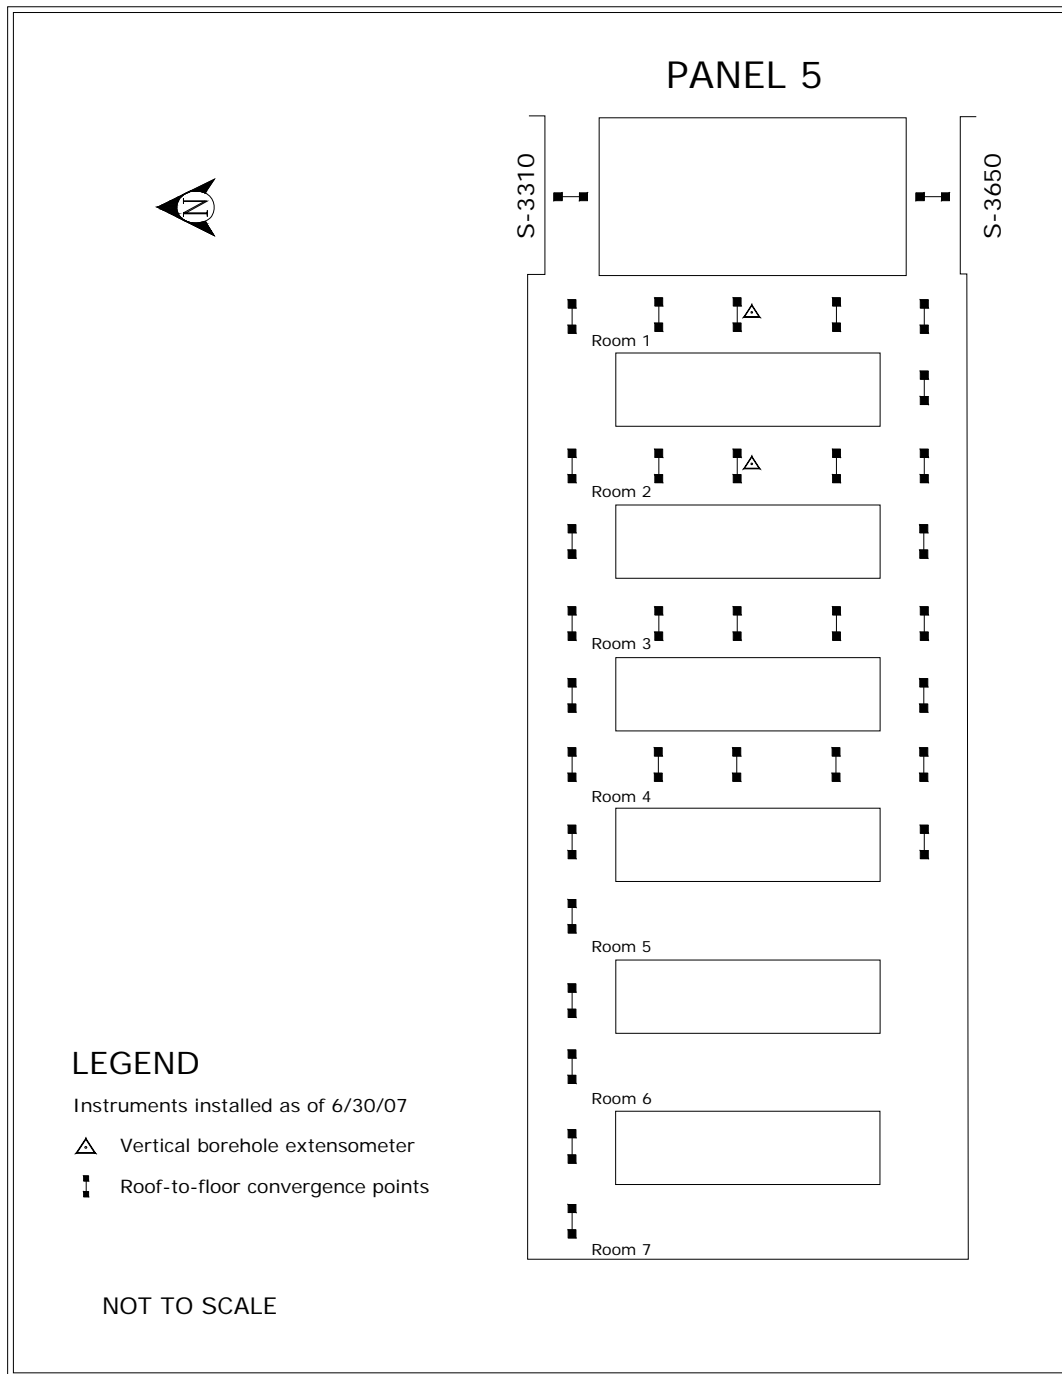


Figure 6-3 – Location of Panel 5 Geotechnical Instruments

6.4 Excavation Performance

Waste handling activities in Panels 1 and 2 have been completed, and geotechnical monitoring inside these panels has been discontinued. Waste handling activities have also been completed in Panel 3; however, extensometers continue to be read remotely. In accessible underground areas, horizontal and vertical convergence rates, calculated at the center of each of the rooms, were compared between this and the previous

reporting period. Generally, the convergence rates have decreased or remained similar. Increased rates observed in some areas are usually associated with areas of roof beam separation and fracturing. Geomechanical monitoring indicates that the early installation of a rigid threaded bar support system in Panel 4 has reduced the generation of shallow roof beam separations below that observed in Panel 3.

Convergence monitoring in the panel entries does not indicate an acceleration of closure rates; however, fracturing of the roof beam continues. It is anticipated that routine ground control maintenance will be sufficient to maintain access to these areas.

6.5 Analysis of Extensometer and Convergence Point Data

Borehole extensometers are installed in the roof at the center of each disposal room and at select locations in the panel access drifts. They show a general decrease in the rate of roof beam deformation. Supplemental ground control support was installed in these areas and has subsequently reduced the observed rates.

Although Panels 1, 2, and 3 are closed, convergence monitoring continues in the panel entries between E-300 and the explosion isolation walls (Panels 1 and 2) and substantial and isolation barriers (Panel 3). The monitoring results indicate a steady long-term trend. The lowest closure rates were observed nearest to the rigid masonry walls. Geotechnical monitoring in Panel 3 indicates continued deformation and deteriorating ground conditions.

Convergence rates in Panel 4 are generally decreasing or approaching steady state. The initial effects due to mining decreased significantly, similar to the experience in previous panels. The number and continuity of these stringers vary; however, the stringers are commonly observed throughout the panel. Deformation rates in these areas have stabilized or decreased in response to the installation of ground control.

Panel 5 mining continues with the installation of pattern bolts soon after mining. Panel 5 is being bolted and monitored at an even earlier stage in its development than were Panels 3 and 4. It appears from early observations that the closure rates are trending to be lower than those observed in Panel 4.

7.0 GEOSCIENCE PROGRAM

The Geoscience Program confirms the suitability of the site through the collection of various geologic data and excavation characteristics from the underground. These include the inspection of open boreholes for fractures (separations) and offsets (lateral displacements) in roof beams and the mapping of fracture development on roof surfaces. Data collected through these activities support the design and evaluation of ground support systems.

During this reporting period, the following activities were performed:

- Borehole Inspections
- Fracture Mapping

Fracture development in the roof is primarily caused by the concentration of compressive stresses in the roof beam and is influenced by the size and shape of the excavation and the stratigraphy in the immediate vicinity of the opening. In a thick roof beam, pillar deformations induce lateral compressive stresses into the immediate roof and floor. With time, the buildup of stress causes differential movement along stratigraphic boundaries. This differential movement is identified as offsets in observation boreholes and by the bends in failed rock bolts. Large strains associated with lateral movements can induce fracturing in the roof, which is frequently seen near the ribs; however, this process may take a long time (years) to develop.

At the upper repository horizon, clay or anhydrite stringers exert significant influence over the effective thickness of the roof beam. The presence of these stringers causes the roof beam to behave as a series of thin independent beams. Little or no tensile support is provided across the stringer interface. As horizontal end-loading continues, each beam can deflect downward causing a tensile fracture to develop along the bottom of the beam. These tensile fractures can develop in relatively new excavations soon after separation occurs along the stringer interface.

The location and initiation of interface separation is also influenced by the dip of the rock layers. The roofs and floors of the disposal panels are mined level through the sloping beds. At some locations, this may result in a significant difference in roof beam thickness from one side of the excavation to the other. Areas with the thinnest beam are the most likely to develop separations and subsequent fracturing.

7.1 Borehole Inspections

Geotechnical observation boreholes are drilled at various locations throughout the underground facility. A location may contain one or more boreholes arranged in an array. These holes are drilled to depths that allow the monitoring of fracture development and offsetting and are inspected for the development of those features. Roof observation holes usually extend up past clays "G" and "H" (Figures 7-1 and 7-2).

The clay seams nearest the excavation surfaces define the immediate roof beam. The roof beam is bounded by clay "G" in most of the access drifts and Panels 1 and 2.

Some areas, such as the Salt Shaft Station, portions of the E-0 and E-140 drifts, the south mains south of S-2620, and Panels 3, 4, and 5 are excavated to clay "G" and so have roof beams bounded by clay "H".

The offset in a borehole is determined by visually estimating the degree of borehole occlusion. The direction of offset along clay seams is observed as the movement of the strata nearer to the observer relative to the strata farther away. Typically, the nearer strata move toward the center of the excavation (Figures 7-3 and 7-4). Based on previous observations in the underground, the magnitude of offset is usually greater in boreholes located near ribs than in those located along excavation centerlines.

Offsetting along the clay layers is observable until the total borehole offset is reached or visibility is obstructed by intervening offsets at other clay seams or fractures. Boreholes are inspected for fractures, using an aluminum rod with a flattened steel wire probe attached to one end perpendicular to the rod (referred to as a "scratcher rod").

Fractures and clay seams are located by moving the probe along the inside of the borehole until it is snagged in one of these features. Depth to each feature is recorded, as is the magnitude of separations encountered. In addition, during this reporting period, the use of a borehole camera has been introduced in conjunction with the scratch rod.

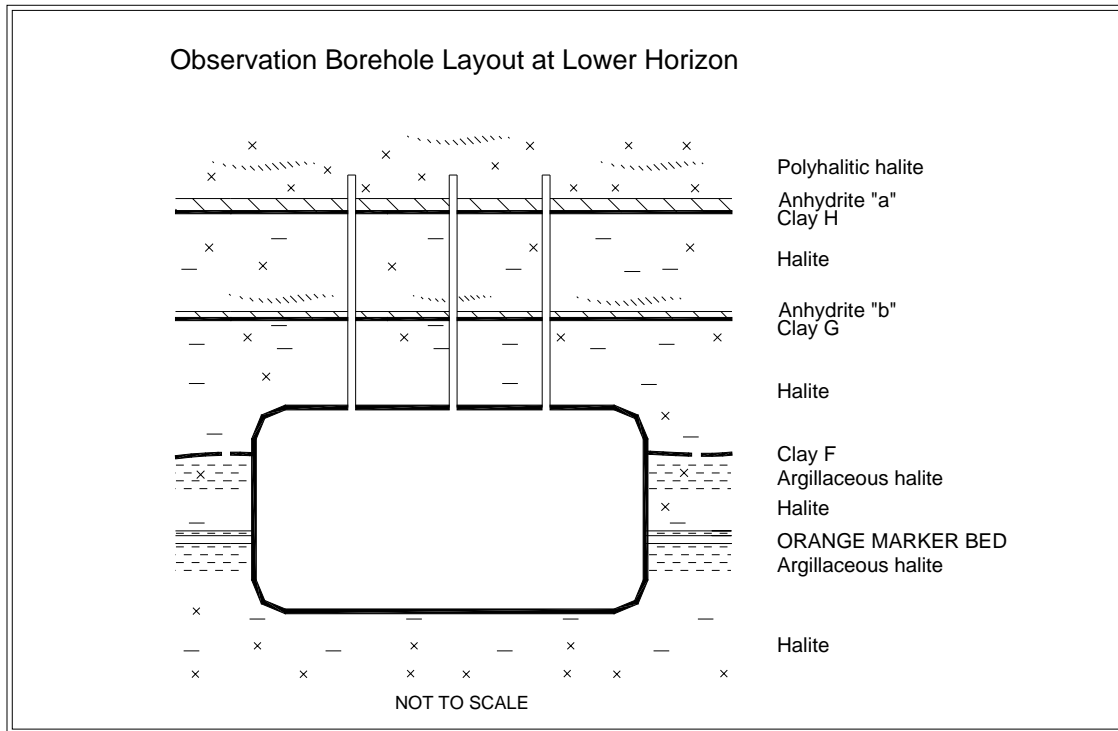


Figure 7-1 – Example of Observation Borehole Layout at Lower Horizon

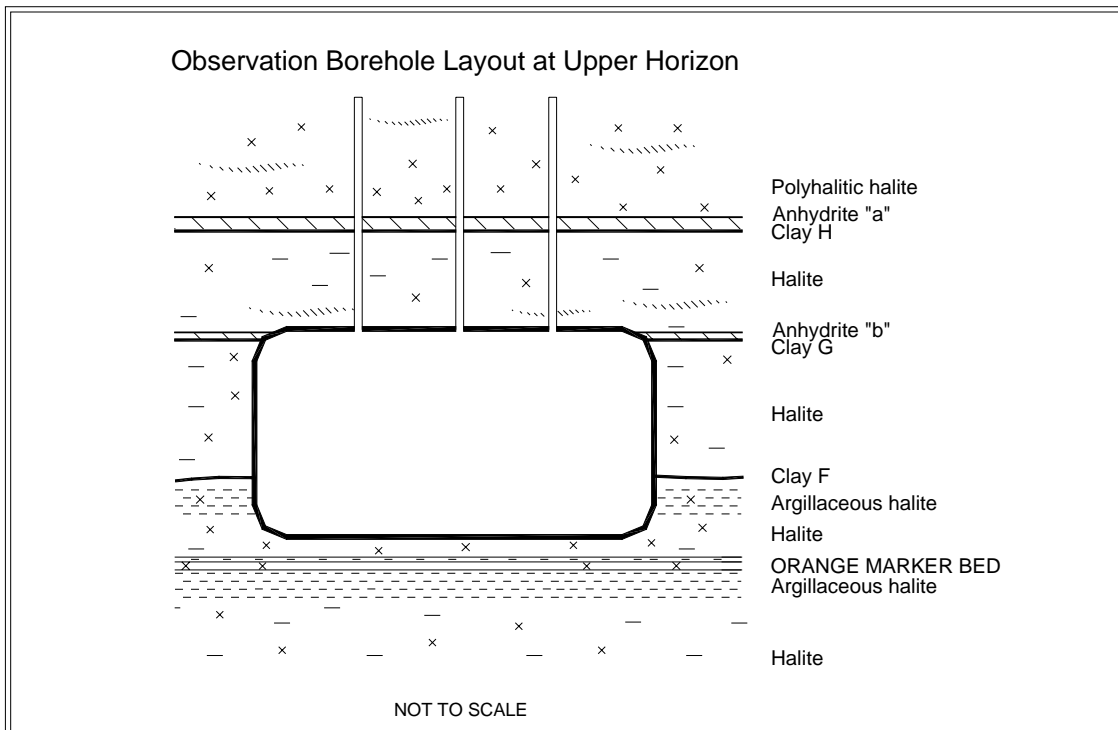


Figure 7-2 – Example of Observation Borehole Layout at Upper Horizon

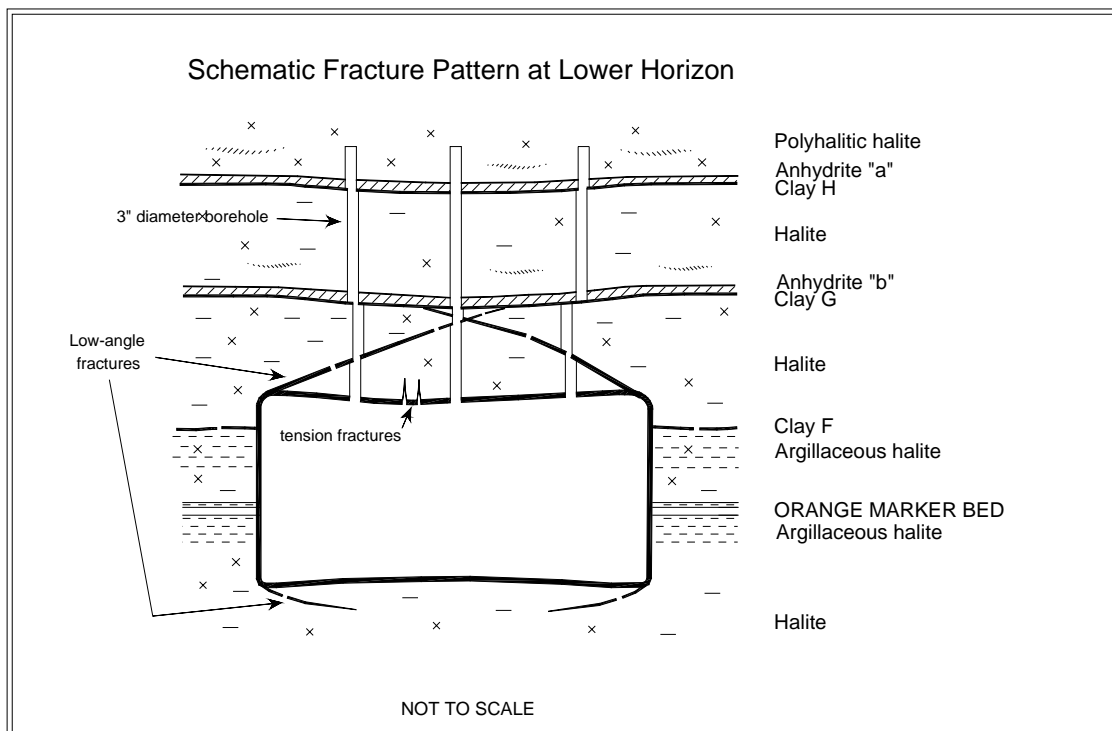


Figure 7-3 – Typical Fracture Patterns at Lower Horizon

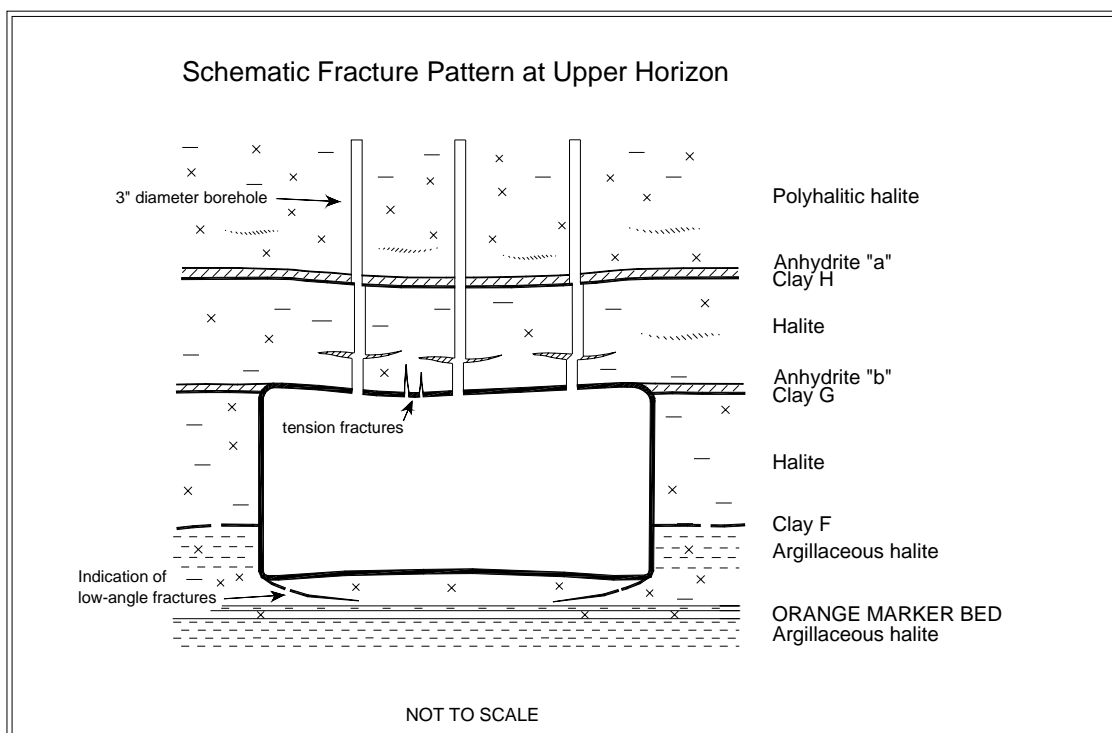


Figure 7-4 – Typical Fracture Patterns at Upper Horizon

The separation and offset data observed in accessible holes in the back are presented in the supporting data document for this report. Forty-eight holes in Panel 4 and 41 in Panel 5 had been drilled at the time of this report. In both Panels 4 and 5, the greatest separations were associated with clay "H" and anhydrite "a". Eight holes in Panel 4 and three holes in Panel 5 had fractures associated with anhydrite stringers in the lower portion (first 3 feet) of the roof beam. Thirty-seven of the 48 holes in Panel 4 and two of the 41 holes in Panel 5 showed some offset.

7.2 Fracture Mapping

Routine mapping documents the progression of fractures in the roof exposed on the excavation surfaces of the drifts and rooms in the underground repository. The fracture surveys are generally performed on an annual basis, and the fracture maps are updated. The fracture maps facilitate the analysis of strain in the immediate roof-beam because they document the development and propagation of fractures through time. The supporting data document contains fracture maps for Panels 4 and 5. For this reporting period, fracture maps include Panel 4, Rooms 1 through 7 and the S-3310 and S-3650 drifts, and Panel 5, Room 1.

This page intentionally left blank

8.0 SUMMARY

At the inception of WIPP, criteria were developed that address the design requirements (DOE, 1984). They pertain to all aspects of the mined facility and its operation as a pilot plant for the demonstration of technical and operational methods for permanent disposal of contact-handled and remote-handled TRU waste. In 1994, as the WIPP focus moved toward the permanent disposal of TRU waste, these design requirements were reassessed and replaced by a new set of requirements called system design descriptions. Table 8-1 shows the comparison of these design requirements with conditions actually observed in the underground from July 2006 through June 2007.

Normal drift and room maintenance continued during this reporting period with rib, roof, and floor scaling and trimming in various locations, and rock bolts and wire mesh installed as needed. Supplemental ground control systems consisting of resin-anchored bolts were installed in select locations in the E-140 and W-170 drift and the E-300 shop area. Some of these supplemental systems also included roof mats.

New geomechanical instrumentation was installed in Panel 5 and its access drifts, as well as in various locations throughout the repository to replace mined-out instruments. Monitoring no longer continues in non-accessible areas except in Panel 3 and closed rooms in Panel 4. All accessible areas of the underground are connected to data-loggers or are monitored manually.

The *in situ* performance of the excavations generally continues to satisfy the appropriate design criteria, although specific areas are being identified where deterioration resulting from ageing must be addressed through routine maintenance and installation of engineered systems. This deterioration has been identified through the analysis of data acquired from geomechanical instrumentation and the Geoscience Program. If the planned life of some of the openings needs to be extended, changing the geometry of the access drifts (removing unstable roof beam or rib spalls, or milling the floor for added clearance), or additional ground control (roof removal, installing bolts, mesh, or straps) may be necessary. The ground conditions in the waste disposal area and associated waste transport routes continue to slowly deteriorate; however, routine ground control installations and maintenance continue to allow safe access in the underground facility.

In addition to underground instrumentation, qualitative assessments of fracture development are documented through mapping the underground repository and inspecting the observation boreholes. The information acquired from these programs provides early detection of ground deterioration, contributes to the understanding of the dynamic geomechanical processes in the WIPP underground, and aids in the design of effective ground control and support systems.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

Table 8-1 – Comparison of Excavation Performance to System Design Requirements

Requirement	Comments
"The lining shall be designed for a hydrostatic pressure. . . ."	Water pressure observed on piezometers located behind the shaft liners remains below design levels.
"The key shall be designed to resist the lateral pressure generated by salt creep."	Geomechanical data from the Waste Shaft indicate that the shaft key is minimally loaded and is structurally stable. Visual inspections of all shaft keys do not indicate any deterioration due to creep loading.
"The key shall be designed to retain the rock formation and will be provided with chemical seal rings and a water collection ring with drains to prevent water from flowing down the unlined shaft from the lining above."	Shaft inspection observations and instrumentation show no indication of instability due to salt dissolution. No water has been observed flowing along the rock-liner interface.
"The underground waste disposal facilities shall be designed to provide space and adequate access for the underground equipment and temporary storage space to support underground operations."	Geomechanical instrument data and visual observations indicate that the current design provides adequate access and storage and disposal space. Ground control maintenance is performed as necessary to maintain access.
"Entries and subentries to the underground disposal area and the experimental areas shall be provided and sized for personnel safety, adequate air flow, and space for equipment."	Deformation of excavation remains within the required limits. Normal periodic maintenance consisting of rock bolting, wire meshing, trimming, and scaling continue throughout the repository. The former experimental area, consisting of the Northeast and Northwest Areas, is now deactivated and closed to access.
"Geomechanical instrumentation shall be provided to measure the cumulative deformation of the rock mass surrounding mined drifts. . . ."	Geotechnical instrumentation is operated and maintained to meet this requirement. This annual report provides a summary and analysis of the geomechanical data.

9.0 REFERENCES

ASTM, 2006, E29-06b, *Standard Practice for Using Significant Digits in Test Data to Determine Conformance with Specifications*.

DOE, see U.S. Department of Energy.

Public Law 96-164, Department of Energy National Security and Military Applications of Nuclear Energy Authorization Act of 1980.

Title 40 CFR Part 191, "Environmental Radiation Protection Standards for Management and Disposal of Spent Nuclear Fuel, High-Level and Transuranic Radioactive Wastes."

Title 40 CFR Part 194, "Criteria for the Certification and Re-certification of the Waste Isolation Pilot Plant's Compliance with the 40 CFR Part 191 Disposal Regulations."

U.S. Environmental Protection Agency, 1998, "Criteria for the Certification and Recertification of the Waste Isolation Pilot Plant's Compliance with the Disposal Regulations: Certification Decision," *Federal Register*, Vol. 63, No. 95, pp. 27354, May 18, 1998, Washington, DC

Holt, R. M., and D. W. Powers, 1990, *Geologic Mapping of the Air Intake Shaft at the Waste Isolation Pilot Plant*, DOE/WIPP 90-051, Waste Isolation Pilot Plant, Carlsbad, New Mexico.

Holt, R. M., and D. W. Powers, 1984, *Geotechnical Activities in the Waste Handling Shaft, Waste Isolation Pilot Plant (WIPP) Project, Southeastern New Mexico*, WTSD-TME 038, Waste Isolation Pilot Plant, Carlsbad, New Mexico.

New Mexico Environment Department (NMED), 2006, Waste Isolation Pilot Plant Hazardous Waste Facility Permit, NM4890139088-TSDF, Santa Fe, New Mexico.

Powers, D. W., and R. M. Holt, 1993, *The Upper Cenozoic Gatuña Formation of Southeastern New Mexico*, New Mexico Geological Society Guidebook, 44th Field Conference, Carlsbad Region, New Mexico and West Texas, D. W. Love et al., Eds., pp 271–282.

Powers, D. W., and R. M. Holt, 1995, *Gatuña Formation (Miocene to Pleistocene) Geology and Paleohydrology*, prepared for Westinghouse Waste Isolation Division by International Technology Corporation, Albuquerque, New Mexico.

Powers, D. W., S. J. Lambert, S. E. Shaffer, L. R. Hill, and W. D. Weart, Eds., 1978, *Geological Characterization Report, Waste Isolation Pilot Plant (WIPP) Site, Southeastern New Mexico*, Vols. I and II, SAND 78-1596; Sandia National Laboratories, Albuquerque, New Mexico.

Geotechnical Analysis Report for July 2006 – June 2007
DOE/WIPP-08-3177, Vol. 1

U.S. Department of Energy (DOE), 2000, *Brine Generation Study*, DOE/WIPP 00-2000, Waste Isolation Pilot Plant, Carlsbad, New Mexico.

U.S. Department of Energy (DOE), 1986a, *Interim Geotechnical Field Data Report*, DOE/WIPP 86-012, Waste Isolation Pilot Plant, Carlsbad, New Mexico.

U.S. Department of Energy (DOE), 1986b, *Waste Isolation Pilot Plant Design Validation Final Report*, DOE/WIPP 86-010; Prepared by Bechtel National, Inc., for the U.S. Department of Energy, San Francisco, California.

U.S. Department of Energy (DOE), 1986c, *Geotechnical Activities in the Exhaust Shaft*, DOE/WIPP 86-008, Waste Isolation Pilot Plant, Carlsbad, New Mexico.

U.S. Department of Energy (DOE), 1985, *Quarterly Geotechnical Field Data Report*, DOE/WIPP-221, Waste Isolation Pilot Plant, Carlsbad, New Mexico.

U.S. Department of Energy (DOE), 1984, *Design Criteria, Waste Isolation Pilot Plant (WIPP) Revised Mission Concept-IIA*, DOE/WIPP-071; Waste Isolation Pilot Plant, Carlsbad, New Mexico.

U.S. Department of Energy (DOE), 1983, *Summary of the Results of the Evaluation of the WIPP Site and Preliminary Design Validation Program*, DOE/WIPP-161; Waste Isolation Pilot Plant, Carlsbad, New Mexico.
